



Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2021												2022																																						
							Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar																																						
West Point Treatment Plant Primary Sedimentation Area Roof Structure - \$							862															10			02-Mar-21 A															26-Jun-24			0														
Pre-Contract Items							97															0			02-Mar-21 A															10-Mar-21			▼ 10-Mar-21 A, Pre-Contract Items														
A1010	Contract Execution	0	0	02-Mar-21 A			▶ Contract Execution																																																		
A2210	Notice to Proceed	0	0	10-Mar-21 A			◆ Notice to Proceed																																																		
Milestones							166															0			25-Oct-23 A															26-Jun-24			0														
A4330	East Basin Complete (including non-weather window work)	0	0		25-Oct-23																																																				
A4480	West Basin Complete (including non-weather window work)	0	0		27-Oct-23																																																				
A2290	SJC Anticipated Substantial Completion (in work days)	0	0	30-Oct-23 A																																																					
A2280	Contract Substantial Completion (611 Calendar Days)	0	0		30-Oct-23																																																				
A2400	Final Acceptance (per 01 14 00 -1.02B - determined post substantial) - Estimated	0	0		26-Jun-24	0																																																			
Submittals - Preparation by Contractor & Vendors							720															0			02-Mar-21 A															12-Feb-24																	
A2350	Submit - 01 35 29 - Health and Safety	2	0	02-Mar-21 A	11-Mar-21		■ Submit - 01 35 29 - Health and Safety																																																		
A4810	01 78 39 Record Drawings - Maintain	351	0	10-Mar-21 A	30-Oct-23																																																				
A4840	01 32 16 Progress Schedules - Maintain	351	0	10-Mar-21 A	30-Oct-23																																																				
A2360	Submit - 03 20 00 - Concrete Reinforcing	24	0	10-Mar-21 A	14-Apr-21		■ Submit - 03 20 00 - Concrete Reinforcing																																																		
A2370	Submit - 03 37 13 - Shotcrete	15	0	10-Mar-21 A	24-Mar-21		■ Submit - 03 37 13 - Shotcrete																																																		
A2380	Submit - 03 60 00 - Grouting	5	0	10-Mar-21 A	19-Mar-21		■ Submit - 03 60 00 - Grouting																																																		
A3560	Submit - 03 83 00 - Cutting and Patching	5	0	10-Mar-21 A	19-Mar-21		■ Submit - 03 83 00 - Cutting and Patching																																																		
A3580	Submit - 02 41 00 Crane Pick Plan	5	0	10-Mar-21 A	16-Mar-21		■ Submit - 02 41 00 Crane Pick Plan																																																		
A3590	Submit - 02 83 00 Lead Abatement Plan	1	0	10-Mar-21 A	10-Mar-21		■ Submit - 02 83 00 Lead Abatement Plan																																																		
A3600	Submit - 02 84 00 PCB Abatement Plan	1	0	10-Mar-21 A	10-Mar-21		■ Submit - 02 84 00 PCB Abatement Plan																																																		
A3610	Submit - 05 50 00 Electrical Conduit Support Frames (12/S460)	5	0	10-Mar-21 A	11-Mar-21		■ Submit - 05 50 00 Electrical Conduit Support Frames (12/S460)																																																		
A3620	Submit - 01 19 50 Odor Control Panel Removal & Replacement Plan	20	0	10-Mar-21 A	29-Apr-21		■ Submit - 01 19 50 Odor Control Panel Removal & Replacement Plan																																																		
A4490	Submit - 05 12 00 - Structural Steel	19	0	10-Mar-21 A	05-Apr-21		■ Submit - 05 12 00 - Structural Steel																																																		
A4500	Submit - Div 26 Submittals	10	0	10-Mar-21 A	18-Mar-21		■ Submit - Div 26 Submittals																																																		
A4510	Submit - 06 84 01 Fiberglass Roof Decking	41	0	10-Mar-21 A	05-May-21		■ Submit - 06 84 01 Fiberglass Roof Decking																																																		
A4520	Submit - 06 84 02 - FRP Grating	10	0	10-Mar-21 A	16-Mar-21		■ Submit - 06 84 02 - FRP Grating																																																		
A4530	Submit - 40 05 36.13 - FRP Duct for Foul Air	25	0	10-Mar-21 A	14-Apr-21		■ Submit - 40 05 36.13 - FRP Duct for Foul Air																																																		
A4640	Submit - 45 05 01 Duct Supports	26	0	10-Mar-21 A	14-Apr-21		■ Submit - 45 05 01 Duct Supports																																																		
A4930	Submit - 40 05 93 Skum Skimmer Motors	23	0	10-Mar-21 A	07-Apr-21		■ Submit - 40 05 93 Skum Skimmer Motors																																																		
A4990	Submit - 41 22 23.19 Monorail Hoist	20	0	10-Mar-21 A	20-Apr-21		■ Submit - 41 22 23.19 Monorail Hoist																																																		
A5100	Submit - Portable Stairs	15	0	10-Mar-21 A	27-May-21		■ Submit - Portable Stairs																																																		
A4890	Submit - 01 78 40 Initial Asset Data Form	10	0	21-Apr-22 A	21-Apr-22																																																				
A4910	Submit - 01 78 40 Final Asset Data Form	10	0	16-Jan-23 A	31-Oct-23																																																				
A4820	Submit - 01 78 39 Final Record Drawings	1	0	01-Nov-23 A	05-Jan-24																																																				
A4850	Submit - 01 33 29 Sustainability Reporting	10	0	01-Nov-23 A	12-Feb-24																																																				
A4870	Submit - 01 78 23 O&M Manual	20	0	01-Nov-23 A	01-Nov-23																																																				
Submittal Reviews - Period by Owner (30 days = 21 Work Days)							739															0			11-Mar-21 A															13-Jun-24			10														
A2410	Review/Approval - 01 35 29 - Health and Safety	21	0	11-Mar-21 A	17-Mar-21		■ Review/Approval - 01 35 29 - Health and Safety																																																		
A4600	Review/Approval - 02 83 00 Lead Abatement Plan	21	0	11-Mar-21 A	30-Apr-21		■ Review/Approval - 02 83 00 Lead Abatement Plan																																																		
A4610	Review/Approval - 02 84 00 PCB Abatement Plan	21	0	11-Mar-21 A	12-May-21		■ Review/Approval - 02 84 00 PCB Abatement Plan																																																		
A4620	Review/Approval - 05 50 00 Electrical Conduit Support Frames (12/S460)	21	0	14-Mar-21 A	26-Mar-21		■ Review/Approval - 05 50 00 Electrical Conduit Support Frames (12/S460)																																																		
A4570	Review/Approval - 06 84 02 - FRP Grating	21	0	16-Mar-21 A	18-May-21		■ Review/Approval - 06 84 02 - FRP Grating																																																		
A4590	Review/Approval - 02 41 00 Crane Pick Plan	21	0	16-Mar-21 A	15-Apr-21		■ Review/Approval - 02 41 00 Crane Pick Plan																																																		
A4550	Review/Approval - Div 26 Submittals	21	0	18-Mar-21 A	28-Apr-21		■ Review/Approval - Div 26 Submittals																																																		
A2440	Review/Approval - 03 60 00 - Grouting	21	0	19-Mar-21 A	29-Mar-21		■ Review/Approval - 03 60 00 - Grouting																																																		

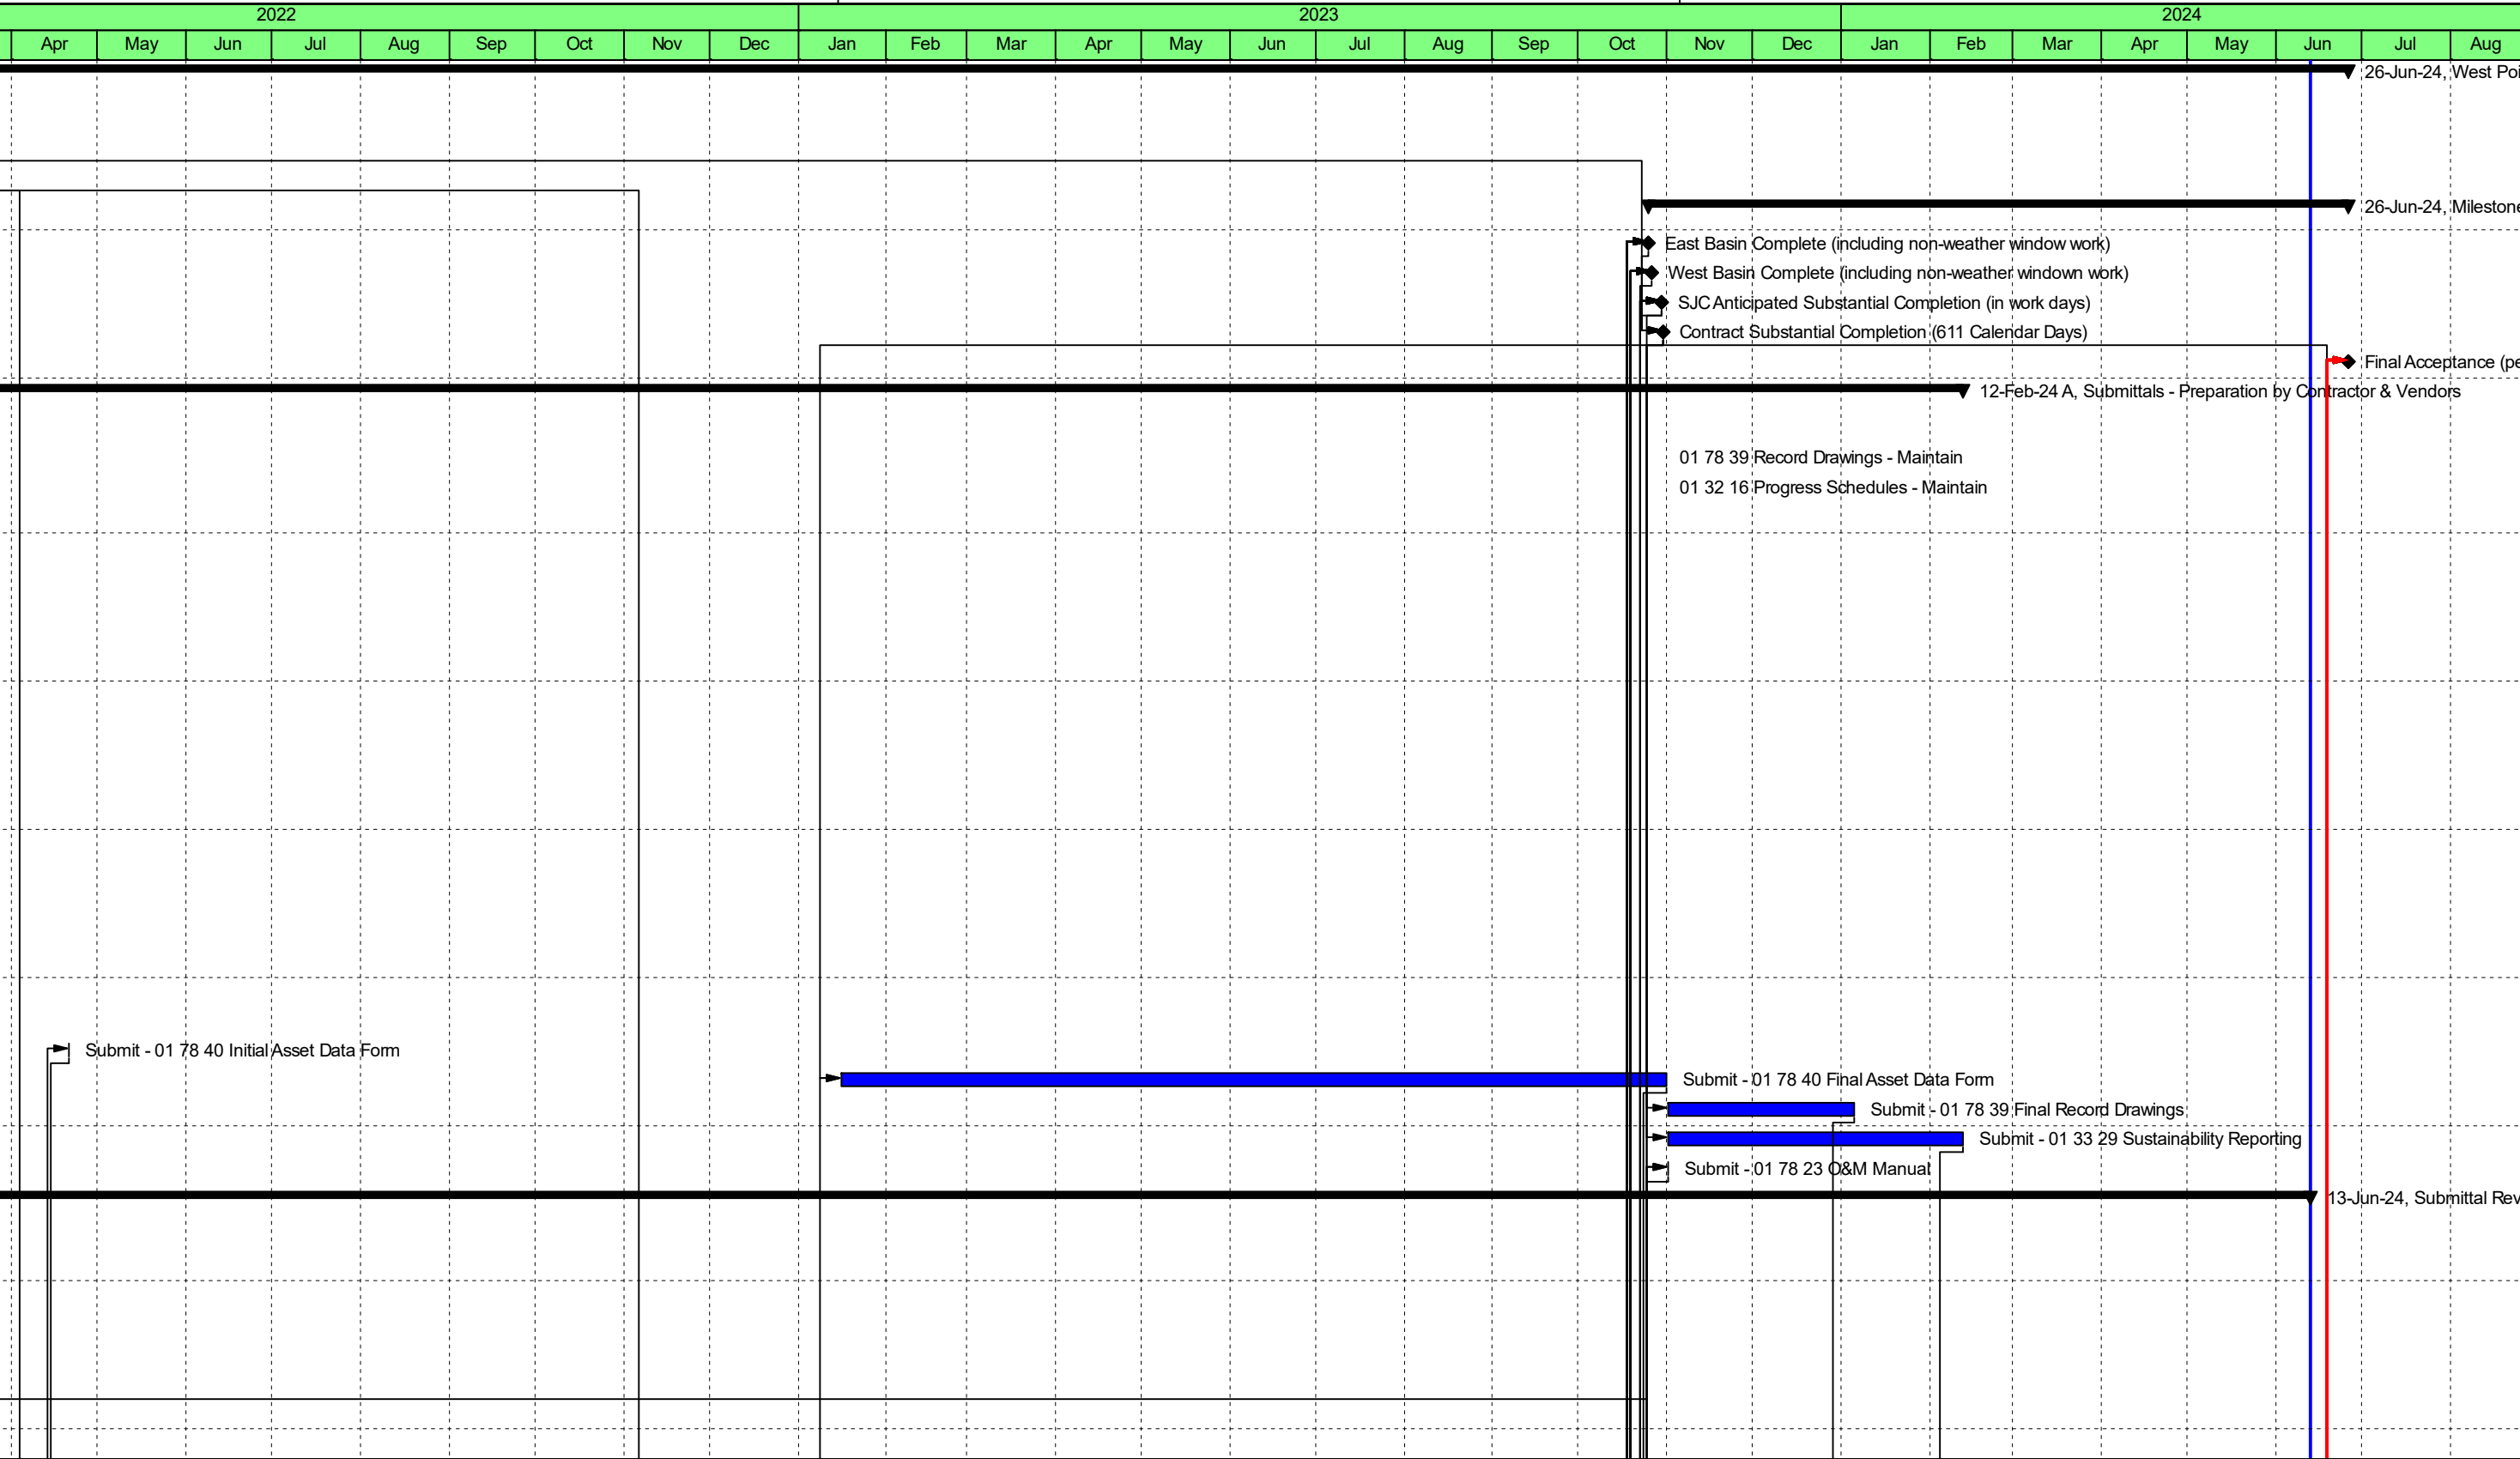


Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2021												2022		
							Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A3570	Review/Approval - 03 83 00 - Cutting and Patching	21	0	19-Mar-21 A	29-Mar-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A2430	Review/Approval - 03 37 13 - Shotcrete	21	0	24-Mar-21 A	03-May-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A4540	Review/Approval - 05 12 00 - Structural Steel	21	0	05-Apr-21 A	12-May-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A4940	Review/Approval - 40 05 93 Skum Skimmer Motors	21	0	07-Apr-21 A	13-May-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A2420	Review/Approval - 03 20 00 - Concrete Reinforcing	21	0	14-Apr-21 A	16-Jun-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A4650	Review/Approval - 45 05 01 Duct Supports	21	0	14-Apr-21 A	18-May-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A4580	Review/Approval - 40 05 36.13 - FRP Duct for Foul Air	15	0	14-Apr-21 A	04-Jun-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A5000	Review/Approval - 41 22 23.19 Monorail Hoist	21	0	20-Apr-21 A	30-Apr-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A4630	Review/Approval - 01 19 50 Odor Control Panel Removal & Replacement Plan	21	0	29-Apr-21 A	30-Apr-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A4560	Review/Approval - 06 84 01 Fiberglass Roof Decking	5	0	06-May-21 A	01-Jun-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A5110	Review/Approval - Portable Stairs	21	0	27-May-21 A	25-Aug-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A4900	Review/Approval - 01 78 40 Initial Asset Data Form	21	0	22-Apr-22 A	13-Jan-23		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A4920	Review/Approval - 01 78 40 Final Asset Data Form	21	0	31-Oct-23 A	13-Jun-24	10	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A4880	Review/Approval - 01 78 23 O&M Manual	21	0	01-Nov-23 A	13-Jun-24	10	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A4830	Review/Approval - 01 78 39 Final Record Drawings	21	0	05-Jan-24 A	13-Jun-24	10	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A4860	Review/Approval - 01 33 29 Sustainability Reporting	21	0	12-Feb-24 A	14-Mar-24		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
Procurement & Offsite Fabrication Time		461	0	26-Apr-21 A	28-Jul-23 A		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A3660	Conduit Supports Metal Fabrications - Furnish	15	0	26-Apr-21 A	07-Jun-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A5010	Monorail Hoist - Furnish	30	0	30-Apr-21 A	02-Aug-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A4660	FRP Roof Decking - Furnish	23	0	10-May-21 A	05-Jul-21 A		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A3670	Canopy Roof /Duct Support Structural Steel - Furnish	27	0	12-May-21 A	21-Jun-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A4950	Skum Skimmer Motors - Furnish	30	0	13-May-21 A	03-Dec-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A3650	FRP Grating - Furnish	25	0	18-May-21 A	21-Jun-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A3680	Duct Supports - Furnish	25	0	18-May-21 A	13-Aug-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A5350	Concrete Reinf - Furnish	15	0	18-May-21 A	09-Jun-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A3640	East Basin FRP Duct - Furnish	40	0	04-Jun-21 A	31-Mar-23		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A5800	West Basin FRP Duct - Furnish	40	0	04-Jun-21 A	28-Jul-23 A		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A5640	Temp Odor Control Duct for Temp Odor Control of Tanks 1E-3E	20	0	21-Jun-21 A	09-Jul-21 A		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A5120	Portable Stairs - Furnish	20	0	25-Aug-21 A	19-Nov-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A5750	CO#06.4 - Portable Stair Width Per RFI 51	1	0	31-May-22 A	31-May-22		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A5960	CO#11 - RCP 05 Materials	65	0	14-Nov-22 A	16-Jan-23		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
Mobilization		408	0	10-Mar-21 A	16-Jan-23		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A5920	CO09.2 Vaccine Mandate	1	0	10-Mar-21 A	16-Jan-23		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A2460	Mobilization to Jobsite	5	0	24-Mar-21 A	30-Mar-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A2530	Constraint Orientation 01 14 00 - 1.04.A.1 Contractors Use of Facilities	0	0	24-Mar-21 A			Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A2540	Constraint Orientation 01 14 00 - 1.04.A.2 Tunnel Access / Flow Protocol	0	0	24-Mar-21 A			Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A2630	Demolition Equipment / Crane / Setup - Mobilization	5	0	19-Apr-21 A	21-Apr-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A2640	Traffic Control Access Road	5	0	19-Apr-21 A	23-Apr-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A3480	Furnish/Mob Gantry Crane - Phase 2	5	0	10-Aug-21 A	17-Aug-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
East Basin		702	0	10-Mar-21 A	27-Oct-23		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
Concrete Demolition & Disposal		540	0	29-Mar-21 A	11-Mar-22		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A3240	Install Access to Roof Level	5	0	29-Mar-21 A	02-Apr-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A3040	Install Temporary Protections - Basin Work	5	0	03-May-21 A	14-May-21		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A5340	Haul & Dispose of Concrete from Staging Area	35	0	14-May-21 A	01-Mar-22		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A3450	Hauling Z-Beams to Landfill from Site	43	0	14-May-21 A	09-Mar-22		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A3750	Hauling of Girders & Columns to Landfill (item shows duration)	11	0	31-Jan-22 A	11-Mar-22		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		

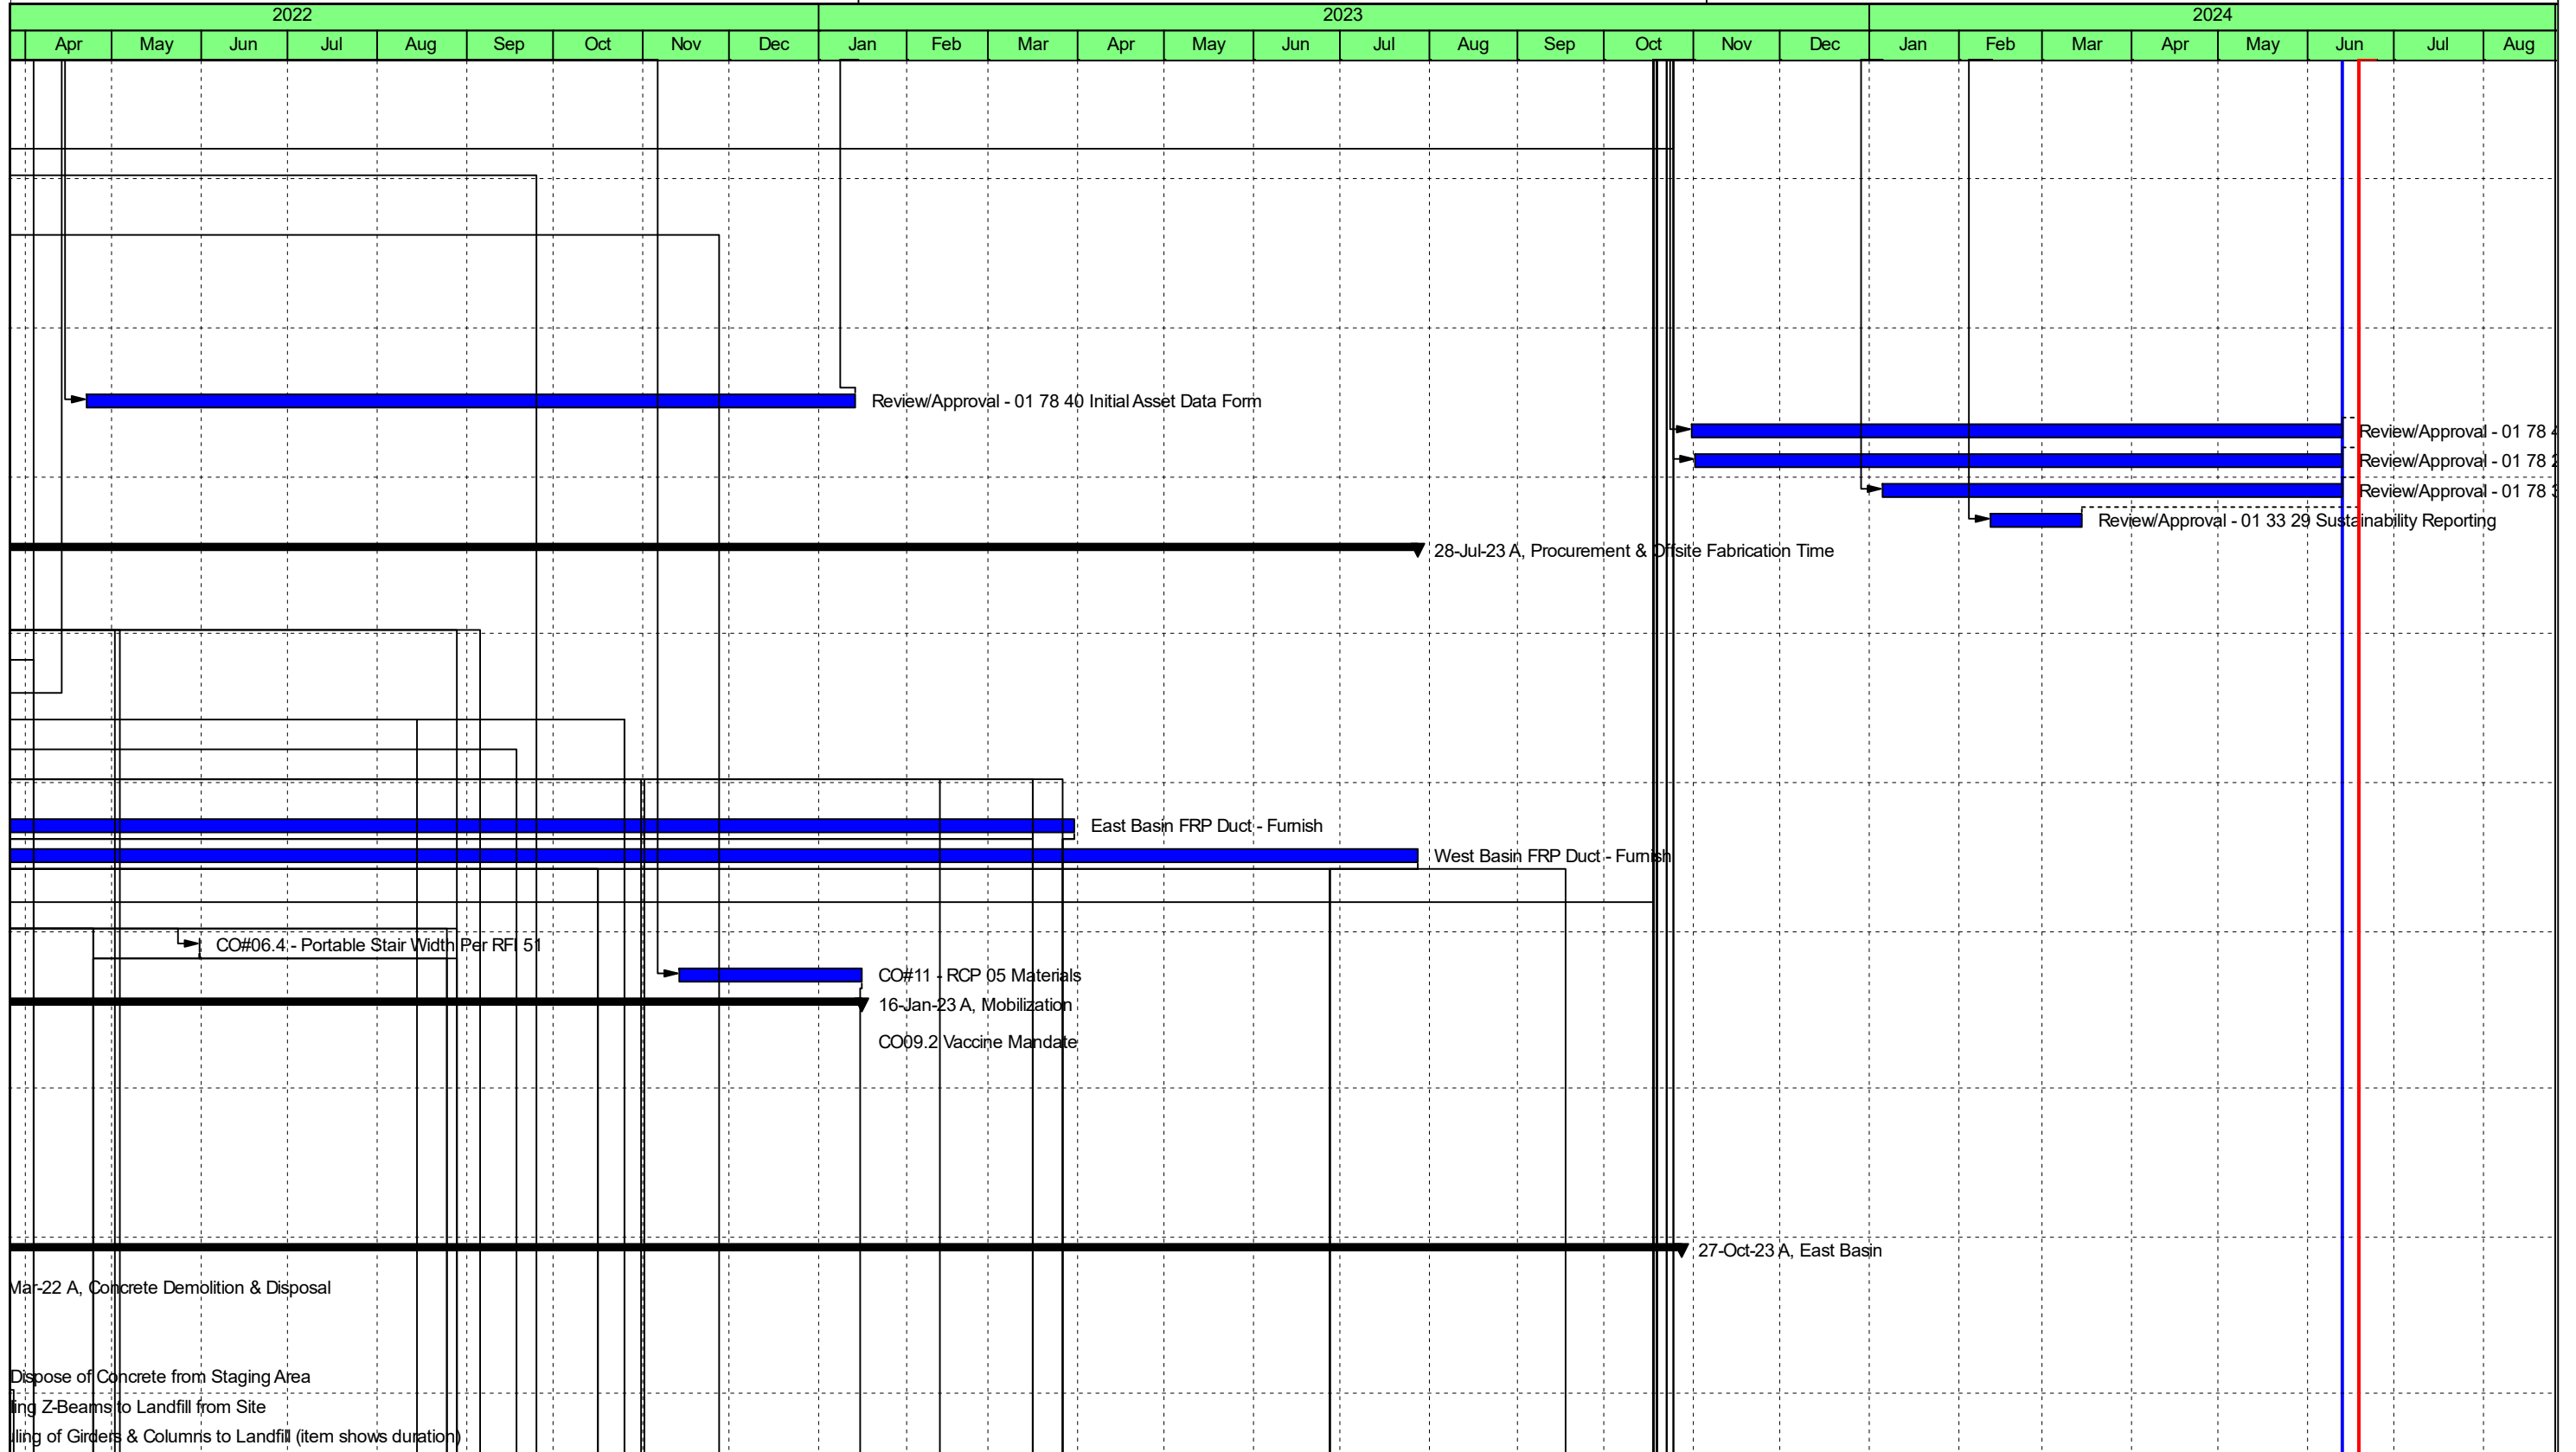


█ Actual Work
 █ Critical Remaining Work
 ▶ Summary
█ Remaining Work
 ◆ Milestone


Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2021												2022							
							Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar							
																			Jan	Feb	Mar					
A3740	Hauling of Z-Beams to Offsite Staging (Pending Offsite Approval)	0	0	10-Mar-22 A	10-Mar-22																					
Phase 1 - Tanks 1E, 2E, 3E		263	0	29-Mar-21 A	11-Mar-22																					
A3500	Install Access for Abatement/Demo	5	0	29-Mar-21 A	13-Apr-21																					
A3430	Prep for Z-Beam Removal - Wait for Abatement progress, Initial Z-Beams removed	10	0	30-Mar-21 A	23-Apr-21																					
A3010	Select Lead & PCB Abatement work to Demo Z-Beams GL B - K	20	0	26-Apr-21 A	23-Dec-21																					
A3460	Traffic Control Access Road	45	0	26-Apr-21 A	04-Jan-22																					
A3030	Z-Beam Removal GL B - K	35	0	03-May-21 A	04-Jan-22																					
A5260	Initial Z-Beams removal for steel, grout work	12	0	24-May-21 A	11-Jun-21																					
A3720	Girder & Column Sawcut Remove at GL D & F	12	0	11-Jan-22 A	11-Mar-22																					
Phase 2 - Tanks 4E, 5E, 6E		428	0	16-Aug-21 A	11-Mar-22																					
A3730	Set Up Gantry & Removal System	10	0	16-Aug-21 A	06-Oct-21																					
A3520	Install Access for Abatement/Demo	5	0	23-Aug-21 A	27-Aug-21																					
A6170	CO18 - Suspension of East Basin Work	3	0	21-Sep-21 A	23-Sep-21																					
A3050	Select Lead & PCB Abatement to Demo Z-Beams GL K - P	20	0	28-Oct-21 A	23-Dec-21																					
A5360	Traffic Control Access Road	61	0	28-Oct-21 A	11-Mar-22																					
A5090	Z-Beam Removal for GL19-20	5	0	28-Oct-21 A	03-Nov-21																					
A3530	Initial Z-Beam Removal GL2-5	4	0	04-Nov-21 A	18-Nov-21																					
A3060	Remaining Z-Beam Removal GL K - P	35	0	19-Nov-21 A	23-Dec-21																					
A3710	Girder & Column Sawcut & Remove at GL K & M	12	0	31-Jan-22 A	10-Mar-22																					
A3760	Remove Gantry System & Removal System	5	0	28-Feb-22 A	03-Mar-22																					
Demo & Install of Odor Control System		618	0	17-May-21 A	29-Sep-23																					
Phase 1 Odor Control - Tanks 1E, 2E, 3E		618	0	17-May-21 A	29-Sep-23																					
A2670	Exhaust Fans EF22BA061, EF22BA051, EF22BA021 operational for 4E, 5E, 6E	0	0	17-May-21 A																						
A2650	Cap 32" ducts at column H @ E/W side of East Basin	1	0	17-May-21 A	17-May-21																					
A2660	Demolish N-S ducts, north of grid H, that serve 1E-3E	5	0	18-May-21 A	21-May-21																					
A2690	Temp Duct from Influent Control Bldg EF22BA061 (includes temp shutdown)	5	0	18-May-21 A	16-Jul-21 A																					
A2680	Temp 32" Duct from Column Line H to EF22BA051	15	0	18-May-21 A	18-Jun-21																					
A3630	Layout/Prep New/Temp Odor Control System	5	0	18-May-21 A	24-May-21																					
A5080	Temp Odor Control for Tanks 1E-3E	6	0	12-Jul-21 A	23-Jul-21 A																					
A2990	Install Duct Supports at GL 2-5	3	0	01-Mar-22 A	14-Apr-23																					
A3420	Install Duct Supports at GL 19-20	3	0	02-Mar-22 A	14-Apr-23																					
A5720	CO#06.1 - Additional Duct Supports Per RFI 23 & 24	1	0	08-Nov-22 A	08-Nov-22																					
A5730	CO#06.2 - Duct Support and Stanchion Additions Per RFI 40 & 44	1	0	09-Nov-22 A	09-Nov-22																					
A5940	CO#11.1 - RCO 05 Duct Support 04 Modifications	1	0	10-Nov-22 A	10-Nov-22																					
A5970	CO#12.1 - RCO 60 Missing Duct Supports	1	0	10-Nov-22 A	10-Nov-22																					
A2700	Install FRP Duct at GL2-5	6	0	24-Mar-23 A	21-Apr-23																					
A2870	Install FRP Duct at GL 19-20	6	0	24-Mar-23 A	21-Apr-23																					
A5810	Fiberglass Duct Joints (Weather Dependent)	20	0	24-Apr-23 A	28-Jul-23 A																					
A5850	Remove Temp Ducting	6	0	05-Jun-23 A	04-Aug-23																					
A2300	Odor Control - Ready for Operation in 1E, 2E and 3E	0	0		04-Aug-23																					
A6210	Condensate Line from Duct	5	0	05-Sep-23 A	29-Sep-23																					
Phase 2 Odor Control - Tanks 4E, 5E, 6E		526	0	27-Sep-21 A	29-Sep-23																					
A3000	Temp Duct Tanks 4E, 5E, 6E	3	0	27-Sep-21 A	30-Sep-21																					
A2730	Demolish existing Ducts serving tanks 4E to 6E	10	0	07-Oct-21 A	19-Oct-21																					
A5630	Install FRP Duct Support from column line H	15	0	20-Feb-23 A	26-May-23																					
A2740	Install FRP Duct to the Influent Screenings Building	12	0	03-Apr-23 A	30-Jun-23																					
A2780	Install FRP Duct from column line H	12	0	03-Apr-23 A	16-Jun-23																					

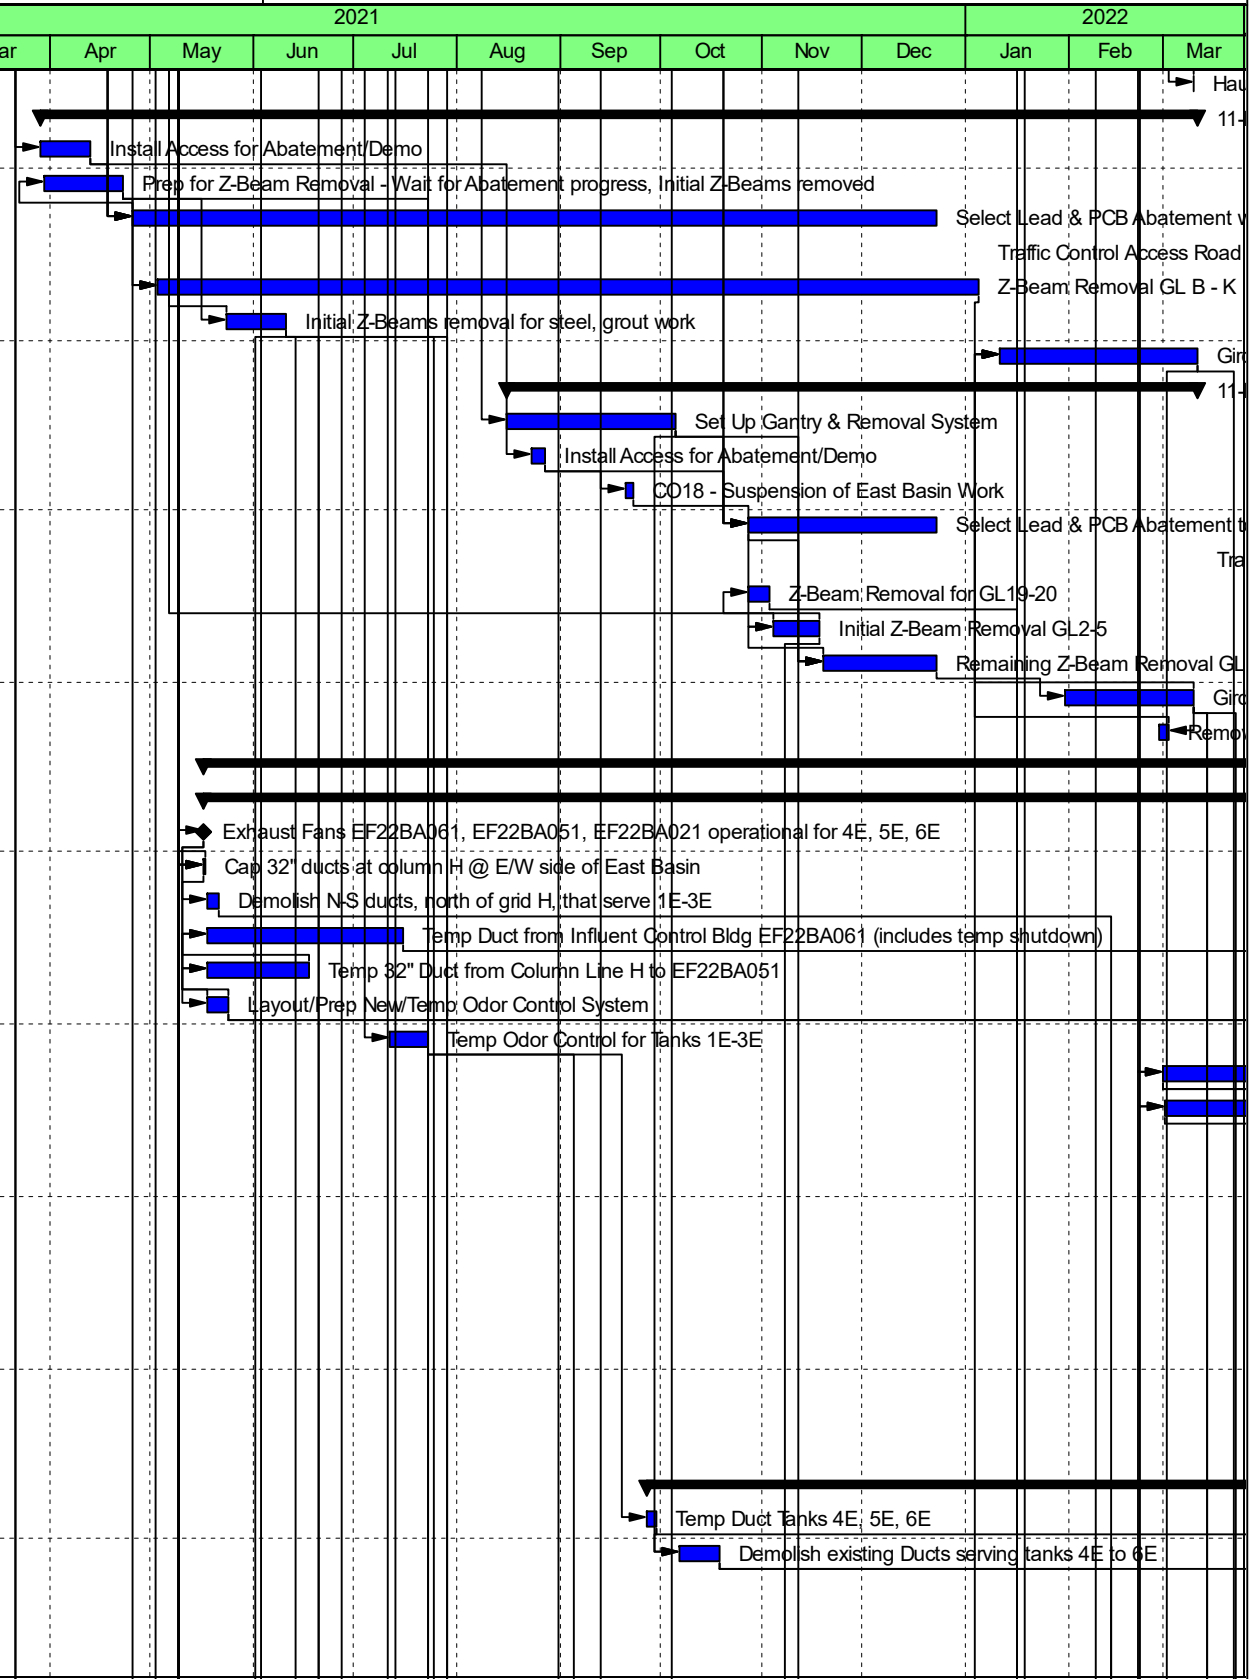


Actual Work Critical Remaining Work Summary
 Remaining Work Milestone

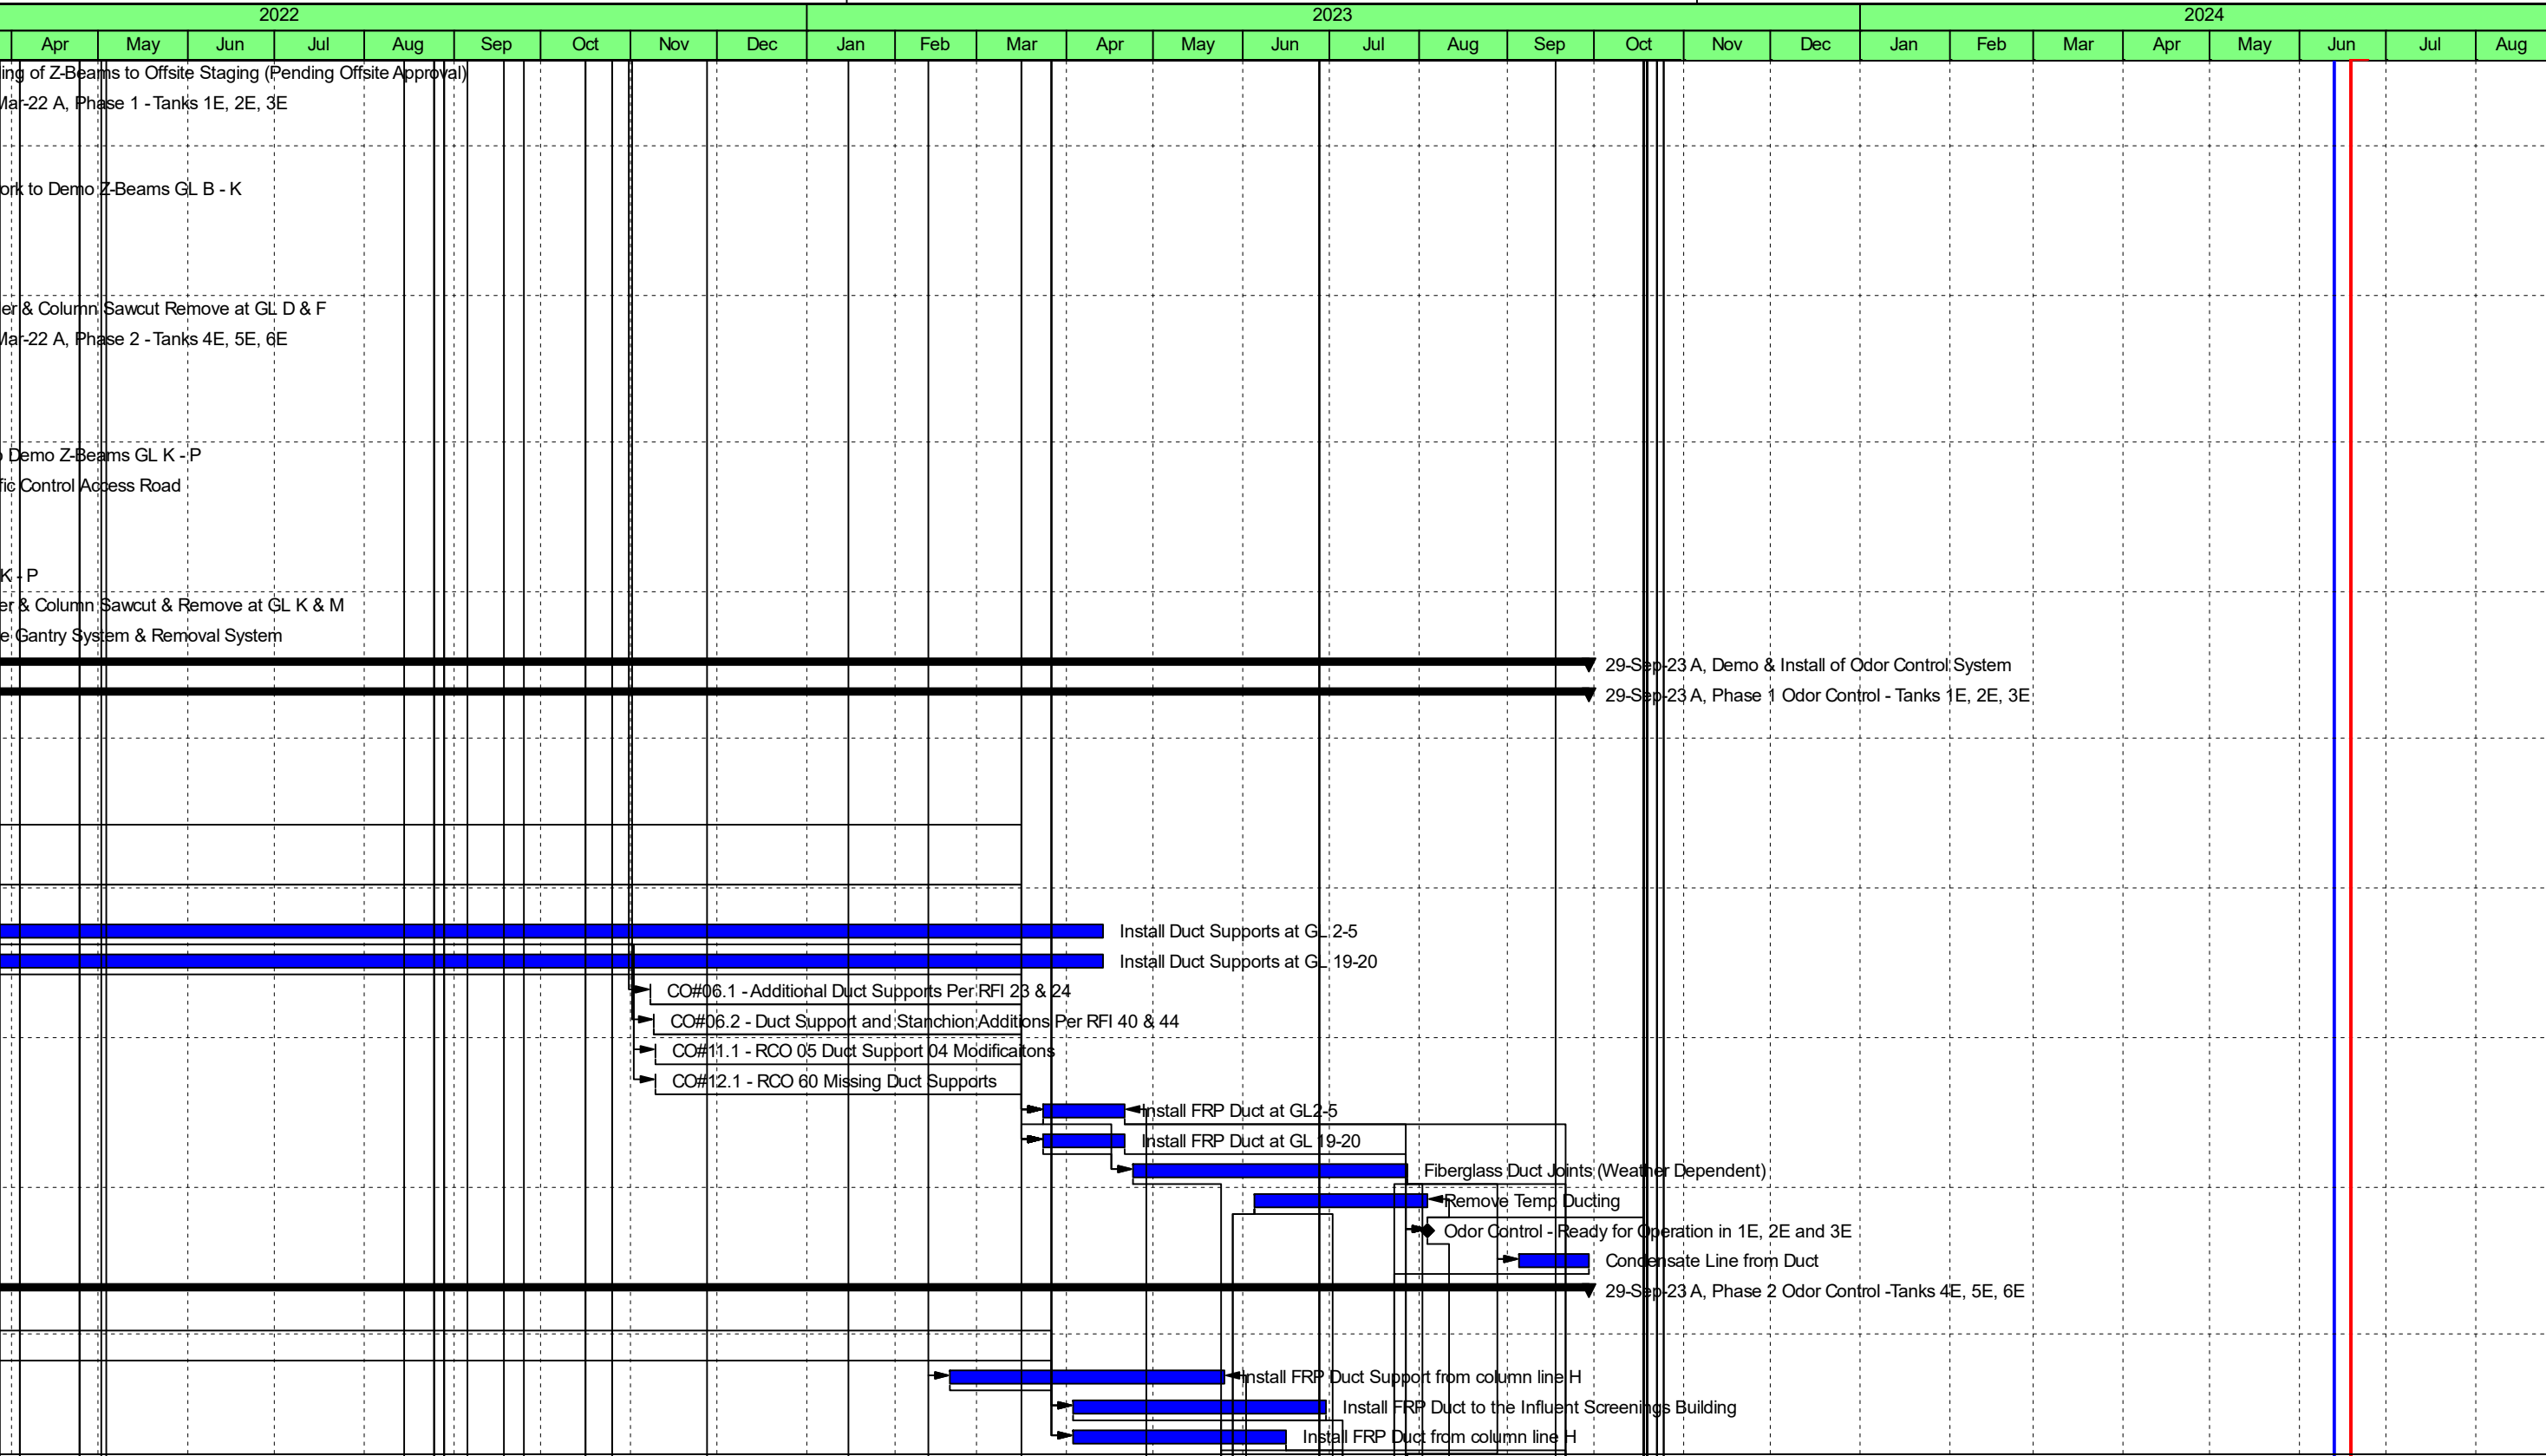


Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2021												2022			
							Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar			
A5830	Fiberglass Duct Joints (Weather Dependent)	10	0	01-Jun-23 A	28-Jul-23 A																	
A5840	Remove Temp Ducting	10	0	05-Jun-23 A	04-Aug-23 A																	
A2750	Connect FRP Duct to the Influent Screenings Building	2	0	13-Jul-23 A	28-Jul-23 A																	
A2760	Connect permanent duct from Influent Scr/Bldg to EF22BA061. Demo Temp (includes sh	2	0	13-Jul-23 A	28-Jul-23 A																	
A2790	Connect new duct tanks 1E to 6E to EF22BA051 and remove temp duct (includes shutdc	2	0	13-Jul-23 A	25-Jul-23 A																	
A6220	Condensate Line from Duct	5	0	31-Jul-23 A	29-Sep-23 A																	
A2320	Odor Control - Ready for Operation in 4E, 5E, 6E	0	0		04-Aug-23 A																	
A2770	Balance EF22BA061 - per M002	0	0	04-Aug-23 A																		
A2800	Balance East Basin foul exhaust system per M132 and balance EF22BA051 to M002	0	0	10-Aug-23 A																		
Removal & Replace Electrical and Lighting System		633	0	29-Mar-21 A	13-Jul-23 A																	
Phase 1 - Tanks 1E, 2E, 3E		633	0	29-Mar-21 A	13-Jul-23 A																	
A2960	Install Temp Power & Temp Lighting	10	0	29-Mar-21 A	05-May-21																	
A5580	Layout Electrical Work	1	0	29-Mar-21 A	02-Apr-21																	
A3070	Isolate Circuits, Disc. and Remove Conduit/Conductors	5	0	17-May-21 A	10-Jun-21																	
A3150	North Quadrant - 1E to 3E (out of operation)	0	0	17-May-21 A																		
A3550	Remove & Replace Wiring Devices	5	0	09-Jun-21 A	28-Feb-22																	
A5290	CO#001 - RCO 12 Control Panel Demo Conflict	5	0	09-Jun-21 A	18-Jun-21																	
A3080	Install Conduit Chase at 14E/15E	5	0	11-Jun-21 A	01-Jul-21 A																	
A3110	Pull new conductors and connect equipment and devices	8	0	28-Jun-21 A	28-Jul-21 A																	
A5300	CO#001 - RCO 13 Missing Control Wires	8	0	28-Jun-21 A	28-Jul-21 A																	
A5740	CO#06.3 - Effluent Pump Conduit Missing Information Per RFI 46	1	0	28-Jun-21 A	28-Jul-21 A																	
A3690	Install Conduit on Support System at GL H	8	0	19-Jul-21 A	23-Jul-21 A																	
A3090	Install Conduit at gridline 3E / 4E	3	0	21-Jul-21 A	28-Jul-21 A																	
A5760	CO#007 - Missing Conduit Runs Per RFI 57	1	0	29-Jul-21 A	29-Jul-21 A																	
A2980	Install Handrail Extensions on N-S Conduit Chase	10	0	09-Aug-21 A	12-May-22																	
A3100	Remove and replace light fixtures under canopy roof	5	0	20-Sep-21 A	07-Apr-22																	
A3130	Install Ligth Poles, Conduits & Terminate Wires	10	0	12-Oct-21 A	21-Apr-22																	
A5650	CO#001 - RCO 25 Replace Conduit @ Column 8E	10	0	12-Oct-21 A	05-Nov-21																	
A5660	CO#001 - RCP 02 Replace Longitudinal Sludge Collector Switches	1	0	10-Mar-22 A	10-Mar-22																	
A3120	Remove existing conduits & Temp System no longer in use	15	0	14-Mar-22 A	18-Mar-22																	
A6040	CO14.2 - RCO 71 Light Pole Location	1	0	20-Apr-22 A	21-Apr-22																	
A3440	Install Grating Over Conduit Chase	1	0	26-Sep-22 A	28-Sep-22																	
A6190	CO#18 - Cable Protection Details at GL14.5	5	0	03-Oct-22 A	07-Oct-22																	
A2340	Tanks 1E, 2E, 3E - System Testing	1	0	02-Nov-22 A	02-Nov-22																	
A3360	Install Skum Skimmer Motors	5	0	02-Nov-22 A	02-Nov-22																	
A2270	WPTP - North Quadrant (1E, 2E, 3E) - Operational Testing	5	0	03-Nov-22 A	09-Nov-22																	
A5950	CO#11.2 - RCP 05 Misc Electrical Components	10	0	23-Jan-23 A	01-Mar-23																	
A2390	Install Light Poles in Conflict with Temp Duct	3	0	10-Jul-23 A	13-Jul-23 A																	
Phase 2 - Tanks 4E, 5E, 6E		332	0	26-Jul-21 A	09-Nov-22																	
A3140	South Quadrant Start- Tuned Over by KC	0	0	26-Jul-21 A																		
A3540	Temp Power & Temp Lighting	5	0	26-Jul-21 A	30-Jul-21 A																	
A3160	Isolate Circuits, Disc. and Remove Conduit/Conductors	5	0	02-Aug-21 A	13-Aug-21																	
A3170	Install conduit on Tie Beams grid 14E/15E	7	0	10-Aug-21 A	03-Sep-21																	
A3180	Install Conduit at 3E/4E	7	0	10-Aug-21 A	03-Sep-21																	
A3200	Remove and replace wiring devices serving tanks 4E, 5E, 6E	7	0	17-Aug-21 A	07-Apr-22																	
A3210	Pull new conductors and connect equipment and devices	7	0	31-Aug-21 A	08-Sep-21																	
A3190	Remove and replace light fixtures under the canopy roof	5	0	01-Apr-22 A	07-Apr-22																	

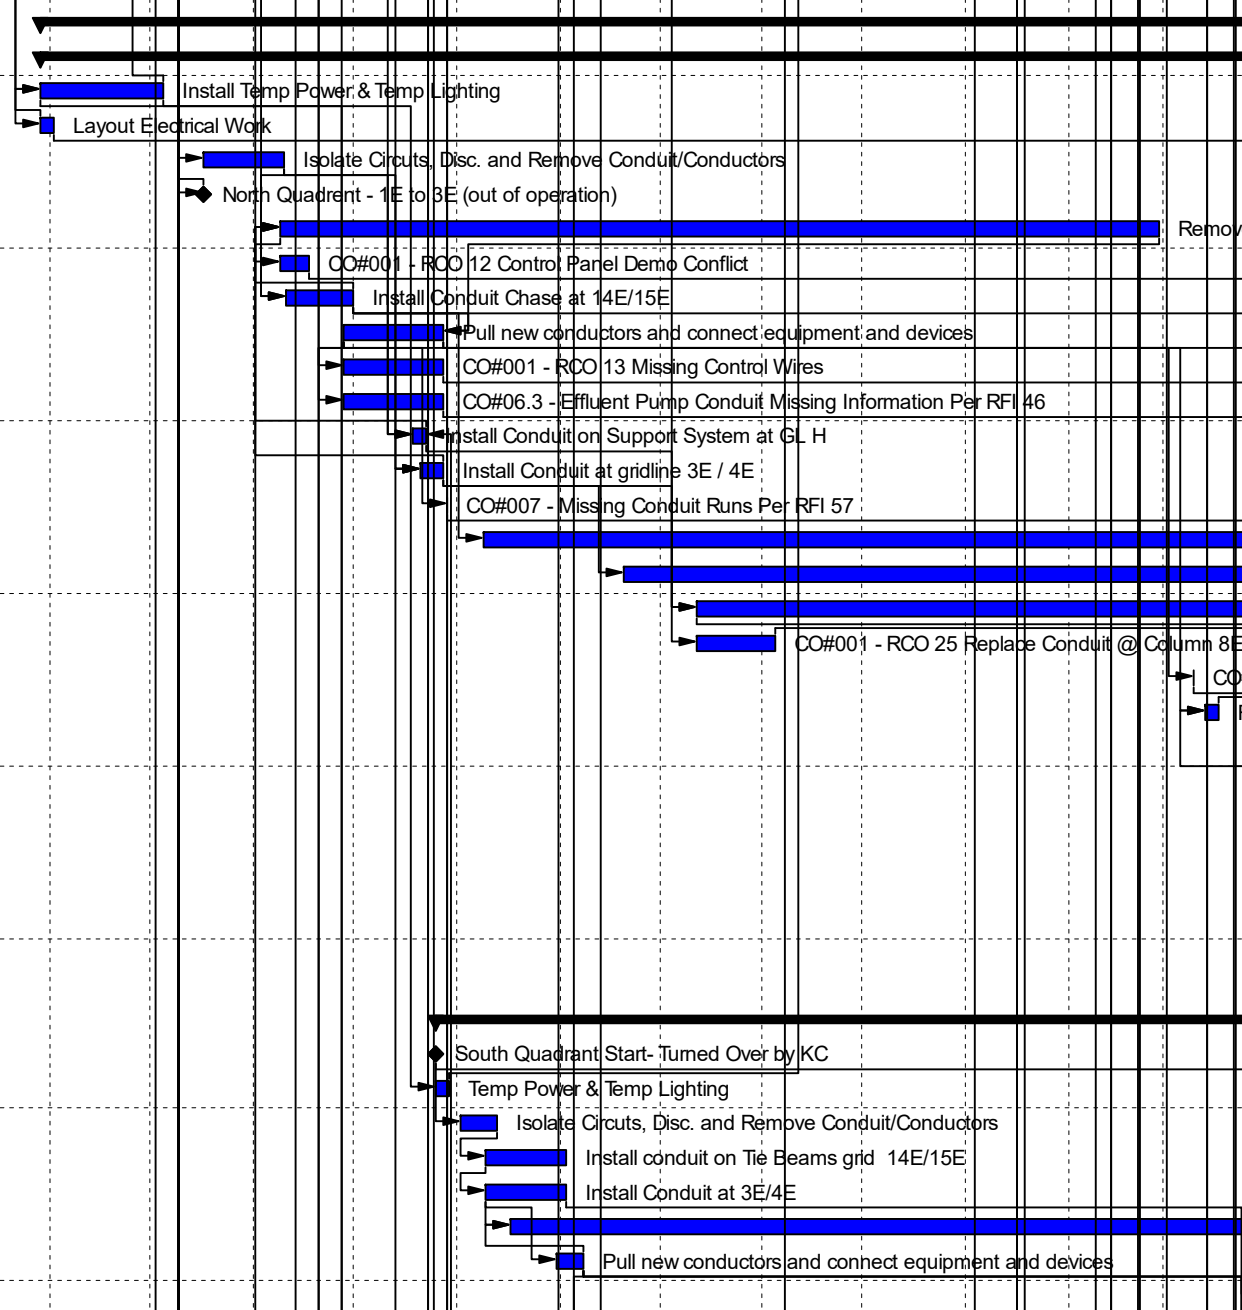

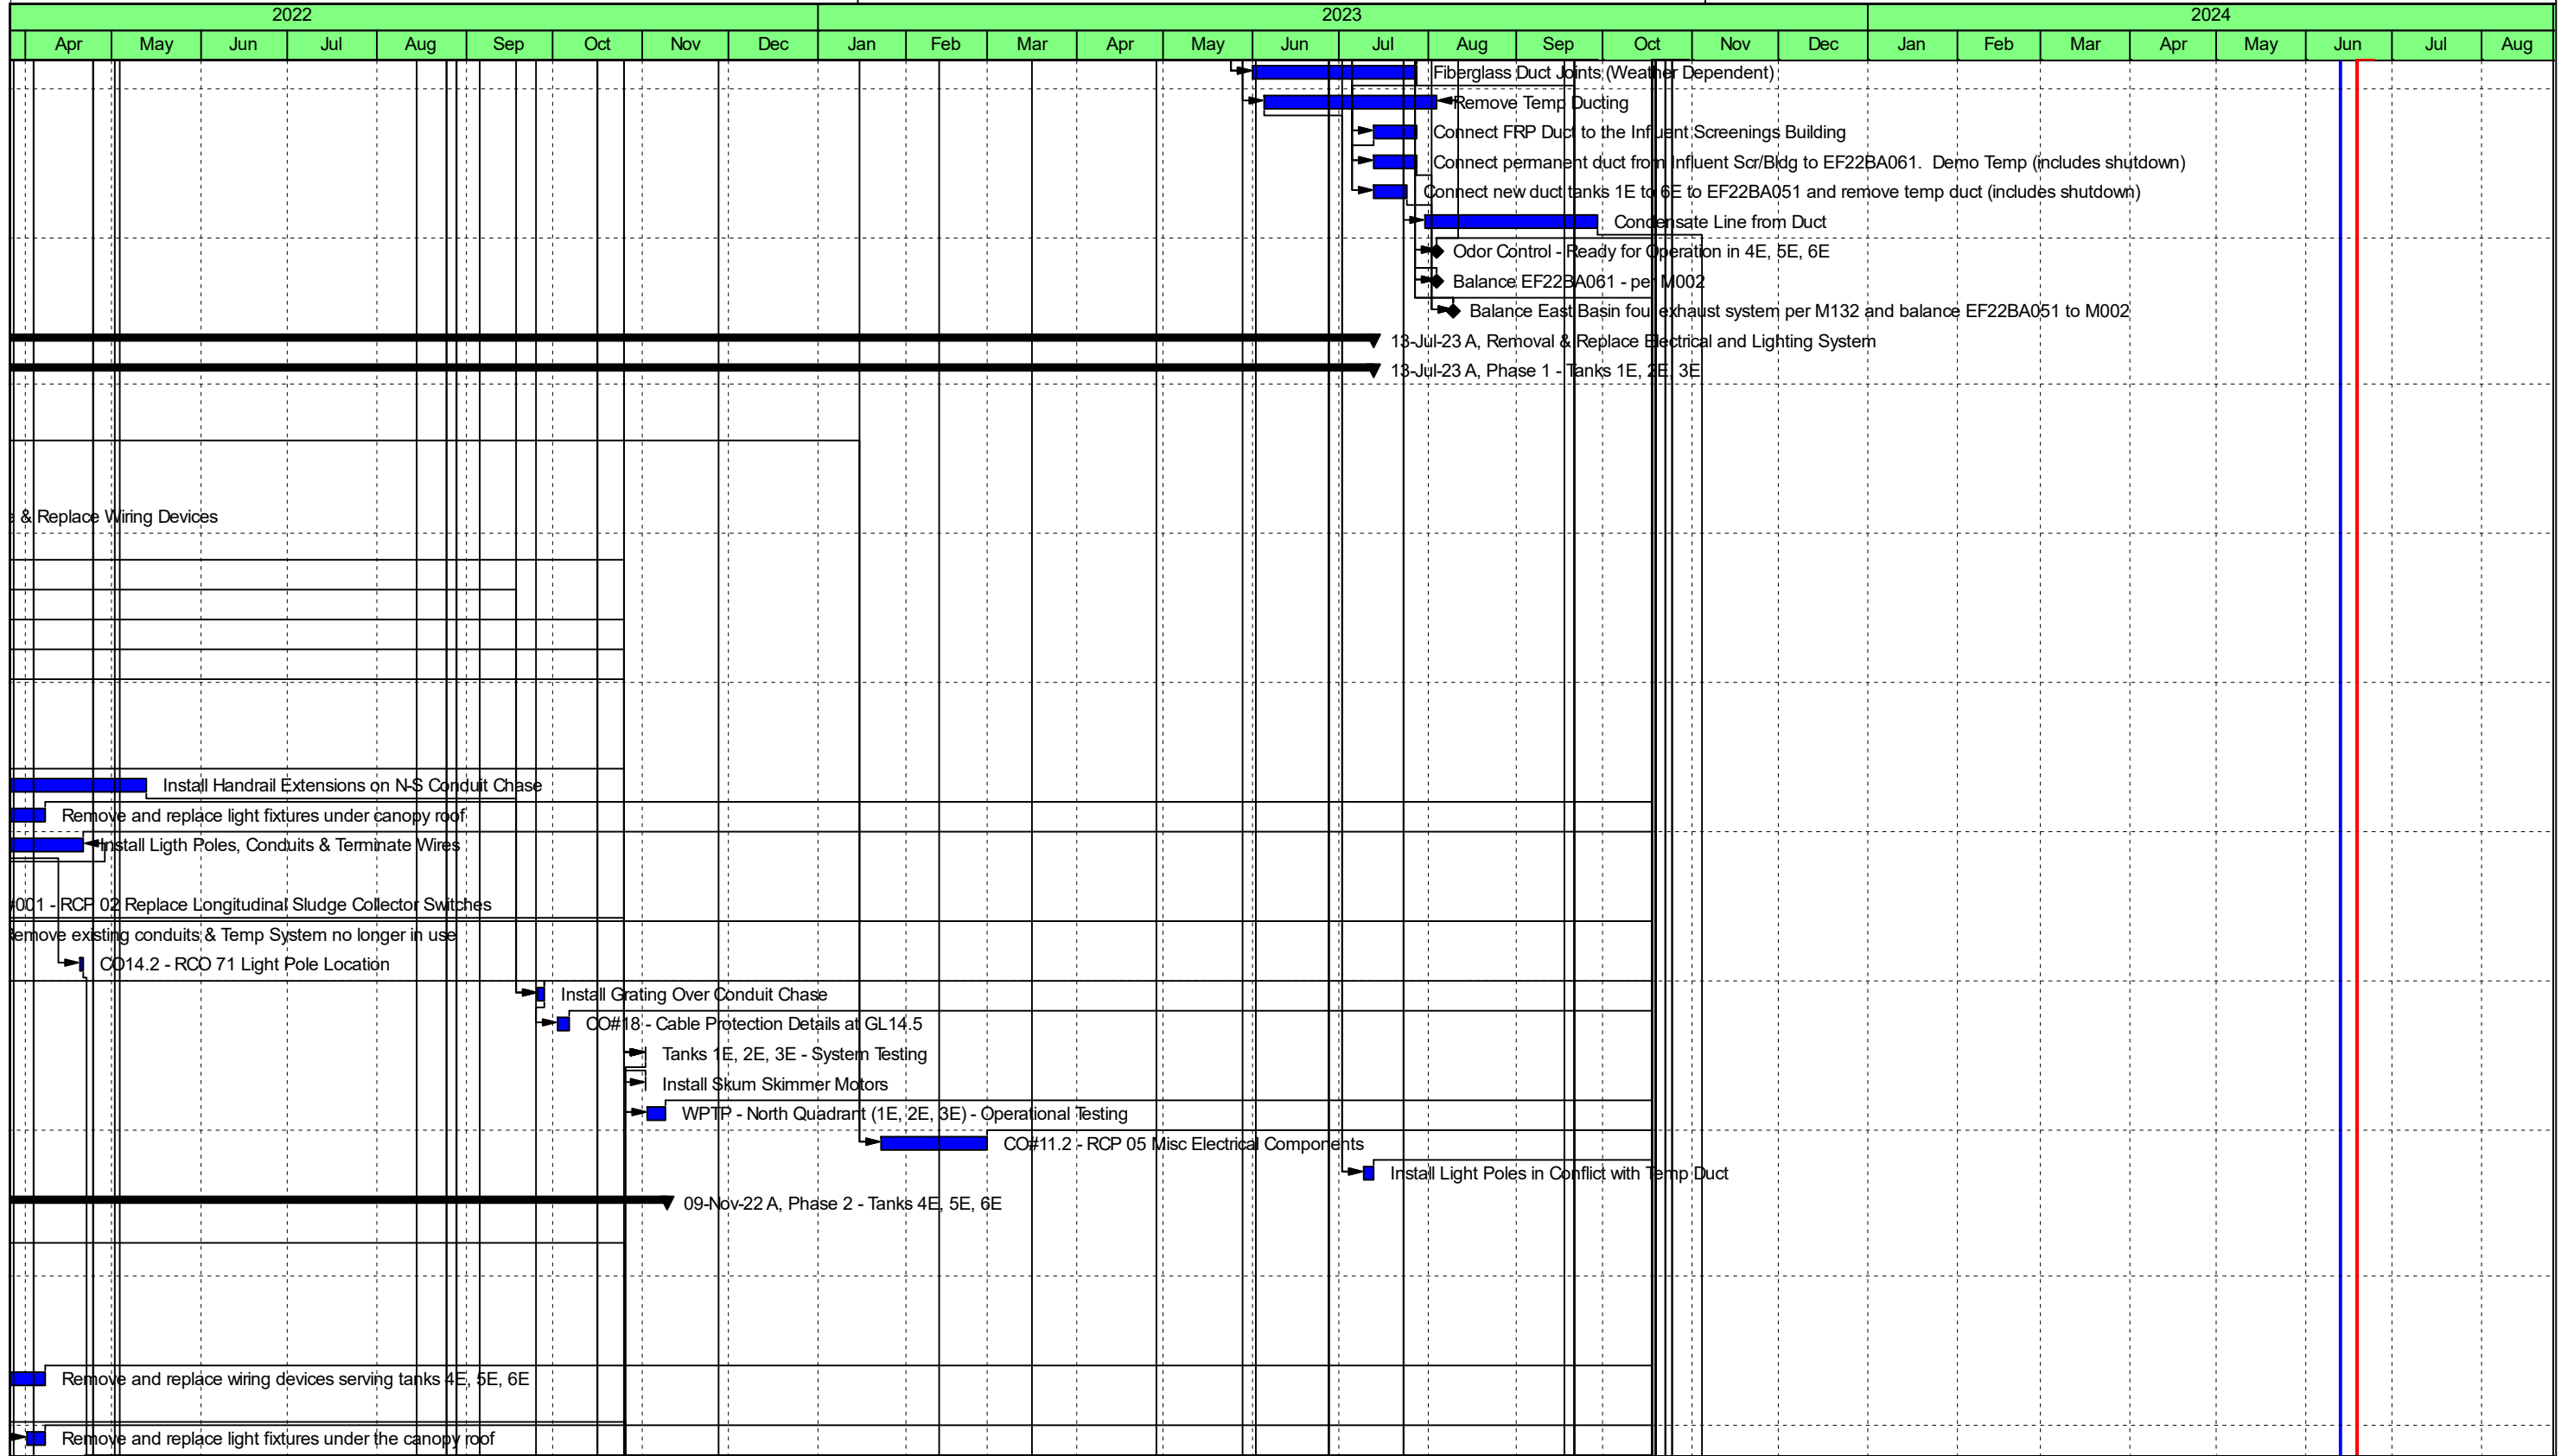

█ Actual Work
 █ Critical Remaining Work
 █ Remaining Work
 ◆ Milestone
 ▼ Summary


Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2021												2022				
							Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar				
A3220	Remove existing conduits no longer in use	15	0	01-Apr-22 A	21-Apr-22																		
A3700	Install Ligth Poles and Conduits to	10	0	01-Apr-22 A	14-Apr-22																		
A4960	Install Skum Skimmer Motors	5	0	02-Nov-22 A	02-Nov-22																		
A4980	Tanks 4E, 5E, 6E - System Testing	1	0	03-Nov-22 A	09-Nov-22																		
A2310	WPTP - South Quadrant (4E, 5E, 6E) - Operational Testing	5	0	04-Nov-22 A	09-Nov-22																		
Other New Constcrtion		665	0	09-Jun-21 A	27-Oct-23																		
Phase 1 - Tanks 1E, 2E, 3E		638	0	09-Jun-21 A	27-Oct-23																		
A3950	Grout Back Z-Beam Voids	10	0	09-Jun-21 A	10-Mar-22																		
A5770	CO#007 - HDPE Grit Line Conflict (RFI 027)	1	0	14-Jun-21 A	15-Jun-21																		
A3850	Access For Steel/FRP Roof & Duct Support Steel Install	21	0	21-Jun-21 A	28-Jan-22																		
A3860	Drill & Dowel for Roof Install (Steel Support)	10	0	21-Jun-21 A	14-Jul-21 A																		
A3870	Install Structural Steel For Roof	4	0	28-Jun-21 A	30-Jul-21 A																		
A2970	Permanent Supports for Primary E-W conduit runs	10	0	05-Jul-21 A	19-Jul-21 A																		
A3900	Canopy Roof Expansion Joint Modifications Between GL A-B	4	0	02-Aug-21 A	03-Mar-22																		
A3890	Install Steel for Duct Supports at GL 19-20	5	0	06-Aug-21 A	26-Jan-22																		
A3880	Install Steel for Duct Support at GL 2-5	4	0	08-Sep-21 A	31-Jan-22																		
A3910	Install FRP Panels	3	0	21-Sep-21 A	05-Sep-22																		
A3970	Chip/Patch Columns Stubs	2	0	18-Jan-22 A	22-Mar-22																		
A3940	Demo/Removal of Existing EPDM Roofing Membrane	5	0	21-Feb-22 A	27-Oct-22																		
A6060	RCO 063 - Existing Flat Roof Membrane	10	0	01-Mar-22 A	27-Oct-22																		
A3980	Concrete Repairs per S202	2	0	08-Mar-22 A	09-Mar-22																		
A3990	Fill & Cap Rain Leader	2	0	21-Mar-22 A	22-Mar-22																		
A3960	Grout Back Girder Voids	5	0	30-Mar-22 A	05-Apr-22																		
A5530	Handrail & Safety Gate Mod S451	1	0	02-May-22 A	05-May-22																		
A5020	Install Monorail Hoist	2	0	09-May-22 A	29-Dec-22																		
A5980	CO#12.2 RCO 61 Conduit Support Frame Conflict	1	0	30-Nov-22 A	30-Nov-22																		
A5860	Demo of Roof Membrane in Conflict with Temp Duct	5	0	05-Jun-23 A	30-Jun-23																		
A3930	Install EPDM Membrane over Existing Flat Roof	5	0	11-Sep-23 A	15-Sep-23																		
A5440	Install Roofing Membrane over FRP Panels (Weather Dependent)	10	0	28-Sep-23 A	27-Oct-23																		
Phase 2 - Tanks 4E, 5E, 6E		511	0	15-Nov-21 A	27-Oct-23																		
A4720	Grout Back Z-Beam Voids	8	0	15-Nov-21 A	20-Jan-22																		
A5780	CO#007 - Hoist Beam Chlorine Line Conflict	1	0	08-Dec-21 A	08-Dec-21																		
A4670	Access For Steel/FRP Roof & Duct Support Steel Install	19	0	03-Jan-22 A	27-Jan-22																		
A4680	Drill & Dowel for Roof Install	6	0	17-Jan-22 A	21-Jan-22																		
A4700	Canopy Roof Expansion Joint Modifications Between GL P-Q	4	0	17-Jan-22 A	03-Mar-22																		
A4780	Install Steel for Duct Supports at GL 19-20	5	0	24-Jan-22 A	25-Jan-22																		
A4730	Install Structural Steel For Roof	5	0	26-Jan-22 A	31-Jan-22																		
A6160	CO#18 - Structural Steel Conflicts	3	0	26-Jan-22 A	31-Jan-22																		
A4790	Install Steel for Duct Support at GL 2-5	5	0	16-Feb-22 A	22-Feb-22																		
A4690	Demo/Removal of Existing EPDM Roofing Membrane	5	0	21-Feb-22 A	27-Oct-22																		
A4750	Concrete Repairs per S202	4	0	01-Mar-22 A	04-Mar-22																		
A4740	Chip/Patch Columns Stubs	2	0	22-Mar-22 A	23-Mar-22																		
A4760	Fill & Cap Rain Leader	2	0	22-Mar-22 A	23-Mar-22																		
A4800	Grout Back Girder Voids	5	0	30-Mar-22 A	04-Apr-22																		
A4770	Install FRP Panels	3	0	11-Apr-22 A	05-Sep-22																		
A5540	Handrail & Safety Gate Mod S451	1	0	02-May-22 A	05-May-22																		
A5030	Install Monorail Hoist	2	0	11-May-22 A	29-Dec-22																		

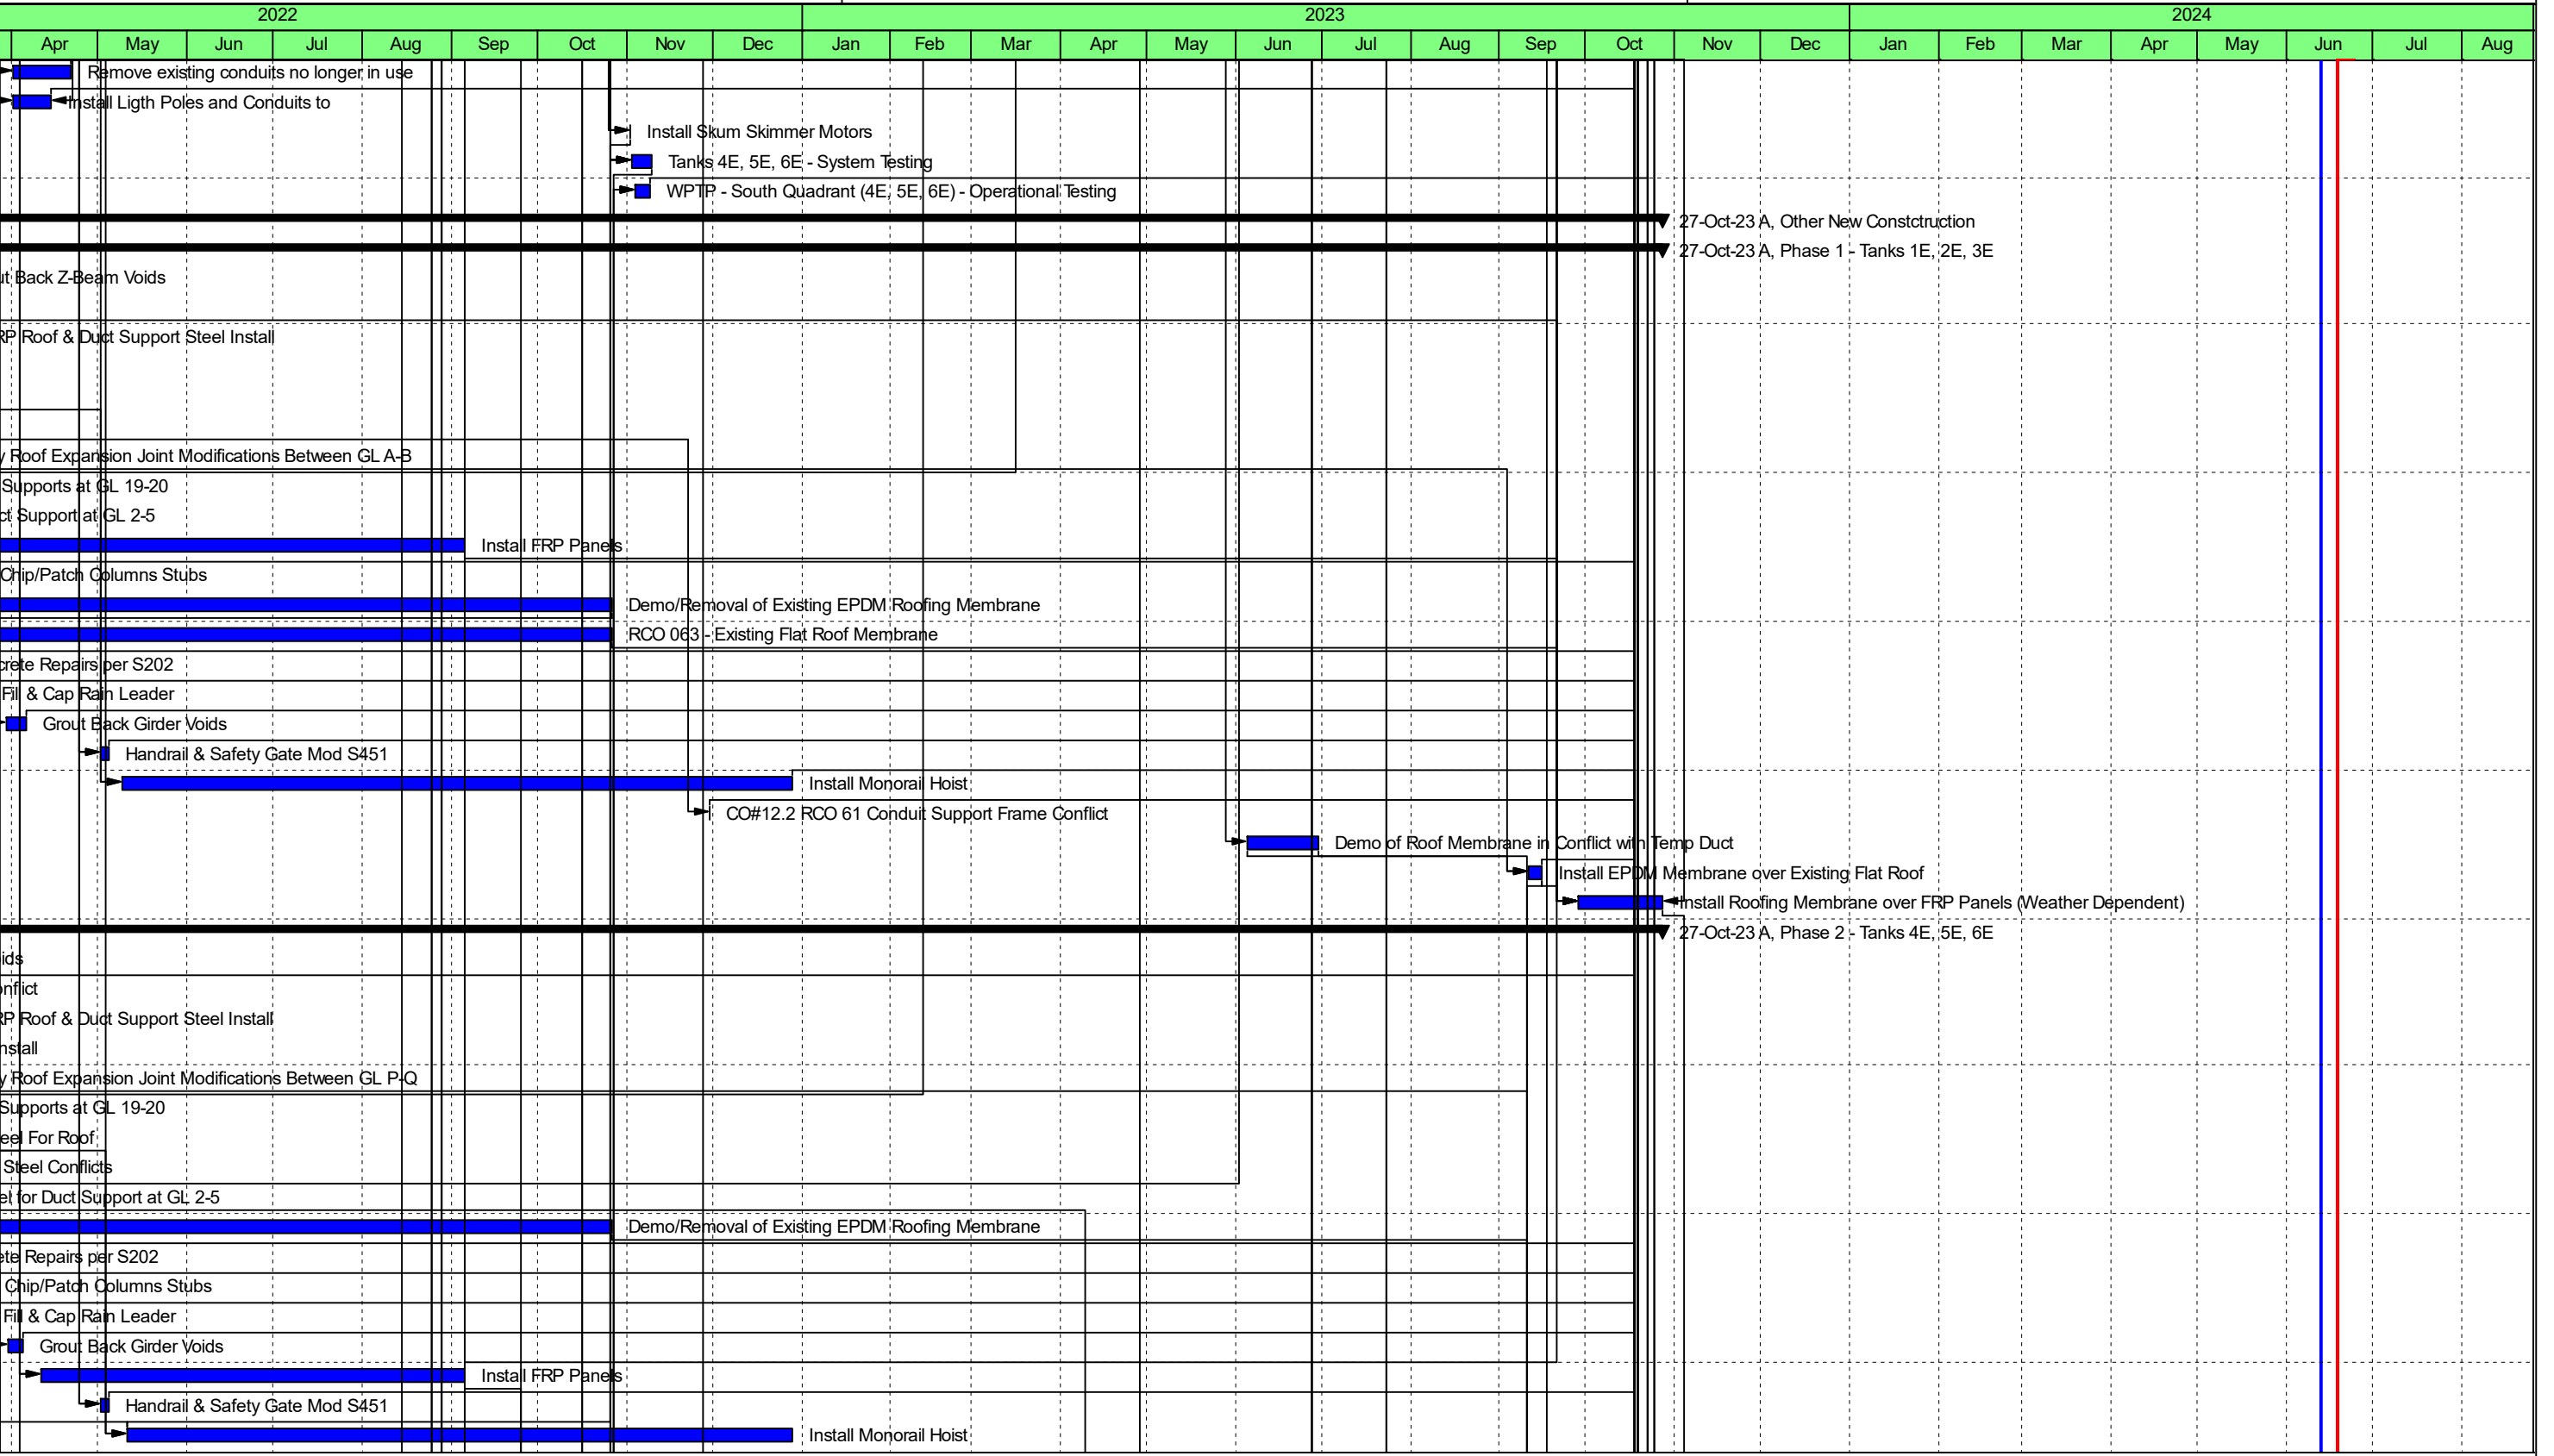


█ Actual Work
 █ Critical Remaining Work
 Summary
 Remaining Work
 ◆ Milestone

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2021												2022					
							Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar					
A6180	CO#18 - Permanent Grit Pipe Routing	5	0	03-Oct-22 A	07-Oct-22																			
A6200	CO#18 - Duct Support Frame Deflection	20	0	17-Apr-23 A	21-Apr-23																			
A4710	Install EPDM Membrane over Existing Flat Roof (Weather Dependent)	5	0	18-Sep-23 A	22-Sep-23																			
A5450	Install Roofing Membrane over FRP Panels (Weather Dependent)	10	0	28-Sep-23 A	27-Oct-23																			
In Tank Concrete Upgrades		411	0	10-Mar-21 A	05-May-22																			
A3230	Select Removal/Tag/Store of Handrail & Install Temp Rail at Tanks 1E, 2E, 3E	3	0	10-Mar-21 A	12-Mar-21																			
A3020	Select Removal/Tag/Store Flat Bat & Odor Control Covers for Tanks 1E, 2E, 3E	5	0	10-May-21 A	14-May-21																			
A3770	Sanitize & Disinfect Tank 1E, 2E, 3E	3	0	13-May-21 A	18-May-21																			
A2190	East Basin - Constraint Start (or earlier per 011400.1.03B)	0	0	17-May-21 A																				
A2220	East Basin - Work Window Period	87	0	17-May-21 A	17-Sep-21																			
A5430	Tanks 1E, 2E and 3E (North Quadrant) Concrete Repair Work	30	0	17-May-21 A	16-Jul-21 A																			
A2720	CO#05.2 - Scum Trough Spilling into Tanks	1	0	27-May-21 A	27-May-21																			
A5710	CO#05.4 - RFI 31 15E Column Wrap Conflict	1	0	01-Jun-21 A	02-Jul-21 A																			
A5280	CO#05.3 - East Basin Tanks 1-3 Aeration Tank Baffle Conflict	1	0	07-Jun-21 A	11-Jun-21																			
A5680	CO#03 - Column Base Utility Conflicts - Phase 1	5	0	14-Jun-21 A	18-Jun-21																			
A5670	CO#02 - RCO 22 Pipe & Curb Conflict - Phase 1	2	0	14-Jul-21 A	16-Jul-21 A																			
A2480	Re-Install Removed Odor Control Panels & Flatbar Tanks 1E, 2E, 3E	5	0	19-Jul-21 A	23-Jul-21 A																			
A3780	Re-Install Removed Handrail Tanks 1E, 2E, 3E	5	0	19-Jul-21 A	23-Jul-21 A																			
A3790	Select Removal/Tag/Store Flat Bat & Odor Control Covers for Tanks 4E, 5E, 6E	3	0	21-Jul-21 A	23-Jul-21 A																			
A3800	Select Removal/Tag/Store of Handrail & Install Temp Rail at Tanks 4E, 5E, 6E	3	0	21-Jul-21 A	23-Jul-21 A																			
A2470	Sanitize & Disinfect Tank 4E, 5E, 6E	2	0	26-Jul-21 A	30-Jul-21 A																			
A5420	Tanks 4E, 5E and 6E (South Quadrant) Concrete Repair Work	29	0	28-Jul-21 A	13-Sep-21																			
A5820	CO#08 - Phase 2 In-Tank Changes RFI 77	1	0	28-Jul-21 A	13-Sep-21																			
A5690	CO#01 - RCO 33 Process Water Channel Concrete Reinf Conflict	1	0	10-Sep-21 A	10-Sep-21																			
A2330	East Basin - Emergency Shutdown (anticipated two weeks interruption)	10	0	13-Sep-21 A	13-Sep-21																			
A2510	East In-Basin Work Complete	0	0		13-Sep-21																			
A2520	WPTP - North Quadrant (1E, 2E, 3E) Ready for Service	0	0		13-Sep-21																			
A2200	East Basin - Constraint End	0	0		17-Sep-21																			
A5910	CO#09.1 FD05 Scum Trough Repairs	10	0	23-Sep-21 A	07-Oct-21																			
A3810	Re-Install Removed Odor Control Panels & Flatbar Tanks 4E, 5E, 6E	5	0	27-Sep-21 A	30-Sep-21																			
A3820	Re-Install Removed Handrail Tanks 4E, 5E, 6E	5	0	27-Sep-21 A	30-Sep-21																			
A3830	Modifications to Odor Control Panels for Tank 1E, 2E, 3E	5	0	02-May-22 A	05-May-22																			
A3840	Modifications to Odor Control Panels for Tank 4E, 5E, 6E	5	0	02-May-22 A	05-May-22																			
West Basin		445	0	10-Mar-22 A	27-Oct-23																			
Concrete Demolition & Disposal		144	0	10-Mar-22 A	31-Oct-22																			
A4320	Install Access to Roof Level	5	0	10-Mar-22 A	15-Mar-22																			
A3510	Install Temporary Protections - Basin Work	5	0	21-Mar-22 A	26-Mar-22																			
A5310	Abate Lead Paint off Z-Beams at Off-Site Staging Area	25	0	30-Mar-22 A	25-Aug-22																			
A4300	Hauling of Z-Beams to Offsite Staging	65	0	01-Apr-22 A	31-Aug-22																			
A5320	Crush & Process Concrete at Staging Area	35	0	04-Apr-22 A	31-Aug-22																			
A5330	Haul & Dispose of Concrete	35	0	04-Apr-22 A	31-Oct-22																			
A4310	Hauling of Girders & Columns to Offsite Staging	37	0	28-Jul-22 A	24-Oct-22																			
Phase 3 - Tanks 4W, 5W, 6W		142	0	10-Mar-22 A	20-Oct-22																			
A5370	Install Access for Abatement/Demo	5	0	10-Mar-22 A	15-Mar-22																			
A4260	Set Up Gantry & Removal System	10	0	16-Mar-22 A	31-Mar-22																			
A4250	Select Lead & PCB Abatement to Demo Z-Beams GL K - P	20	0	31-Mar-22 A	25-Aug-22																			
A5390	Traffic Control Access Road	13	0	31-Mar-22 A	25-Aug-22																			


█ Actual Work
 █ Critical Remaining Work
 ▶ Summary
█ Remaining Work
 ◆ Milestone

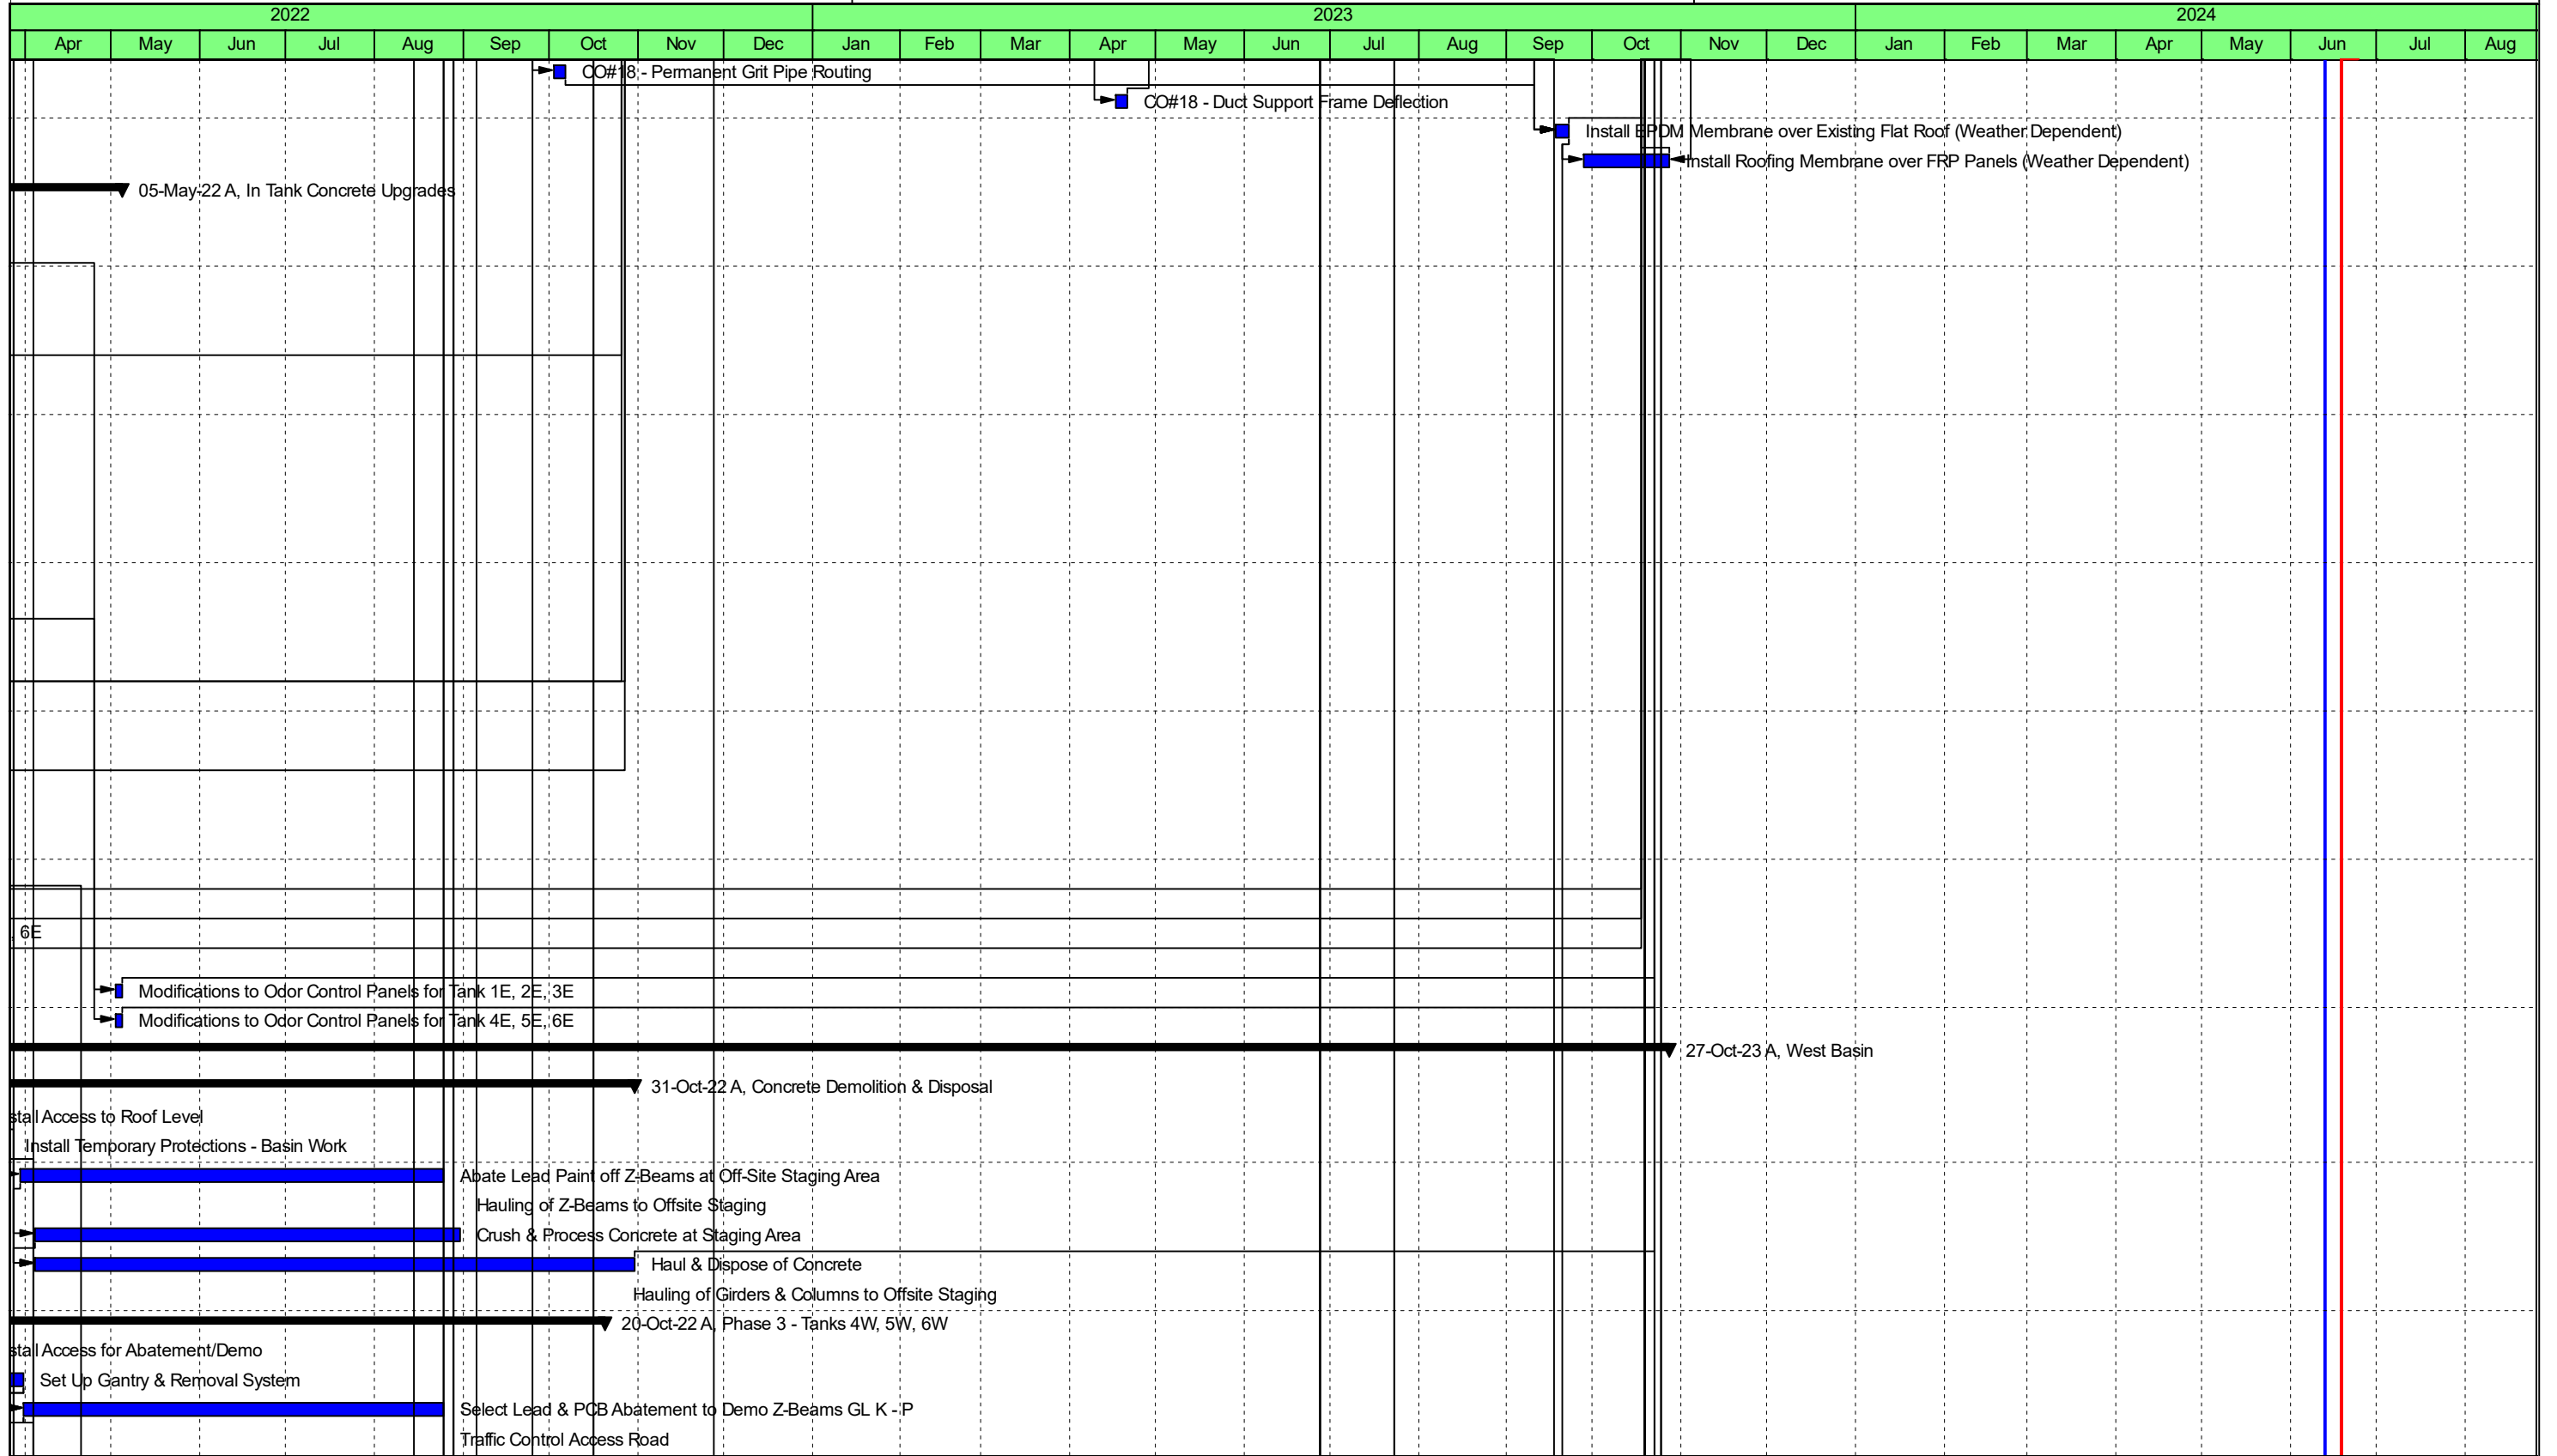

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2021												2022			
							Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar			
A4270	Z-Beam Removal GL K - P (Not Supporting Existing Duct System)	30	0	01-Apr-22 A	25-Aug-22																	
A5490	Z-Beam Removal GL K - P (Beams Supporting Existing Duct System)	2	0	16-May-22 A	09-Jun-22																	
A4280	Girder & Column Sawcut & Remove at GL K & M	12	0	28-Jul-22 A	20-Oct-22																	
A4290	Remove Gantry System & Removal System	2	0	28-Jul-22 A	20-Oct-22																	
Phase 4 - Tanks 1W, 2W, 3W		132	0	17-Mar-22 A	20-Oct-22																	
A5380	Install Access for Abatement/Demo	5	0	17-Mar-22 A	23-Mar-22																	
A4220	Select Lead & PCB Abatement work to Demo Z-Beams GL B - K	20	0	11-Apr-22 A	25-Aug-22																	
A4230	Z-Beam Removal GL B - K (Not Supporting Existing Duct System)	35	0	11-Apr-22 A	25-Aug-22																	
A5400	Traffic Control Access Road	45	0	11-Apr-22 A	25-Aug-22																	
A5590	Z-Beam Removal GL B - K (Supporting Existing Duct System)	1	0	13-Jun-22 A	30-Jun-22																	
A4240	Girder & Column Sawcut Remove at GL D & F	12	0	28-Jul-22 A	20-Oct-22																	
Demo & Install Odor Control System		412	0	04-Apr-22 A	27-Oct-23																	
Phase 3 Odor Control - Tanks 4W, 5W, 6W		412	0	04-Apr-22 A	27-Oct-23																	
A2810	Provide Temp duct from grid H to GL P	5	0	04-Apr-22 A	02-May-22																	
A3380	Layout/Prep New & Temp Duct System	1	0	04-Apr-22 A	03-Jun-22																	
A2820	Connect Temp duct to existing duct serving Tanks 1W to 3W on both east and west side c	1	0	03-May-22 A	04-May-22																	
A2860	Remove Existing ducts serving tanks 4W, 5W, 6W	4	0	10-May-22 A	31-May-22																	
A2840	Provide Temp duct from grid P to exhaust fan EF22BA021	3	0	23-May-22 A	30-Jun-22																	
A2830	Connect existing duct from Influent Screening Bldg. Temp 1W, 2W, 3W and influent Buildir	1	0	25-May-22 A	26-May-22																	
A2850	Exhaust fan EF22BA021 serving West Basin temp re-balanced to 18,515 CFM	0	0	26-May-22 A																		
A2880	Install FRP Ducts & Supports Serving tanks 4W, 5W, 6W at GL 2- 5	14	0	24-Oct-22 A	28-Jul-23 A																	
A6100	CO16 - RCO 56 Odor Control Duct Supports	1	0	05-Dec-22 A	06-Dec-22																	
A5510	Install FRP Ducts & Supports Serving tanks 4W, 5W, 6W at GL P and GL 19 - 20	19	0	05-Jul-23 A	28-Jul-23 A																	
A5870	Fiberglass Duct Joints (Weather Dependent)	15	0	31-Jul-23 A	20-Oct-23																	
A2710	Remove Temp Ducting	5	0	18-Sep-23 A	29-Sep-23																	
A2890	Install FRP Duct From Fan EF22BA21 to West Basin & Infl Screen Bldg	4	0	25-Sep-23 A	29-Sep-23																	
A5520	Connect New Duct to Fan EF22BA021	1	0	29-Sep-23 A	29-Sep-23																	
A2900	Exhaust fan Ef22BA021 rebalanced to 25,920 CFM	0	0	26-Oct-23 A																		
A2570	Odor Control - Ready for Operation in 4W, 5W and 6W	0	0		27-Oct-23																	
Phase 4 Odor Control - Tanks 1W, 2W, 3W		346	0	20-Jun-22 A	27-Oct-23																	
A5790	Temp Duct in Tanks 1W, 2W, 3W	10	0	20-Jun-22 A	30-Jun-22																	
A2910	Demolish existing duct serving tanks 1W, 2W, 3W	5	0	28-Jun-22 A	30-Aug-22																	
A2920	Exhaust Fans EF22BA021 to remain in operation	0	0	28-Jun-22 A																		
A2930	Install Duct Supports serving tanks 1W, 2W, 3W at GL 19-20	7	0	24-Oct-22 A	30-Nov-22																	
A3920	Install Duct Support Serving Tanks 1W, 2W, 3W at GL 2-5	7	0	24-Oct-22 A	30-Nov-22																	
A5610	Install FRP Duct serving tanks 1W, 2W, 3W at GL 19-20	7	0	05-Jul-23 A	28-Jul-23 A																	
A5620	Install FRP Duct Serving Tanks 1W, 2W, 3W at GL 2-5	7	0	05-Jul-23 A	28-Jul-23 A																	
A5880	Fiberglass Duct Joints (Weather Dependent)	30	0	31-Jul-23 A	20-Oct-23																	
A5890	Remove Temp Ducting	10	0	18-Sep-23 A	29-Sep-23																	
A2940	Connect new ductwork serving tanks 1W, 2W, 3W at column H	2	0	19-Oct-23 A	20-Oct-23																	
A2950	West Basin FA exhaust complete - balance per M132, balance EF22BA021 to M002	3	0	23-Oct-23 A	25-Oct-23																	
A2600	Odor Control - Ready for Operation 1W, 2W, 3W	0	0		27-Oct-23																	
Removal and Replace Electrical and Lighting System		243	0	28-Mar-22 A	29-Aug-23																	
Phase 3 - Tanks 4W, 5W, 6W		243	0	28-Mar-22 A	29-Aug-23																	
A5570	Layout Electrical Work	1	0	28-Mar-22 A	01-Apr-22																	
A3250	Install Temp Power & Temp Lighting	10	0	28-Mar-22 A	14-Apr-22																	
A3270	Temp Supports under N-S conduit runs at the east and west ends of the basin	10	0	18-Apr-22 A	29-Apr-22																	

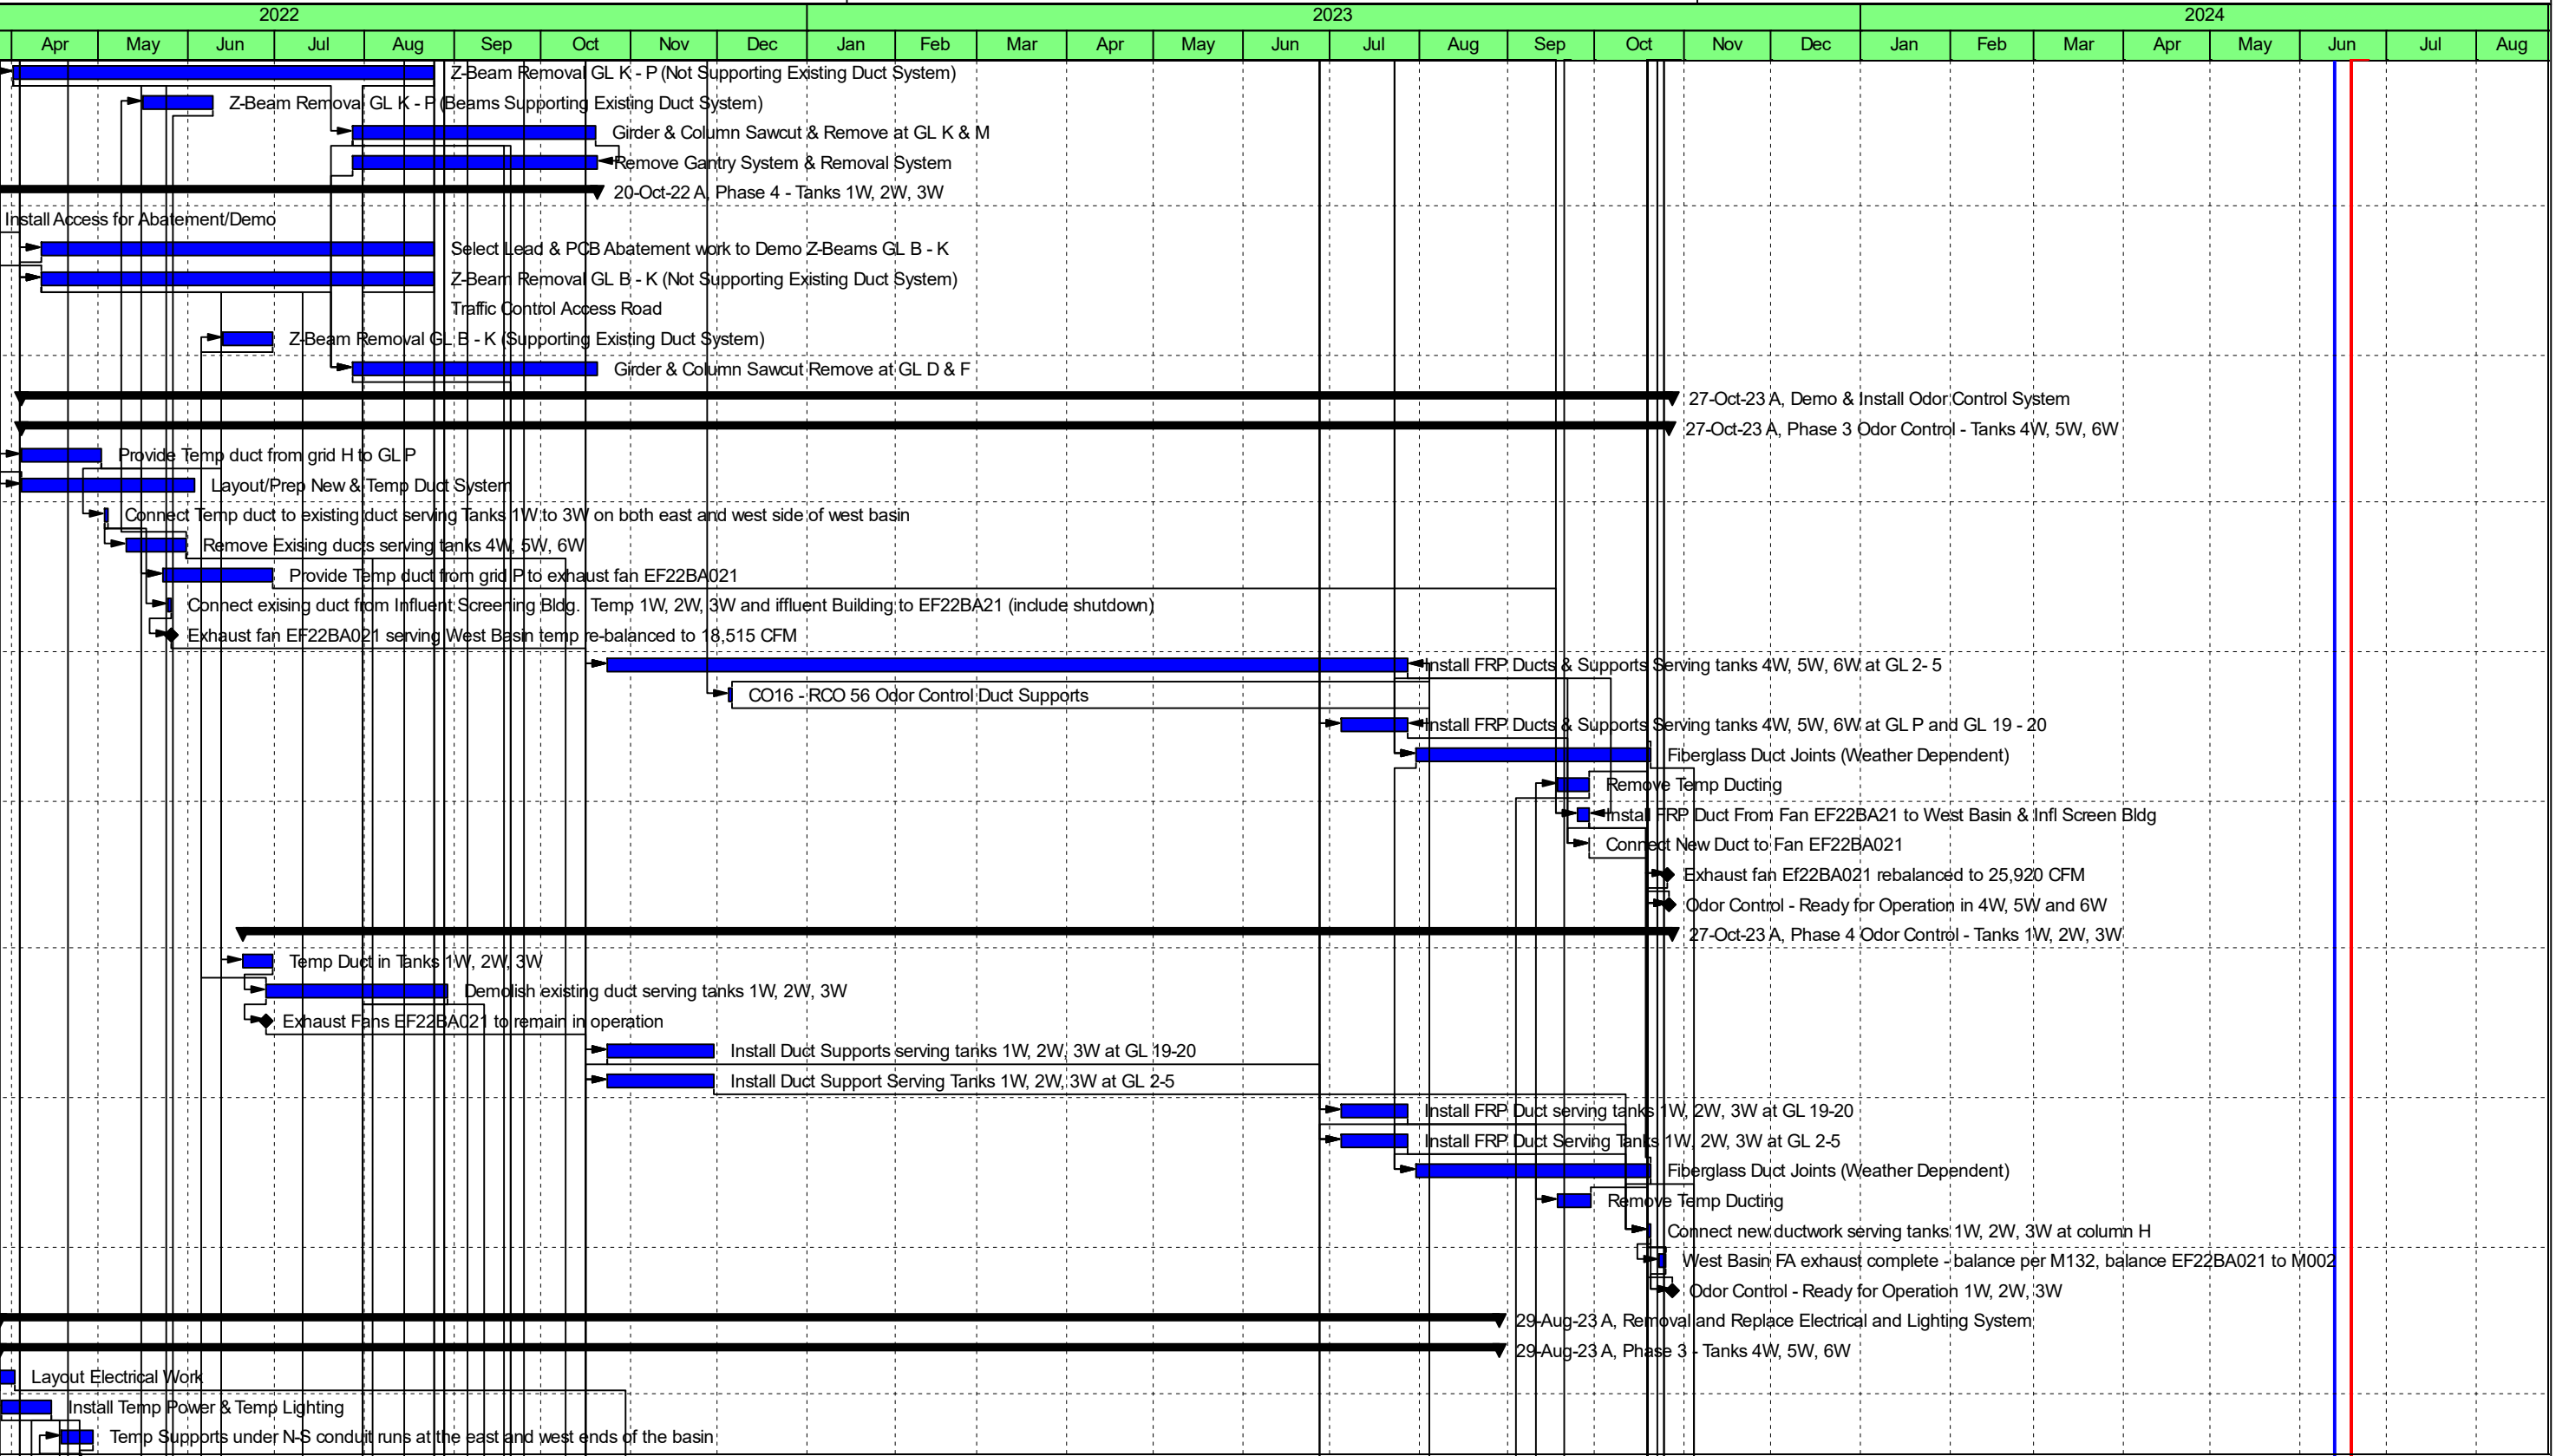


Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2021												2022		
							Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A3260	Permanent Supports for Primary E-W conduit runs	10	0	25-Apr-22 A	18-Jul-22 A																
A3280	Demolition - Start Milestone	0	0	02-May-22 A																	
A3300	Isolate Circuits, Disc. and Remove Conductors 4W, 5W, 6W	4	0	02-May-22 A	13-Jun-22																
A3290	South Quadrant - 4W to 6W (out of operation)	0	0	02-May-22 A																	
A4120	Install Ligth Poles and Conduits to	10	0	08-Jun-22 A	29-Aug-23																
A3310	Install new Conduit Chase GL 14W/15W	5	0	13-Jun-22 A	29-Sep-22																
A3320	Install Conduits at 3W/4W	5	0	13-Jun-22 A	07-Feb-23																
A3330	Remove and replace light fixtures under canopy roof	10	0	13-Jun-22 A	24-Mar-23																
A4130	Install Conduit on Support System at GL H	8	0	13-Jun-22 A	16-Feb-23																
A3490	Remove and replace wiring devices 4W, 5W, 6W	5	0	20-Jun-22 A	24-Mar-23																
A3350	Remove existing conduits no longer in use	5	0	21-Jun-22 A	28-Jun-22																
A3340	Pull new conductors and connect equipment and devices	5	0	27-Jun-22 A	16-Feb-23																
A3390	Install Skum Skimmer Motors	5	0	27-Jun-22 A	13-Jul-22 A																
A2560	WPTP - South Quadrant (4W, 5W, 6W) - Operational Testing	5	0	14-Jul-22 A	14-Jul-22 A																
A5050	Tank 4W, 5W, 6W - System Testing	1	0	14-Jul-22 A	14-Jul-22 A																
A6080	CO#16 - RCO 29 Existing .5 HP Motors	1	0	03-Oct-22 A	14-Oct-22																
A6130	CO#16 - RCO 070 Flushing Valve	1	0	07-Nov-22 A	18-Nov-22																
A6110	CO#16 - RCO 059 Electrical Receptacles for Hoist Motors	1	0	06-Feb-23 A	17-Feb-23																
Phase 4 - Tanks 1W, 2W, 3W		137	0	15-Apr-22 A	21-Jul-23 A																
A5270	Temp Power & Temp Lighting	5	0	15-Apr-22 A	21-Apr-22																
A3370	North Quadrant - Once tanks 4W to 6W are back in Service	0	0	11-Jul-22 A																	
A4140	Isolate Circuits serving equipment and devices for tanks 1W, 2W, 3W Disc. and remove c	5	0	11-Jul-22 A	05-Aug-22																
A4150	Install Conduit at gridline 14W/15W	5	0	11-Jul-22 A	09-Feb-23																
A4200	Pull new conductors and connect equipment and devices	8	0	11-Jul-22 A	09-Feb-23																
A4160	Install Conduit at 3W/4W	5	0	18-Jul-22 A	09-Feb-23																
A4190	Remove and replace wiring devices serving tanks 1W, 2W, 3W	5	0	25-Jul-22 A	24-Mar-23																
A4170	Remove and replace light fixtures under the canopy roof	10	0	01-Aug-22 A	21-Jul-23 A																
A4210	Remove existing conduits no longer in use	5	0	11-Aug-22 A	23-Aug-22																
A4180	Install Ligth Poles and Conduits to	10	0	15-Aug-22 A	24-Mar-23																
A5040	Install Skum Skimmer Motors	5	0	22-Aug-22 A	23-Sep-22																
A2590	WPTP - North Quadrant (1W, 2W, 3W) - Operational Testing	5	0	23-Sep-22 A	23-Sep-22																
A3400	Tank 1W, 2W, 3W - System Testing	1	0	23-Sep-22 A	23-Sep-22																
Other New Construction		401	0	10-Mar-22 A	27-Oct-23																
Phase 3 - Tanks 4W, 5W, 6W		399	0	10-Mar-22 A	27-Oct-23																
A4360	Demo/Removal of Existing EPDM Roofing Membrane	5	0	10-Mar-22 A	13-Oct-22																
A4050	Access For Steel/FRP Roof & Duct Support Steel Install	23	0	25-Apr-22 A	28-Apr-22																
A4000	Grout Back Z-Beam Voids (Not Z-beams Supporting Existing Duct)	8	0	23-May-22 A	29-Sep-22																
A6090	CO#16 - RCO 50 - Reclaimed Water Piping	1	0	01-Jun-22 A	01-Aug-23																
A5500	Grout Back Z-Beam Voids (Z-beams Supporting Existing Duct)	2	0	03-Jun-22 A	09-Jun-22																
A4030	Concrete Repairs per S202	2	0	13-Jun-22 A	05-Jul-22 A																
A4060	Drill & Dowel for Roof Install	6	0	11-Jul-22 A	18-Aug-22																
A4090	Install Structural Steel For Roof	5	0	25-Jul-22 A	25-Aug-22																
A6050	CO14.3 - RCO 83 Conflict w GL 14.5 Hoist	1	0	26-Jul-22 A	04-Aug-22																
A4070	Install Steel for Duct Supports at GL 19-20	4	0	08-Aug-22 A	11-Aug-22																
A4080	Canopy Roof Expansion Joint Modifications Between GL P-Q	4	0	08-Aug-22 A	07-Sep-22																
A4110	Install Steel for Duct Support at GL 2-5	5	0	11-Aug-22 A	17-Aug-22																
A6030	CO#14.1 RCO 42 - RFI 84 Sed Tank Safety Gate	1	0	01-Sep-22 A	05-Sep-22																

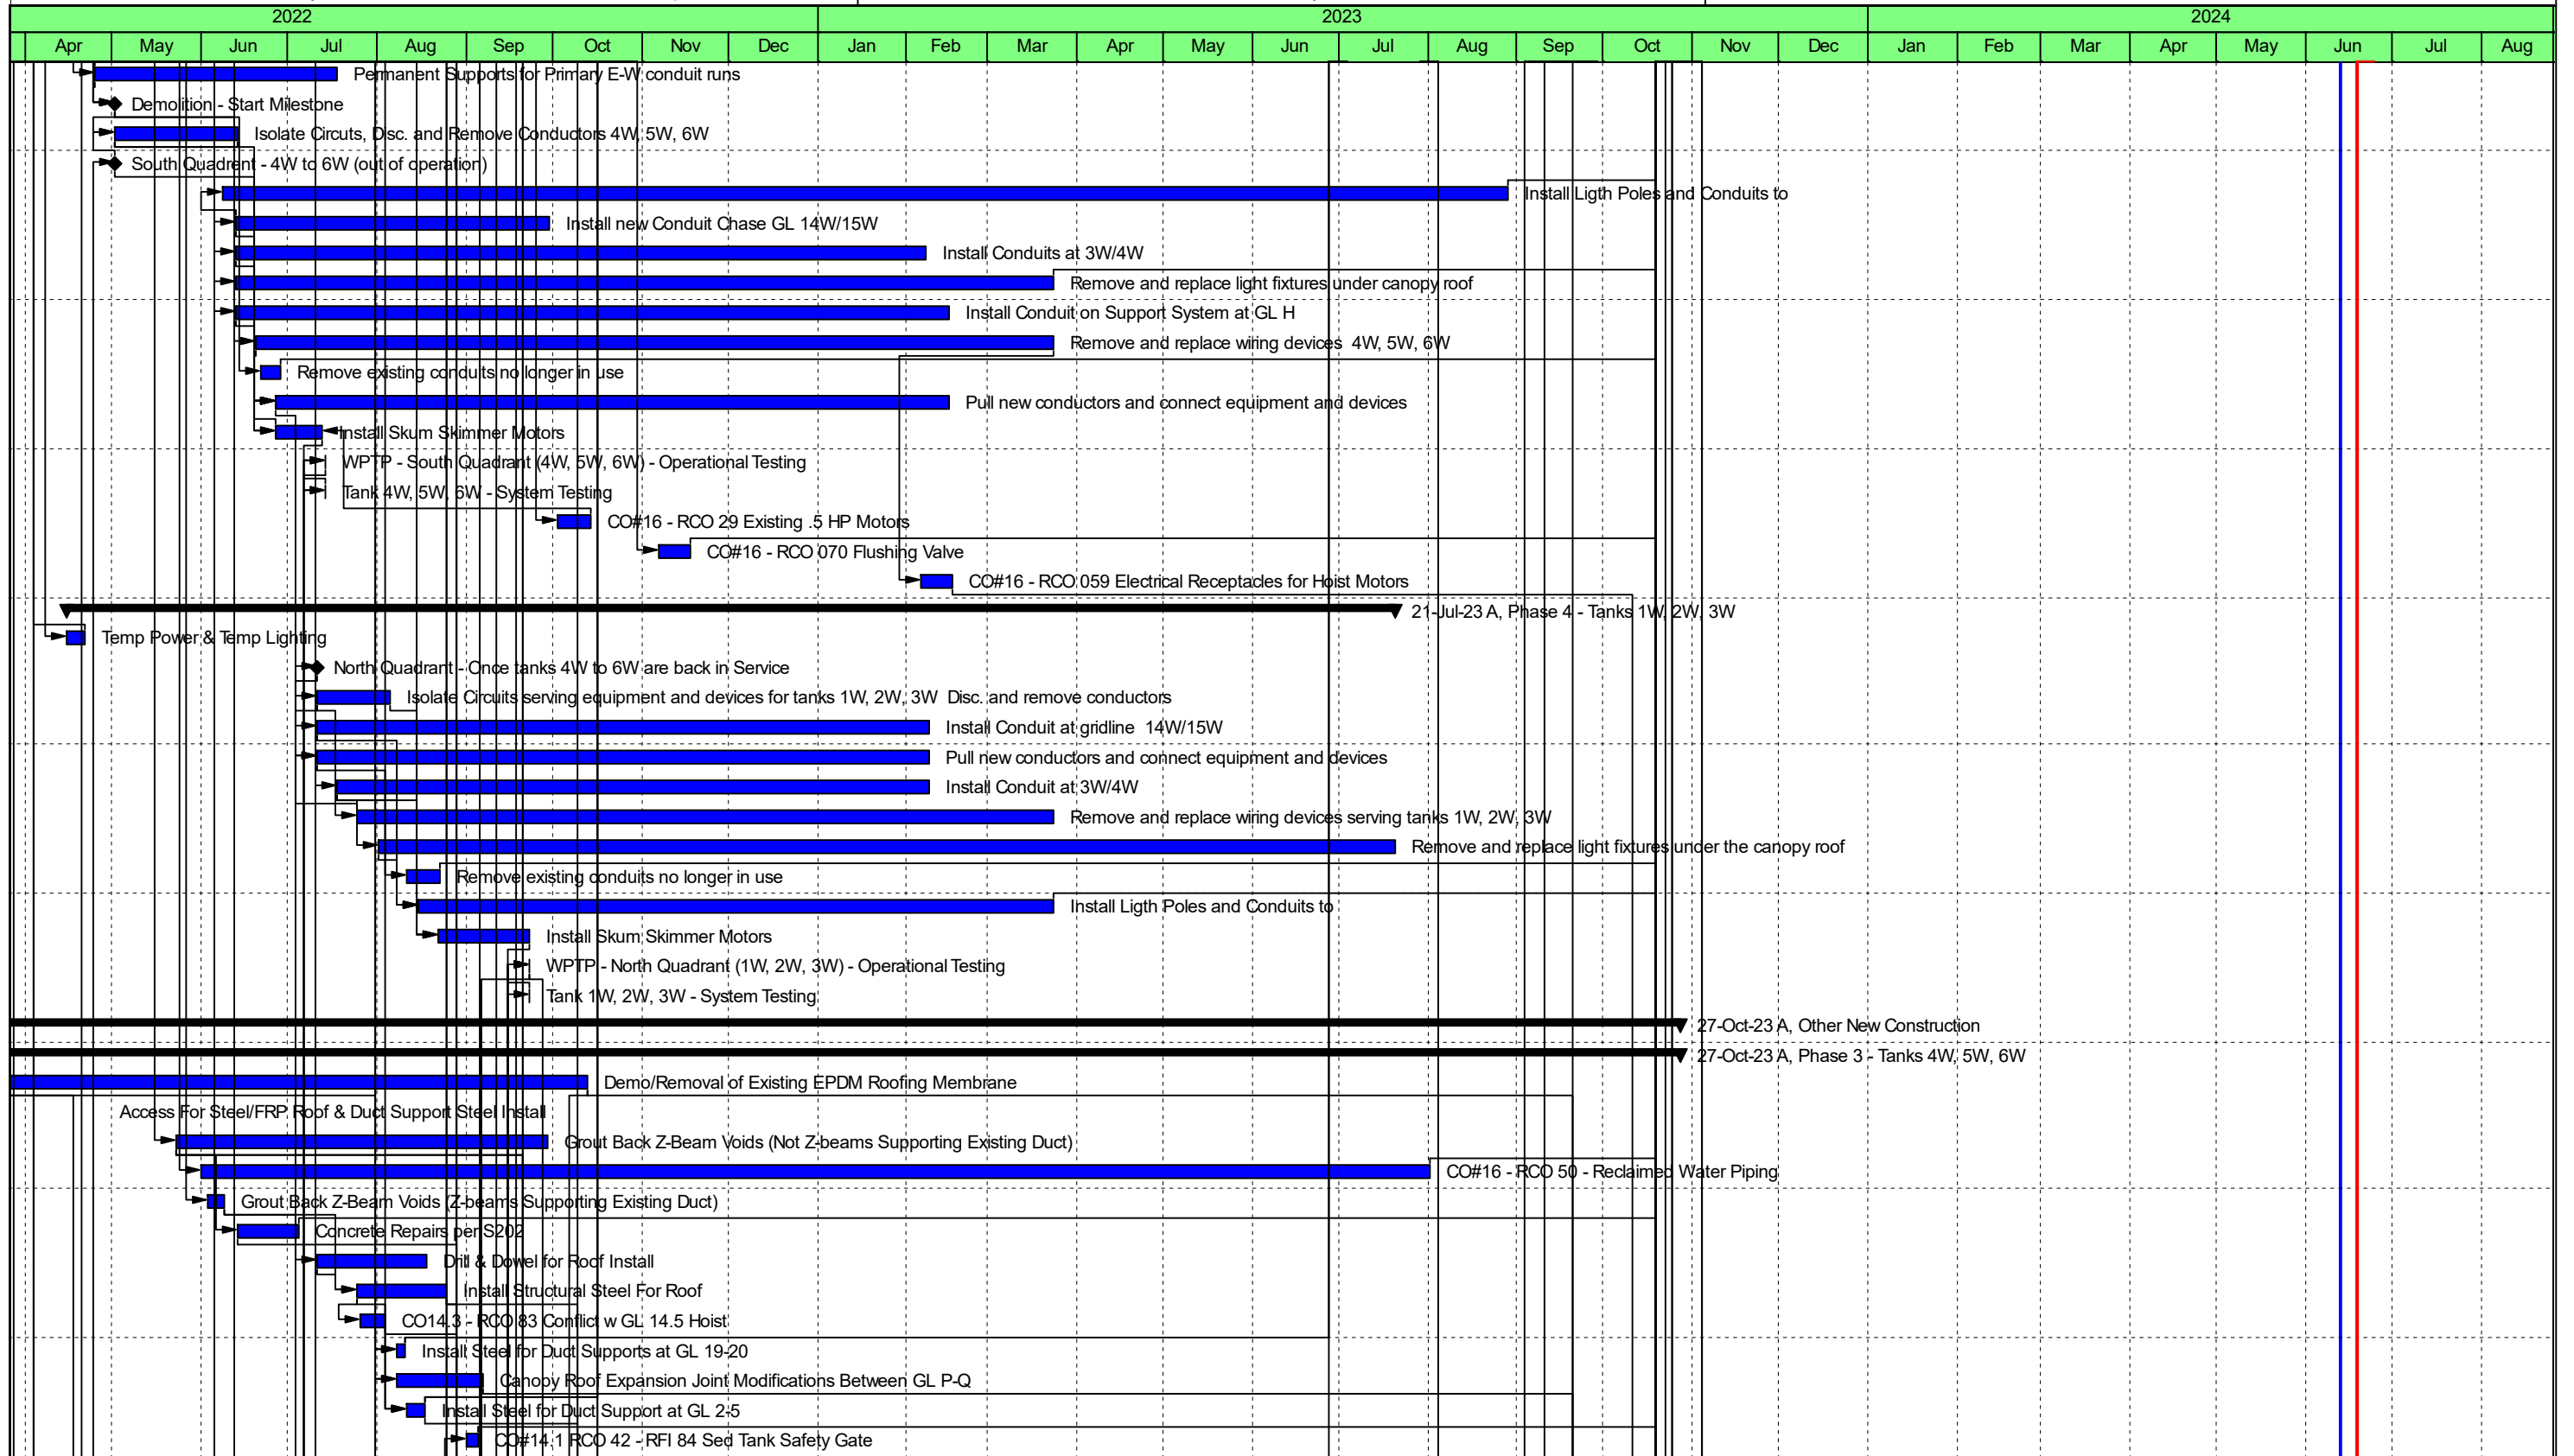

█ Actual Work
 █ Critical Remaining Work
 ▬ Summary
█ Remaining Work
 ◆ Milestone

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2021												2022		
							Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar		
A5550	Handrail & Safety Gate Mod S451	1	0	01-Sep-22 A	05-Sep-22																
A4970	Install Monorail Hoist	2	0	05-Sep-22 A	03-Oct-23																
A6140	CO#16 - RCO 082 Pipe Conflict w/ W Basin GL F3	1	0	05-Sep-22 A	08-Sep-22																
A6150	CO#16 - RCO 086 - FD 14 Concrete Spall Repair	1	0	05-Sep-22 A	09-Sep-22																
A4010	Grout Back Girder Voids	2	0	26-Sep-22 A	04-Oct-22																
A4020	Chip/Patch Columns Stubs	2	0	28-Sep-22 A	27-Oct-22																
A4040	Fill & Cap Rain Leader	2	0	28-Sep-22 A	27-Oct-22																
A6070	RCO 063 - Existing Flat Roof Membrane	10	0	14-Oct-22 A	27-Oct-22																
A4100	Install FRP Panels	3	0	17-Oct-22 A	27-Oct-22																
A6120	CO#16 - RCO 062 Stanchion Support Connection Issues	1	0	17-Oct-22 A	20-Oct-22																
A5900	Demo/Removal of EPDM Roof in Conflict with Temp Duct	10	0	11-Sep-23 A	22-Sep-23																
A5460	Install Roofing Membrane over FRP Panels (Weather Dependent)	10	0	28-Sep-23 A	27-Oct-23																
A5480	Install EPDM Membrane over Existing Flat Roof (Weather Dependent)	15	0	28-Sep-23 A	30-Sep-23																
Phase 4 - Tanks 1W, 2W, 3W		370	0	04-Apr-22 A	27-Oct-23																
A4420	Concrete Repairs per S202	2	0	04-Apr-22 A	05-Jul-22 A																
A5070	Demo/Removal of Existing EPDM Membrane	5	0	25-Apr-22 A	13-Oct-22																
A4340	Access For Steel/FRP Roof & Duct Support Steel Install	19	0	13-Jun-22 A	30-Jun-22																
A5600	Grout Back Z-Beam Voids (Z-beams Supporting Existing Duct)	2	0	13-Jun-22 A	23-Jun-22																
A4390	Grout Back Z-Beam Voids (Z-beams Not Supporting Existing Duct)	8	0	20-Jun-22 A	21-Sep-22																
A4350	Drill & Dowel for Roof Install	6	0	18-Jul-22 A	11-Aug-22																
A4400	Install Structural Steel For Roof	5	0	18-Jul-22 A	30-Aug-22																
A4460	Install Steel for Duct Support at GL 2-5	5	0	08-Aug-22 A	01-Sep-22																
A4450	Install Steel for Duct Supports at GL 19-20	5	0	08-Aug-22 A	01-Sep-22																
A5560	Handrail & Safety Gate Mod S451	1	0	05-Sep-22 A	07-Sep-22																
A4370	Canopy Roof Expansion Joint Modifications Between GL A-B	4	0	08-Sep-22 A	13-Sep-22																
A5060	Install Monorail Hoist	2	0	13-Sep-22 A	09-Oct-23																
A4440	Install FRP Panels	3	0	19-Sep-22 A	22-Sep-22																
A4470	Grout Back Girder Voids	2	0	28-Sep-22 A	06-Oct-22																
A4410	Chip/Patch Columns Stubs	2	0	28-Sep-22 A	27-Oct-22																
A4430	Fill & Cap Rain Leader	2	0	28-Sep-22 A	27-Oct-22																
A5470	Install Roofing Membrane over FRP Panels (Weather Dependent)	10	0	28-Sep-23 A	27-Oct-23																
A4380	Install EPDM Membrane over Existing Flat Roof	15	0	28-Sep-23 A	30-Sep-23																
In Tank Concrete Upgrades		191	0	11-Apr-22 A	07-Nov-22																
A5250	West Basin Prep Work Start Milestone	0	0	11-Apr-22 A																	
A2580	Tanks 4W, 5W, 6W Distribution Channel Concrete Repair Work (11/S404)	15	0	11-Apr-22 A	28-Jun-22																
A5700	Tanks 1W, 2W, 3W Distribution Channel Concrete Repair Work (11/S404)	15	0	11-Apr-22 A	08-Sep-22																
A5130	Select Removal/Tag/Store Flat Bat & Odor Control Covers for Tanks 4W, 5W, 6W	5	0	25-Apr-22 A	02-May-22																
A5140	Select Removal/Tag/Store of Handrail & Install Temp Rail at Tanks 4W, 5W, 6W	3	0	25-Apr-22 A	02-May-22																
A2450	West Basin - Constraint Start (or earlier per 011400.1.03C)	0	0	28-Apr-22 A																	
A2490	West Basin - Work Window Period	79	0	28-Apr-22 A	15-Sep-22																
A2550	Tanks 4W, 5W and 6W (South Quadrant) Concrete Repair Work	30	0	28-Apr-22 A	12-Jul-22 A																
A5150	Sanitize & Disinfect Tank 4W, 5W, 6W	2	0	28-Apr-22 A	03-May-22																
A6020	CO#13 - RCO 65 WB In-Tank Changes	1	0	29-Apr-22 A	14-Sep-22																
A5190	Select Removal/Tag/Store Flat Bat & Odor Control Covers for Tanks 1W, 2W, 3,W	3	0	20-Jun-22 A	07-Jul-22 A																
A5200	Select Removal/Tag/Store of Handrail & Install Temp Rail at Tanks 1W, 2W, 3,W	3	0	20-Jun-22 A	07-Jul-22 A																
A5930	CO#09.3 FD11 Concrete Embeds at Operating Level	1	0	23-Jun-22 A	23-Jun-22																
A5170	Re-Install Removed Odor Control Panels & Flatbar Tanks 4W, 5W, 6W	5	0	27-Jun-22 A	12-Jul-22 A																

█ Actual Work
 █ Critical Remaining Work
 ▼ Summary
█ Remaining Work
 ◆ Milestone

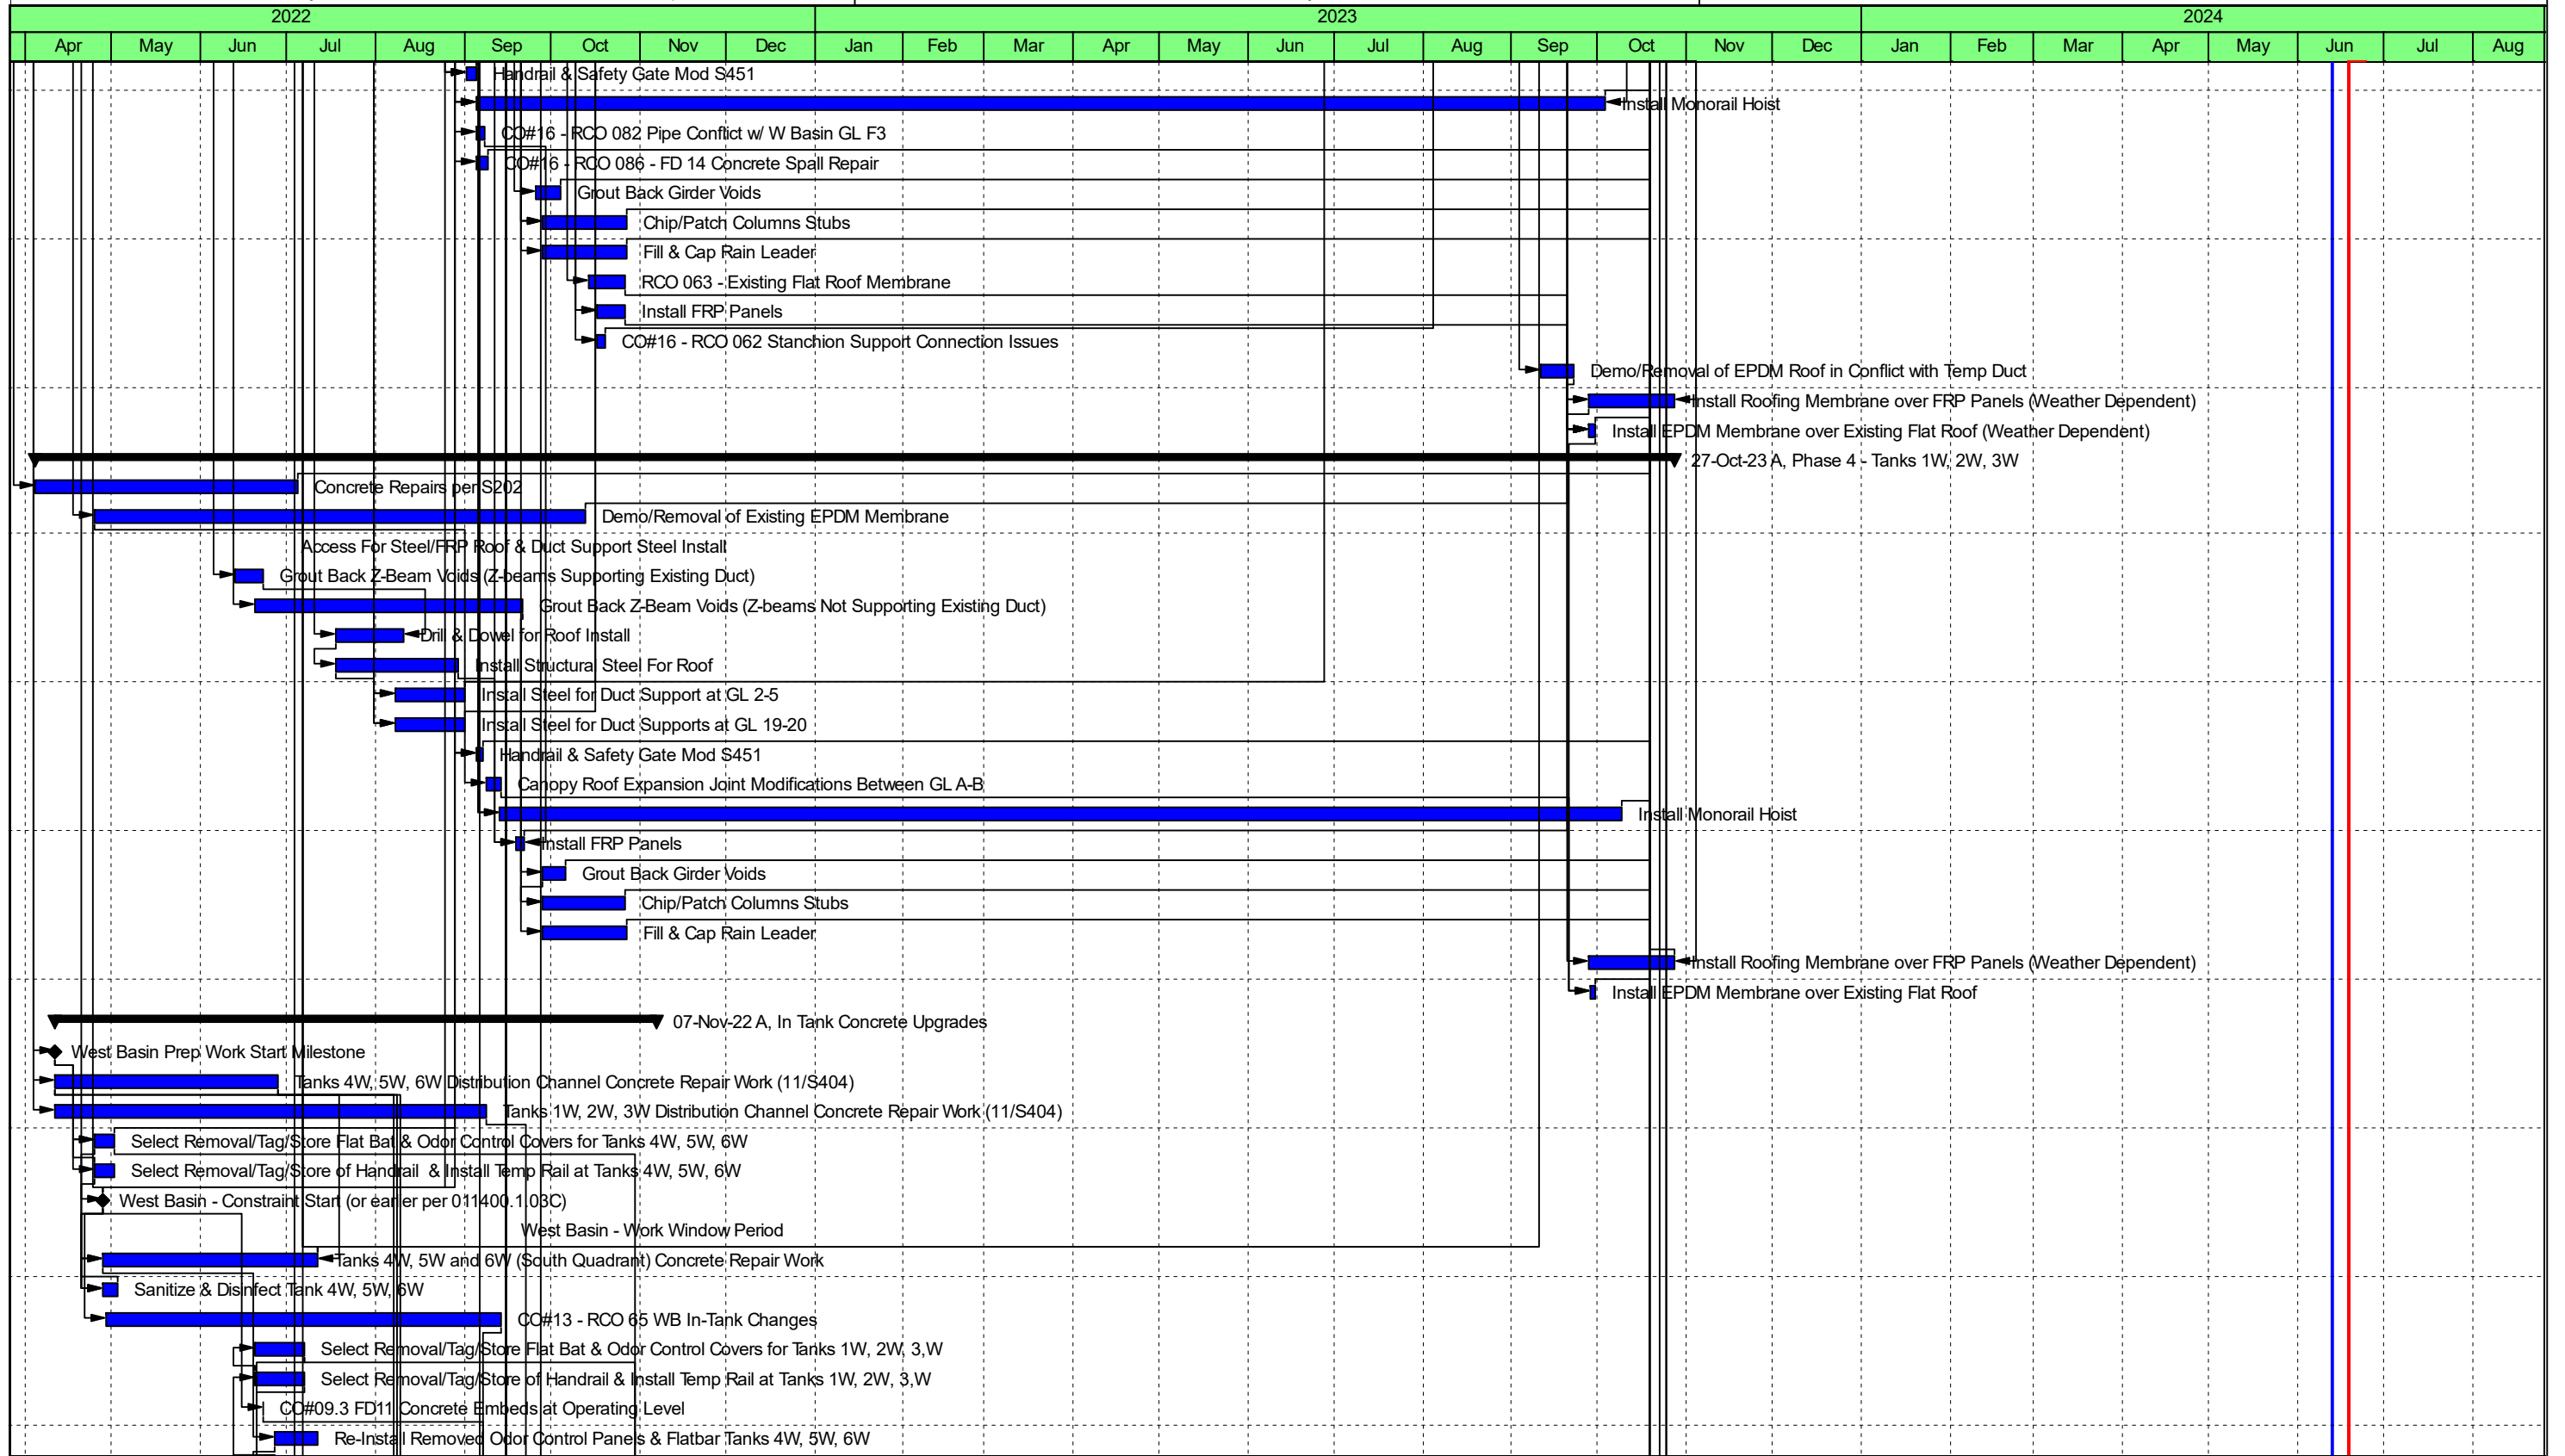

█ Actual Work
 █ Critical Remaining Work
 ▶ Summary
█ Remaining Work
 ◆ Milestone

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2021												2022			
							Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar			
A5180	Re-Install Removed Handrail Tanks 4W, 5W, 6W	5	0	27-Jun-22 A	12-Jul-22 A																	
A5210	Sanitize & Disinfect Tank 1W, 2W, 3,W	2	0	28-Jun-22 A	12-Jul-22 A																	
A5410	Tanks 1W, 2W and 3W (North Quadrant) Concrete Repair Work	29	0	29-Jun-22 A	15-Sep-22																	
A3410	WPTP South Quadrant (4W, 5W, 6W) in Service	0	0		14-Jul-22 A																	
A5990	CO#12.3 - RCO 73 Shear Wall Tank Hatch Conflict	1	0	15-Aug-22 A	15-Aug-22																	
A6000	CO#12.4 - RCO 74 Scum Trough FD05 Followup	1	0	16-Aug-22 A	16-Aug-22																	
A6010	CO#12.5 - RCO 81 West Basin Dist Channel Pipe	1	0	17-Aug-22 A	17-Aug-22																	
A5230	Re-Install Removed Odor Control Panels & Flatbar Tanks 1W, 2W, 3,W	1	0	14-Sep-22 A	15-Sep-22																	
A2500	West Basin - Constraint End	0	0		15-Sep-22																	
A2610	West Basin - Emergency Shutdown (anticipated two weeks interruption)	0	0	15-Sep-22 A	15-Sep-22																	
A2620	Re-Cleaning / Sanitize	0	0	15-Sep-22 A	15-Sep-22																	
A5240	Re-Install Removed Handrail Tanks 1W, 2W, 3,W	1	0	19-Sep-22 A	20-Sep-22																	
A5160	Modifications to Odor Control Panels for Tank 4W, 5W, 6W	5	0	07-Nov-22 A	07-Nov-22																	
A5220	Modifications to Odor Control Panels for Tank 1W, 2W, 3,W	5	0	07-Nov-22 A	07-Nov-22																	
Final Closeout Activities		162	10	01-Nov-23 A	26-Jun-24	0																
A2250	Final Punch List	60	5	01-Nov-23 A	19-Jun-24	0																
A3470	Demobilization	5	5	20-Jun-24	26-Jun-24	0																

