


Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2023												2024												2025												2026																
							S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J												
22016 Yelm Water Reclamation Facility Phase 2 Upgrades Project_Update 34_June 20																																																											
Project Milestones							1121	29	16-Sep-22 A	01-Feb-27	0																																																
A3500	Adminstrative Notice to Proceed	0	0	07-Oct-22 A			◆ Adminstrative Notice to Proceed																																																				
A9850	CO 006_SJC COR 36.02 -Additional Biodryer Procurment - Approval	1	0	16-Dec-24 A	16-Dec-24		▶ CO 006_SJC COR 36.02 -Additional Biodryer Procurment - Approval																																																				
A10090	CO 007_SJC COR 040.05-Additional Biodryer Install-Approval (KWS Removed)	1	0	29-May-25 A	25-Jul-25 A																																																						
A8520	Contract Execution	0	0	16-Sep-22 A			◆ Contract Execution																																																				
A10110	FD 041-Partial Direction on Centrifuge Relocation	1	0	23-May-25 A	23-May-25																																																						
A10120	FD 041-Standby for Complete Direction from Parametrix and RFI 183 Response	5	0	23-May-25 A	16-Sep-25		▶ FD 041-Standby for Complete Direction from Parametrix and RFI 183 Response																																																				
A8740	Full Notice to Proceed with Site Construction	0	0	13-Oct-22 A			◆ Full Notice to Proceed with Site Construction																																																				
A8430	Phase 1A Completion	0	0		22-Aug-25																																																						
A8450	Phase 1B Completion	0	0		14-Apr-26 A																																																						
A5290	Phase 2A Completion	0	0		22-Aug-25		▶ Phase 2A Completion																																																				
A8460	Phase 2B Completion	0	0		24-Apr-26 A																																																						
A8440	Phase 3A Completion	0	0		14-Jan-26 A																																																						
A6390	Physical Completion-1,572 CD from Full NTP: January 31, 2027	0	0		01-Feb-27*	0																																																					
A6550	Project Closeout	20	20	22-Dec-26	18-Jan-27	9																																																					
A9150	PSE Contract Execution with City of Yelm	0	0	21-Oct-24 A			▶ PSE Contract Execution with City of Yelm																																																				
A8920	Punchlist	25	0	01-May-26 A	19-Jun-26 A		▶ Punchlist																																																				
A3510	Substantial Completion-1,537 CD from Full NTP: December 28, 2026	0	0		24-Apr-26 A		◆ Substantial Completion																																																				
Major Submittals and Procurement							911	0	10-Oct-22 A	13-Apr-26 A		▶ 13-Apr-26 A, Major Submittals and Procurement																																															
Submittal Prep							787	0	10-Oct-22 A	26-Sep-25		▶ 26-Sep-25 A, Submittal Prep																																															
A9860	Submittal Prep - CO 006_SJC COR 036.02 - Additional Biodryer (February 28, 2025)	50	0	16-Dec-24 A	24-Feb-25		▶ Submittal Prep - CO 006_SJC COR 036.02 - Additional Biodryer																																																				
A1900	Submittal Prep-Aeration Diffuser System	40	0	10-Oct-22 A	06-Dec-22		▶ Submittal Prep-Aeration Diffuser System																																																				
A1400	Submittal Prep-Aluminum Storefronts	40	0	10-Oct-22 A	09-Feb-23		▶ Submittal Prep-Aluminum Storefronts																																																				
A1600	Submittal Prep-Asphalt Paving	30	0	24-Jan-23 A	19-Apr-23 A		▶ Submittal Prep-Asphalt Paving																																																				
A1940	Submittal Prep-Biodryer	60	0	13-Jan-23 A	03-Apr-23 A		▶ Submittal Prep-Biodryer																																																				
A1700	Submittal Prep-Biodryer Boiler	40	0	10-Oct-22 A	18-Jan-23 A		▶ Submittal Prep-Biodryer Boiler																																																				
A1930	Submittal Prep-Centrifuge	50	0	24-Oct-22 A	21-Dec-22		▶ Submittal Prep-Centrifuge																																																				
A1750	Submittal Prep-Centrifuge Feed Pumps	50	0	24-Oct-22 A	21-Dec-22		▶ Submittal Prep-Centrifuge Feed Pumps																																																				
A1680	Submittal Prep-Chain Conveyors	60	0	13-Jan-23 A	03-Apr-23 A		▶ Submittal Prep-Chain Conveyors																																																				
A1760	Submittal Prep-Chemical Feed System	30	0	16-Jan-23 A	28-Feb-23		▶ Submittal Prep-Chemical Feed System																																																				
A1790	Submittal Prep-Chemical Storage Tanks	40	0	07-Nov-22 A	16-Mar-23		▶ Submittal Prep-Chemical Storage Tanks																																																				
A1350	Submittal Prep-CMU	20	0	10-Oct-22 A	29-Nov-22		▶ Submittal Prep-CMU																																																				
A1340	Submittal Prep-CMU Reinforcement	20	0	10-Oct-22 A	12-Dec-22		▶ Submittal Prep-CMU Reinforcement																																																				
A10080	Submittal Prep-CO 007_SJC COR 040.05-Additional Biodryer Install	20	0	25-Jul-25 A	15-Aug-25		▶ Submittal Prep-CO 007_SJC COR 040.05-Additional Biodryer Install																																																				
A1430	Submittal Prep-Coatings	20	0	10-Oct-22 A	24-Feb-23		▶ Submittal Prep-Coatings																																																				
A1330	Submittal Prep-Concrete Ready Mix	10	0	10-Oct-22 A	18-Oct-22 A		▶ Submittal Prep-Concrete Ready Mix																																																				
A1320	Submittal Prep-Concrete Reinforcement	20	0	10-Oct-22 A	11-Nov-22		▶ Submittal Prep-Concrete Reinforcement																																																				
A1650	Submittal Prep-Control Panels and PLC	90	0	10-Oct-22 A	25-Apr-23 A		▶ Submittal Prep-Control Panels and PLC																																																				
A1690	Submittal Prep-Cranes and Hoists	40	0	10-Oct-22 A	15-Mar-23		▶ Submittal Prep-Cranes and Hoists																																																				
A1620	Submittal Prep-Ductile Iron Pipe and Fittings	30	0	10-Oct-22 A	14-Dec-22		▶ Submittal Prep-Ductile Iron Pipe and Fittings																																																				
A1590	Submittal Prep-Earthwork Materials	15	0	10-Oct-22 A	03-Nov-22		▶ Submittal Prep-Earthwork Materials																																																				
A1450	Submittal Prep-Electrical Grounding	35	0	10-Oct-22 A	29-Nov-22		▶ Submittal Prep-Electrical Grounding																																																				
A1560	Submittal Prep-Engine Generator	20	0	10-Oct-22 A	01-Nov-22		▶ Submittal Prep-Engine Generator																																																				
A10130	Submittal Prep-FD 041 Centrifuge Relocation	15	0	16-Sep-25 A	26-Sep-25		▶ Submittal Prep-FD 041 Centrifuge Relocation																																																				
A1740	Submittal Prep-Feed Forward Pumps	20	0	10-Oct-22 A	17-Oct-22 A		▶ Submittal Prep-Feed Forward Pumps																																																				
A1580	Submittal Prep-Fire Alarm System	60	0	10-Oct-22 A	08-May-23		▶ Submittal Prep-Fire Alarm System																																																				
A1840	Submittal Prep-Grit Chamber Equipment	40	0	10-Oct-22 A	30-Nov-22		▶ Submittal Prep-Grit Chamber Equipment																																																				

		Data Date: 30-Jun-26																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2023					2024					2025					2026					27																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
							Q	N	D	J	F	M	A	M	J	J	A	S	Q	N	D	J	F	M	A	M		J	J	A	S	Q	N	D	J	F	M	A	M	J	J	A	S	Q	N	D	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
	A2600	Submittal Review/Approval-Chain Conveyors	15	0	04-Apr-23 A	20-Jul-23 A																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												

[illegible]

[illegible]

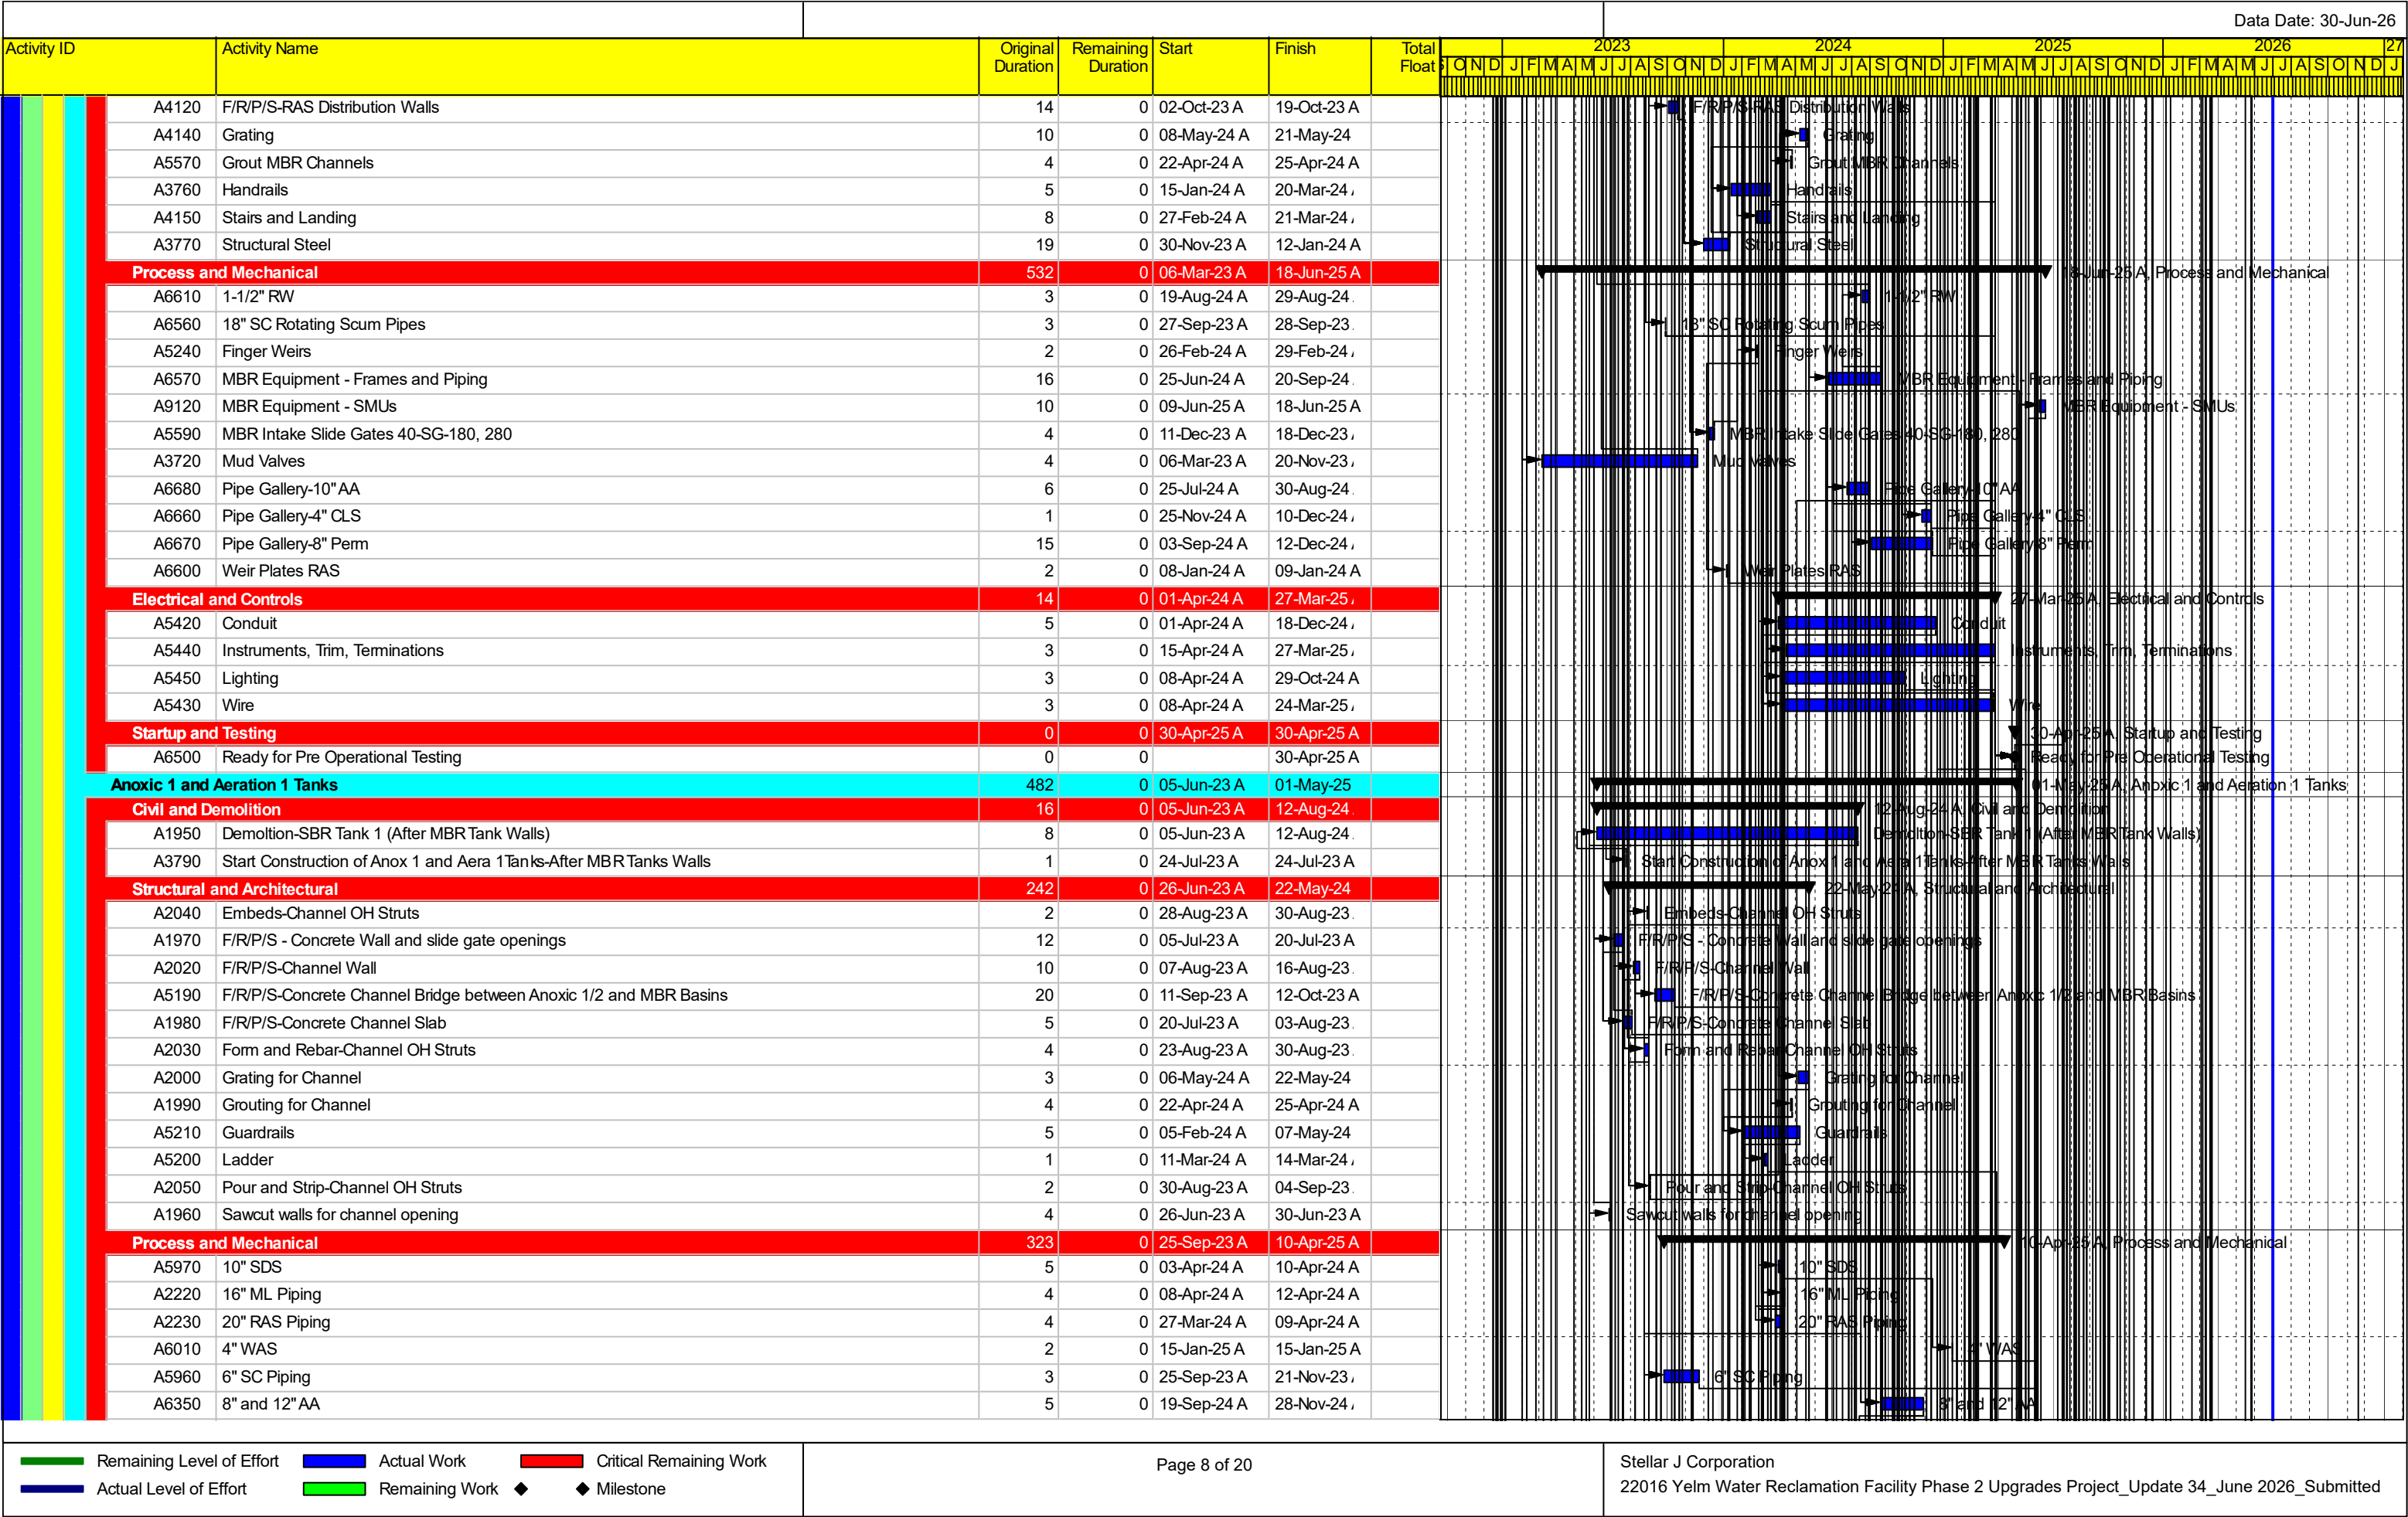

							Data Date: 30-Jun-26																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2023												2024												2025												2026												27																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
							O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
	A2190	Air Diffusers (Finish right before startup)	5	0	18-Nov-24 A	10-Apr-25 A																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																</

[illegible]

[illegible]

							Data Date: 30-Jun-26																																																
Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2023												2024												2025												2026												27
							O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J									
<																																																							

[illegible]

[illegible]

								Data Date: 30-Jun-26																											
Activity ID		Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2023				2024				2025				2026															
								Q	N	D	J	F	M	A	M	J	J	A	S	Q	N	D	J	F	M	A	M	J	J	A	S	Q	N	D	J
A10600		Delivery Lead- Mechanical/Misc Materials	40	35	23-Jun-26 A	17-Aug-26	59																												
A10510		FD 053 Received from City/PMX	0	0	05-May-26 A																														
A10710		Prepare and Submit COR 066 (Valve Vault)	10	0	06-May-26 A	21-May-26																													
A10530		Prepare and Submit COR 068 (Pump Station and Valve Vault)	10	0	06-May-26 A	02-Jun-26 A																													
Construction			95	95	11-Aug-26	21-Dec-26	9																												
A10610		Electrical Install - Conduit Equipment	10	10	13-Oct-26	26-Oct-26	29																												
A10790		Electrical Install - Wiring	10	10	17-Nov-26	30-Nov-26	14																												
A10630		Install Pump Skid	15	15	27-Oct-26	16-Nov-26	9																												
A10700		Install Vault and Check Valve	15	15	11-Aug-26	31-Aug-26	49																												
A10650		Mechanical Install	15	15	17-Nov-26	07-Dec-26	9																												
A10670		Startup and Testing	10	10	08-Dec-26	21-Dec-26	9																												
Construction - Schedule B Solids Handling			878	0	08-Feb-23 A	29-May-26																													
Phase 1B Construction			865	0	08-Feb-23 A	29-May-26																													
Site Improvements			10	0	23-Nov-23 A	27-Nov-23 ,																													
A7570		Septage Pump Station Valve Vault	10	0	23-Nov-23 A	27-Nov-23 ,																													
Septage Receiving Station Area			741	0	14-Mar-23 A	14-Jan-26 A																													
Civil and Demolition			375	0	14-Mar-23 A	31-Jul-24 A																													
A8290		4" D Underground from septage receiving	3	0	02-May-23 A	03-May-23																													
A8300		6" SDS from Storage Tank	5	0	12-Apr-23 A	12-Apr-23 A																													
A7670		Backfill-Septage Pump Station	2	0	03-Apr-23 A	03-Apr-23 A																													
A7660		Backfill-Septage Storage Tank	2	0	25-Apr-23 A	26-Apr-23 A																													
A7680		Concrete Pathway	4	0	09-Jul-24 A	31-Jul-24 A																													
A7740		Connections to yard piping	5	0	04-Apr-23 A	04-Apr-23 A																													
A7550		Demolition	10	0	16-Mar-23 A	16-Mar-23 ,																													
A7730		Excavation and Base Rock-Septage Area Equipment Concrete Equipment Pad	5	0	05-Jun-23 A	08-Jun-23 A																													
A7640		Excavation and Base Rock-Septage Pump Station	5	0	20-Mar-23 A	23-Mar-23 ,																													
A7630		Excavation and Base Rock-Septage Storage Tank	3	0	17-Apr-23 A	20-Apr-23 A																													
A8050		FD 007 Septage Wet Well Waterproofing	1	0	23-Mar-23 A	28-Mar-23 ,																													
A7610		Install Septage Storage Tank	3	0	25-Apr-23 A	25-Apr-23 A																													
A7650		Set Precast-Septage Pump Station	3	0	29-Mar-23 A	29-Mar-23 ,																													
A7580		Temp Erosion Control	3	0	14-Mar-23 A	15-Mar-23 ,																													
A7590		Yard Piping-SEP Forcemain to plant drain PS	10	0	01-Apr-24 A	10-Apr-24 A																													
Structural and Architectural			247	0	15-Jun-23 A	14-May-24																													
A7780		F/R/P/S-Housekeeping Pads and electrical panel Slab	5	0	13-May-24 A	14-May-24																													
A7600		F/R/P/S-Septage Area Concrete Equipment Pad	5	0	15-Jun-23 A	21-Jun-23 A																													
Process and Mechanical			262	0	14-Aug-23 A	14-Jan-26 A																													
A7690		Install Septage Receiving Station Equipment	1	0	14-Aug-23 A	08-Aug-24																													
A7620		Interior Piping and supports-Pump Station	3	0	15-Apr-24 A	20-May-24																													
A8310		Piping-Septage Receiving Equipment	5	0	23-Oct-24 A	05-Dec-24 ,																													
A8280		Submersible Pumps and guiderails-Septage Receiving Pump Station	3	0	10-Apr-24 A	14-Jan-26 A																													
Electrical and Controls			572	0	12-Apr-23 A	12-Sep-25																													
A8330		Conduit	5	0	08-Aug-23 A	22-Nov-24 ,																													
A8390		Electrical Demo-Existing RV Dump Station	2	0	12-Apr-23 A	14-Apr-23 A																													
A8350		Instruments, Trim, Terminations	3	0	08-Sep-25 A	12-Sep-25																													
A8360		Lighting	2	0	22-Oct-24 A	23-Oct-24 A																													
A8320		Panels/Service Equipment	5	0	20-Nov-24 A	22-Nov-24 ,																													
A8340		Wire	3	0	01-Sep-25 A	04-Sep-25																													
Startup and Testing			0	0	14-Jan-26 A	14-Jan-26 A																													
A7700		Ready for Startup	0	0		14-Jan-26 A																													

Remaining Level of Effort

Actual Work

Critical Remaining Work

Actual Level of Effort

Remaining Work

◆

 Milestone

◆

 Milestone

Page 17 of 20

Stellar J Corporation
22016 Yelm Water Reclamation Facility Phase 2 Upgrades Project_Update 34_June 2026_Submitted

										Data Date: 30-Jun-26																																														
Activity ID		Activity Name		Original Duration	Remaining Duration	Start	Finish	Total Float	2023												2024												2025												2026											
									Q	N	D	J	F	M	A	M	J	J	A	S	Q	N	D	J	F	M	A	M	J	J	A	S	Q	N	D	J	F	M	A	M	J	J	A	S	Q	N	D	J								
	A7800	Metal Siding	5	0	15-Apr-26 A	16-Apr-26 A																																																		
	A7790	Metal Stud Framing (Hold Per City Direction)	10	0	13-Jan-26 A	14-Jan-26 A																																																		
	A9840	Relocate Eco Blocks (Per RFI 141Rev)	4	0	24-Mar-25 A	26-Mar-25 ,																																																		
	A7810	Wall opening for conveyor	1	0	12-Feb-25 A	18-Feb-25 ,																																																		
Process and Mechanical			2	0	03-Nov-25 A	04-Nov-25 ,																																																		
A8030	Install Solids handling Air compressor	2	0	03-Nov-25 A	04-Nov-25 ,																																																			
Startup and Testing			0	0	14-Jan-26 A	14-Jan-26 A																																																		
A8910	Ready for Startup	0	0		14-Jan-26 A																																																			
Centrifuge Feed Pump Station			676	0	03-Oct-23 A	29-May-26																																																		
Civil and Demolition			571	0	03-Oct-23 A	19-Feb-26 ,																																																		
A1020	4" WAS Piping - RFI 179 (Perform at 2B Startup)	5	0	01-Dec-25 A	19-Feb-26 ,																																																			
A1000	Excavation	3	0	03-Oct-23 A	19-Oct-23 A																																																			
A1010	Foundation Rock	2	0	18-Oct-23 A	19-Oct-23 A																																																			
A4950	Start Centrifuge Feed Pump Station after Biodryer foundation slab	1	0	03-Oct-23 A	03-Oct-23 A																																																			
A1270	Underslab Electrical	2	0	23-Oct-23 A	24-Oct-23 A																																																			
A1260	Underslab Piping	2	0	17-Oct-23 A	18-Oct-23 A																																																			
Structural and Architectural			653	0	23-Oct-23 A	29-May-26																																																		
A3810	Coatings - Architectural	3	0	18-Nov-24 A	20-Nov-24 ,																																																			
A9770	Coatings - Piping	2	0	01-May-26 A	29-May-26																																																			
A1060	F/R/P/S - Equipment Pads	3	0	26-Feb-24 A	06-Mar-24 ,																																																			
A1030	F/R/P/S - Foundation Slab	4	0	23-Oct-23 A	01-Nov-23 ,																																																			
A1050	F/R/P/S - Stairs	3	0	18-Dec-23 A	20-Dec-23 ,																																																			
A1040	F/R/P/S - Walls	12	0	16-Nov-23 A	21-Nov-23 ,																																																			
A1190	Grating	2	0	11-Aug-25 A	13-Aug-25																																																			
A1140	Gypsum Board-Type X	8	0	24-Jul-24 A	06-Aug-24																																																			
A1080	Insulation	4	0	25-Apr-24 A	29-Apr-24 A																																																			
A1130	Louver	2	0	19-Aug-24 A	22-Aug-24																																																			
A1090	Metal Roofing	8	0	19-Mar-24 A	01-Apr-24 A																																																			
A1120	Railings	3	0	23-May-24 A	28-May-24																																																			
A1070	Roof Framing and Sheathing	5	0	21-Dec-23 A	18-Jan-24 A																																																			
A1100	Skylights	2	0	22-Apr-24 A	23-Apr-24 A																																																			
A1110	Stud Wall Framing and Sheathing	5	0	18-Dec-23 A	21-Dec-23 ,																																																			
Process			242	0	20-Jun-24 A	08-Jul-25 A																																																		
A1170	1-1/2" PD -	2	0	08-Jul-25 A	08-Jul-25 A																																																			
A1160	4" WAS Piping and Valving	3	0	25-Jun-24 A	04-Jul-25 A																																																			
A1150	Centrifuge Feed Pumps 90-P-150, 151	2	0	20-Jun-24 A	24-Jun-24 A																																																			
A1180	Centrifuge Sump Pump - 90-P-152 (RFI 147 Response)	1	0	08-Jul-25 A	08-Jul-25 A																																																			
A1200	HVAC	2	0	14-Oct-24 A	18-Oct-24 A																																																			
Electrical and Controls			202	0	21-Oct-24 A	17-Jul-25 A																																																		
A1220	Conduit	3	0	21-Oct-24 A	30-Oct-24 A																																																			
A1250	Grounding	2	0	15-Jul-25 A	17-Jul-25 A																																																			
A1240	Instruments, Trim, Terminations	3	0	09-Jul-25 A	14-Jul-25 A																																																			
A1210	Panels/Service Equipment	2	0	28-Oct-24 A	29-Oct-24 A																																																			
A1230	Wire	2	0	07-Jul-25 A	08-Jul-25 A																																																			
Startup and Testing			0	0	19-Feb-26 A	19-Feb-26 ,																																																		
A4970	Ready for Startup	0	0		19-Feb-26 ,																																																			
Phase 2B Construction			229	0	03-Feb-25 A	08-May-26																																																		
Solids Handling Facility-New Centrifuge Room			229	0	03-Feb-25 A	07-May-26																																																		
Civil and Demolition			189	0	22-Aug-25 A	07-May-26																																																		
A7520	Demo Gravity Belt Press, Sludge Pump Station, supports, stairs	12	0	22-Apr-26 A	07-May-26																																																			

Remaining Level of Effort

Actual Work

Critical Remaining Work

Actual Level of Effort

Remaining Work

◆

◆ Milestone

Page 19 of 20

Stellar J Corporation
22016 Yelm Water Reclamation Facility Phase 2 Upgrades Project_Update 34_June 2026_Submitted

