


Activity Name	Start	Original Duration	Remaining Duration	Finish	Total Float	Predecessors	Successors	Calendar	Calendar															
									Tr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	2025							
									F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M
SPU PS 62, 63, 71 Improvements - Update 2024-01-25	01/19/23 A	521d	264d	02/05/25	0d																			
Milestones	01/19/23 A	342d	38d	02/05/25	0d																			
Contract Execution	01/19/23 A	0d	0d			A1130, A'		Standard w/ Basic Holidays	Contract Execution															
Notice to Proceed	10/10/23 A	0d	0d			A2020	A2570, A'	Standard w/ Basic Holidays	Notice to Proceed															
SJC Anticipated Substantial Completion	12/11/24	1d	1d	12/12/24	28d	A3620, A'	A3430	SPU 4x10 Schedule	SJC															
Contract Physical Completion		0d	0d	02/05/25*	0d	A1760, A		SPU 4x10 Schedule																
Procurement	01/19/23 A	400d	183d	10/10/24	27d			Standard w/ Basic Holidays	10/10/24, Proc															
Submittals	01/19/23 A	332d	75d	05/08/24	135d			Standard w/ Basic Holidays	05/08/24, Submittals															
Submittal Prep	01/19/23 A	277d	60d	04/17/24	135d			Standard w/ Basic Holidays	04/17/24, Submittal Prep															
05 12 00 - Structural & Misc Steel - Prep & Submit	01/19/23 A	77d	0d	05/03/23 A		A2020	A1770	Standard w/ Basic Holidays	05 12 00 - Structural & Misc Steel - Prep & Submit															
05 50 00 - Metal Grating - Prep & Submit PS 63	01/19/23 A	122d	0d	05/08/23 A		A2020	A1780	Standard w/ Basic Holidays	05 50 00 - Metal Grating - Prep & Submit PS 63															
09 90 00 - Painting & Coatings - Prep & Submit	01/19/23 A	127d	0d	06/02/23 A		A2020	A1790	Standard w/ Basic Holidays	09 90 00 - Painting & Coatings - Prep & Submit															
23 00 00 - Ventilation Fans - Prep & Submit	01/19/23 A	96d	0d	04/14/23 A		A2020	A1800	Standard w/ Basic Holidays	23 00 00 - Ventilation Fans - Prep & Submit															
23 00 00 - Ventilation Enclosures - Prep & Submit PS 62 & 63	01/19/23 A	127d	0d	07/14/23 A		A2020	A1810	Standard w/ Basic Holidays	23 00 00 - Ventilation Enclosures - Prep & Submit PS 62 & 63															
23 80 00 - Odor Control Equipment	01/19/23 A	60d	0d	04/13/23 A		A2020	A1820	Standard w/ Basic Holidays	23 80 00 - Odor Control Equipment															
26 24 19 - Motor Control Centers - Prep & Submit	01/19/23 A	108d	0d	06/20/23 A		A2020	A1840	Standard w/ Basic Holidays	26 24 19 - Motor Control Centers - Prep & Submit															
26 29 13 - Combination Motor Starter - Prep & Submit	01/19/23 A	75d	0d	05/04/23 A		A2020	A1850	Standard w/ Basic Holidays	26 29 13 - Combination Motor Starter - Prep & Submit															
31 23 19 - Dewatering Plan - Prep & Submit	01/19/23 A	60d	0d	11/21/23 A		A2020	A1860	Standard w/ Basic Holidays	31 23 19 - Dewatering Plan - Prep & Submit															
Div 31 - Landscape Materials - Prep & Submit	01/19/23 A	60d	60d	04/17/24	135d	A2020	A1870	Standard w/ Basic Holidays	Div 31 - Landscape Materials - Prep & Submit															
40 05 08 - Stainless Steel Slide Gates Prep & Submit	01/19/23 A	60d	0d	04/13/23 A		A2020	A1900	Standard w/ Basic Holidays	40 05 08 - Stainless Steel Slide Gates Prep & Submit															
40 05 15 Pipe Supports- Prep & Submit PS63	01/19/23 A	50d	0d	03/30/23 A		A2020	A1910	Standard w/ Basic Holidays	40 05 15 Pipe Supports- Prep & Submit PS63															
40 23 00 - Process Pipe, Fittings, & Accessories	01/19/23 A	45d	0d	03/23/23 A		A2020	A1920	Standard w/ Basic Holidays	40 23 00 - Process Pipe, Fittings, & Accessories															
43 21 13 - Vert Centrifugal Non-Clog Sewage Pumps - Prep & Submit	01/19/23 A	52d	0d	04/03/23 A		A2020	A1960	Standard w/ Basic Holidays	43 21 13 - Vert Centrifugal Non-Clog Sewage Pumps - Prep & Submit															
43 21 39 - Sump Pumps	01/19/23 A	67d	0d	04/24/23 A		A2020	A1970	Standard w/ Basic Holidays	43 21 39 - Sump Pumps															
01 57 13 - Construction Stormwater & Erosion Control Plan	01/19/23 A	65d	0d	04/21/23 A		A2020	A1980	Standard w/ Basic Holidays	01 57 13 - Construction Stormwater & Erosion Control Plan															
00 31 00 - Site Security Plan	01/19/23 A	65d	0d	04/20/23 A		A2020	A1990	Standard w/ Basic Holidays	00 31 00 - Site Security Plan															
01 57 13 - Tree, Vegetation, and Soil Protection Plan	01/19/23 A	55d	0d	04/06/23 A		A2020	A2000	Standard w/ Basic Holidays	01 57 13 - Tree, Vegetation, and Soil Protection Plan															
01 57 13 - Spill Plan	01/19/23 A	55d	0d	04/06/23 A		A2020	A2010	Standard w/ Basic Holidays	01 57 13 - Spill Plan															
26 24 00 - Panelboards - Prep & Submit	01/19/23 A	70d	0d	04/27/23 A		A2020	A3250	Standard w/ Basic Holidays	26 24 00 - Panelboards - Prep & Submit															
26 50 00 Lighting - Prep & Submit	01/19/23 A	80d	0d	05/11/23 A		A2020	A3270	Standard w/ Basic Holidays	26 50 00 Lighting - Prep & Submit															
05 50 00 - Metal Grating - Prep & Submit PS 62 & 71	01/19/23 A	80d	0d	01/25/24	29d	A2020	A3400	Standard w/ Basic Holidays	05 50 00 - Metal Grating - Prep & Submit PS 62 & 71															
26 05 00 EV Charging Station	01/19/23 A	59d	0d	04/13/23 A		A2020	A3490	Standard w/ Basic Holidays	26 05 00 EV Charging Station															
23 00 00 - Ventilation Enclosures - Prep & Submit PS 21	01/30/23 A	80d	30d	03/06/24	97d	A2020	A3380	Standard w/ Basic Holidays	23 00 00 - Ventilation Enclosures - Prep & Submit PS 21															
40 05 15 Pipe Supports- Prep & Submit PS62 & PS71	01/30/23 A	215d	5d	01/31/24	18d	A2020	A3390	Standard w/ Basic Holidays	40 05 15 Pipe Supports- Prep & Submit PS62 & PS71															
Div 26 - Electrical Materials - Prep & Submit	03/13/23 A	1d	0d	03/13/23 A		A2020	A1830	Standard w/ Basic Holidays	Div 26 - Electrical Materials - Prep & Submit															
40 23 01 - Pump Station Valves - Prep & Submit	03/21/23 A	1d	0d	03/21/23 A		A2020	A1930	Standard w/ Basic Holidays	40 23 01 - Pump Station Valves - Prep & Submit															
Div 40 - Instrumentation - Prep & Submit	04/13/23 A	1d	0d	04/13/23 A		A2020	A1940	Standard w/ Basic Holidays	Div 40 - Instrumentation - Prep & Submit															
32 31 13/32 31 19 Fencing - Prep & Submit	06/19/23 A	6d	0d	11/10/23 A		A2020	A1880	Standard w/ Basic Holidays	32 31 13/32 31 19 Fencing - Prep & Submit															
33 05 16 - Utility Structure - Prep & Submit	06/19/23 A	40d	0d	11/21/23 A		A2020	A1890	Standard w/ Basic Holidays	33 05 16 - Utility Structure - Prep & Submit															
41 22 13 - Cranes & Hoist - Prep & Submit	06/19/23 A	40d	40d	03/20/24	56d	A2020	A1950	Standard w/ Basic Holidays	41 22 13 - Cranes & Hoist - Prep & Submit															
01 75 00 - Commishioning & Startup Plan - Prep & Submit	01/25/24	20d	20d	02/21/24	8d	A2780	A3560	Standard w/ Basic Holidays	01 75 00 - Commishioning & Startup Plan - Prep & Submit															
Submittal Review & Approval	03/13/23 A	296d	75d	05/08/24	135d			Standard w/ Basic Holidays	05/08/24, Submittal Review & Approval															
Div 26 - Electrical Materials Review & Approved	03/13/23 A	132d	0d	09/14/23 A		A1190	A3240	Standard w/ Basic Holidays	Div 26 - Electrical Materials Review & Approved															
40 23 01 - Pump Station Valves - Review & Approved	03/21/23 A	15d	0d	05/01/23 A		A1290	A3200	Standard w/ Basic Holidays	40 23 01 - Pump Station Valves - Review & Approved															
40 23 00 - Process Pipe, Fittings, & Accessories - Review & Approved	03/23/23 A	15d	0d	04/12/23 A		A1280	A3190	Standard w/ Basic Holidays	40 23 00 - Process Pipe, Fittings, & Accessories - Review & Approved															
40 05 15 Pipe Supports - Review & Approved PS 63	03/30/23 A	87d	0d	07/31/23 A		A1270	A3180	Standard w/ Basic Holidays	40 05 15 Pipe Supports - Review & Approved PS 63															
43 21 13 - Vert Centrifugal Non-Clog Sewage Pumps - Review & Approved	04/03/23 A	30d	0d	05/03/23 A		A1320	A3210	Standard w/ Basic Holidays	43 21 13 - Vert Centrifugal Non-Clog Sewage Pumps - Review & Approved															

█ Remaining Level of Effort
 █ Actual Work
 █ Critical Remaining Work
█ Actual Level of Effort
 █ Remaining Work
 ◆ Milestone

Activity Name	Start	Original Duration	Remaining Duration	Finish	Total Float	Predecessor	Successors	Calendar	02/01/24 09:42															
									Calendar															
									Tr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	2025							
	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	Jan
01 57 13 - Tree, Vegetation, and Soil Protection Plan - Review & Approved	04/06/23 A	8d	0d	04/14/23 A		A1360	A2580, A:	Standard w/ Basic Holidays																
01 57 13 - Spill Plan - Review & Approved	04/06/23 A	24d	0d	05/08/23 A		A1370	A2570	Standard w/ Basic Holidays																
26 05 00 - EV Charing Station - Review & Approved	04/12/23 A	15d	0d	05/02/23 A		A3480	A3510	Standard w/ Basic Holidays																
23 80 00 - Odor Control Equipment - Review & Approved	04/13/23 A	18d	0d	05/08/23 A		A1180	A3140	Standard w/ Basic Holidays																
40 05 08 - Stainless Steel Slide Gates - Review & Approved	04/13/23 A	87d	0d	08/14/23 A		A1260	A3170	Standard w/ Basic Holidays																
Div 40 - Instrumentation - Review & Approved	04/13/23 A	97d	0d	08/28/23 A		A1300	A3300	Standard w/ Basic Holidays																
23 00 00 - Ventilation Fans - Review & Approved	04/14/23 A	36d	0d	06/02/23 A		A1160	A3120	Standard w/ Basic Holidays																
00 31 00 - Site Security Plan - Review & Approved	04/20/23 A	50d	0d	06/28/23 A		A1350	A2570	Standard w/ Basic Holidays																
01 57 13 - Construction Stormwater & Erosion Control Plan - Review & Approved	04/21/23 A	1d	0d	04/21/23 A		A1340	A2580, A:	Standard w/ Basic Holidays																
43 21 39 - Sump Pumps - Review & Approved	04/24/23 A	7d	0d	05/02/23 A		A1330	A3470	Standard w/ Basic Holidays																
26 24 00 - Panelboards - Review & Approve	04/27/23 A	27d	0d	06/02/23 A		A3110	A3260	Standard w/ Basic Holidays																
05 12 00 - Structural & Misc Steel - Review & Approved	05/03/23 A	4d	0d	05/08/23 A		A1130	A3220	Standard w/ Basic Holidays																
26 29 13 - Combination Motor Starter - Review & Approved	05/04/23 A	64d	0d	08/02/23 A		A1210	A3160	Standard w/ Basic Holidays																
05 50 00 - Metal Grating - Review & Approved PS 63	05/08/23 A	46d	0d	07/11/23 A		A1140	A3230	Standard w/ Basic Holidays																
26 50 00 Lighting - Review & Approved	05/11/23 A	5d	0d	05/17/23 A		A3280	A3290	Standard w/ Basic Holidays																
09 90 00 - Painting & Coatings - Review & Approved	06/02/23 A	32d	0d	07/18/23 A		A1150	A1740, A:	Standard w/ Basic Holidays																
23 00 00 - Ventilation Enclosures - Review & Approved PS 62 & 63	06/14/23 A	13d	0d	07/18/23 A		A1170	A3130	Standard w/ Basic Holidays																
26 24 19 - Motor Control Centers - Review & Approved	06/20/23 A	44d	0d	08/21/23 A		A1200	A3150	Standard w/ Basic Holidays																
32 31 13/32 31 19 Fencing - Review & Approved	11/10/23 A	32d	0d	01/02/24 A		A1240	A3050, A:	Standard w/ Basic Holidays																
31 23 19 - Dewatering Plan - Review & Approved	11/21/23 A	15d	0d	12/08/23 A		A1220	A2100	Standard w/ Basic Holidays																
33 05 16 - Utility Structure - Review & Approved	01/25/24	15d	15d	02/14/24	161d	A1250	A1620, A	Standard w/ Basic Holidays																
05 50 00 - Metal Grating - Review & Approved PS 62 & 71	01/25/24	15d	15d	02/14/24	29d	A3340	A2250, A	Standard w/ Basic Holidays																
40 05 15 Pipe Supports - Review & Approved PS 62 & 71	02/01/24	15d	15d	02/21/24	18d	A3360	A3420	Standard w/ Basic Holidays																
01 75 00 - Commishioning and Startup Plan - Review & Approved	02/22/24	0d	0d	02/22/24	8d	A3370	A3070	Standard w/ Basic Holidays																
23 00 00 - Ventilation Enclosures - Review & Approved PS 71	03/07/24	15d	15d	03/27/24	97d	A3350	A3410	Standard w/ Basic Holidays																
41 22 13 - Cranes & Hoist - Review & Approved	03/21/24	15d	15d	04/10/24	56d	A1310	A2430	Standard w/ Basic Holidays																
Div 31 - Landscape Materials - Review & Approved	04/18/24	15d	15d	05/08/24	135d	A1230	A2470, A	Standard w/ Basic Holidays																
Delivery Lead	04/13/23 A	341d	183d	10/10/24	24d			Standard w/ Basic Holidays																
40 23 00 - Process Pipe, Fittings, & Accessories	04/13/23 A	50d	0d	09/29/23 A		A1920	A1410, A	Standard w/ Basic Holidays																
26 05 00 - EV Charing Station	05/02/23 A	60d	0d	01/26/24 A		A3490	A3020, A:	Standard w/ Basic Holidays																
43 21 13 - Vert Centrifugal Non-Clog Sewage Pumps	05/04/23 A	140d	15d	02/14/24	49d	A1960	A2220	Standard w/ Basic Holidays																
05 12 00 - Structural & Misc Steel	05/09/23 A	50d	0d	01/08/24 A		A1770	A1430, A:	Standard w/ Basic Holidays																
23 80 00 - Odor Control Equipment	05/09/23 A	85d	0d	10/30/23 A		A1820	A2410, A:	Standard w/ Basic Holidays																
43 21 39 - Sump Pump Delivery	05/09/23 A	60d	0d	08/01/23 A		A1970	A2820, A:	Standard w/ Basic Holidays																
26 50 00 - Lighting	05/18/23 A	45d	0d	01/10/24 A		A3270	A2120, A:	Standard w/ Basic Holidays																
23 00 00 - Ventilation Fans	06/05/23 A	65d	0d	09/22/23 A		A1800	A1730, A:	Standard w/ Basic Holidays																
26 24 00 - Panelboards	06/05/23 A	110d	2d	01/26/24	1d	A3250	A1470, A:	Standard w/ Basic Holidays																
40 23 01 - Pump Station Valves	07/10/23 A	50d	0d	09/19/23 A		A1930	A1410, A	Standard w/ Basic Holidays																
05 50 00 - Metal Grating	07/12/23 A	45d	0d	10/25/23 A		A1780	A2790	Standard w/ Basic Holidays																
23 00 00 - Ventilation Enclosures PS 62 & 63	07/19/23 A	65d	0d	10/20/23 A		A1810	A3000, A:	Standard w/ Basic Holidays																
40 05 15 - Pipe Supports PS 63	08/01/23 A	50d	0d	12/13/23 A		A1910	A2800, A:	Standard w/ Basic Holidays																
26 29 13 - Combination Motor Starter	08/03/23 A	50d	0d	01/25/24	3d	A1850	A2260, A:	Standard w/ Basic Holidays																
40 05 08 - Stainless Steel Slide Gates	08/15/23 A	90d	0d	12/06/23 A		A1900	A1490, A:	Standard w/ Basic Holidays																
26 24 19 - Motor Control Centers	08/22/23 A	250d	183d	10/10/24	4d	A1840	A1470	Standard w/ Basic Holidays																
Div 40 - Instrumentation	08/29/23 A	50d	0d	01/25/24	-6d	A1940	A2240, A:	Standard w/ Basic Holidays																
Div 26 - Electrical Materials	09/15/23 A	30d	0d	01/25/24 A		A1830	A1470, A	Standard w/ Basic Holidays																
32 31 13/32 31 19 Fencing	01/25/24	1d	1d	01/25/24	38d	A1880	A3050, A:	Standard w/ Basic Holidays																

■ Remaining Level of Effort
 ■ Actual Work
 ■ Critical Remaining Work
■ Actual Level of Effort
 ■ Remaining Work
 ◆ Milestone

Activity Name	Start	Original Duration	Remaining Duration	Finish	Total Float	Predecessor	Successors	Calendar	Calendar														
									Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	2025						
									F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr
05 50 00 - Metal Grating PS 62 & 71	02/15/24	30d	30d	03/27/24	29d	A3400	A2250, A	Standard w/ Basic Holidays	05 50 00 - Metal Grating PS 62 & 71														
40 05 15 - Pipe Supports PS 62 & 71	02/22/24	30d	30d	04/03/24	18d	A3390	A2240, A	Standard w/ Basic Holidays	40 05 15 - Pipe Supports PS 62 & 71														
23 00 00 - Ventilation Enclosures PS 71	03/28/24	65d	65d	06/27/24	97d	A3380	A1720, A	Standard w/ Basic Holidays	23 00 00 - Ventilation Enclosures PS 71														
Pump Station 63	09/05/23 A	145d	48d	04/01/24	216d				04/01/24, Pump Station 63														
Boring and Soil Sample Collection	09/05/23 A	1d	0d	09/06/23 A		A2020	A3450	SPU 4x10 Schedule	Boring and Soil Sample Collection														
Soil Sample Lab Analysis & Waste Profile Creation	09/05/23 A	1d	0d	09/26/23 A		A3440	A3460	SPU 4x10 Schedule	Soil Sample Lab Analysis & Waste Profile Creation														
Profile Review for Disposal - Republic Services	09/27/23 A	2d	0d	09/29/23 A		A3450	A2030	SPU 4x10 Schedule	Profile Review for Disposal - Republic Services														
Site Mobilization	10/10/23 A	3d	0d	10/16/23 A		A2780, A	A2580, A	SPU 4x10 Schedule	Site Mobilization														
Install Traffic Control	10/16/23 A	1d	0d	10/24/23 A		A2570	A2580	SPU 4x10 Schedule	Install Traffic Control														
Demo Ex. Retaining Wall	10/17/23 A	2d	0d	10/24/23 A		A2580, A	A2640	SPU 4x10 Schedule	Demo Ex. Retaining Wall														
Demo Existing Fence	10/17/23 A	1d	0d	10/18/23 A		A2580	A2590	SPU 4x10 Schedule	Demo Existing Fence														
Install Erosion Control/Tree Protection	10/17/23 A	1d	0d	10/17/23 A		A2570, A	A2590, A	SPU 4x10 Schedule	Install Erosion Control/Tree Protection														
Demo Existing Pavers in conflict with underground	10/17/23 A	2d	0d	10/19/23 A		A2580	A2710, A	SPU 4x10 Schedule	Demo Existing Pavers in conflict with underground														
Install Temp Power Panel	10/18/23 A	2d	0d	10/19/23 A		A2570	A2610, A	SPU 4x10 Schedule	Install Temp Power Panel														
Install Temp PS Bypass	10/24/23 A	4d	0d	10/30/23 A		A2600	A2630, A	SPU 4x10 Schedule	Install Temp PS Bypass														
Pump Station in Bypass	10/30/23 A	58d	33d	03/25/24	0d	A2610	A3090, A	SPU 4x10 Schedule	Pump Station in Bypass														
Demo Existing Electrical	10/31/23 A	2d	0d	11/02/23 A		A2590, A	A2650, A	SPU 4x10 Schedule	Demo Existing Electrical														
Demo Existing Sidewalk, Curb, Asphalt in conflict with underground	11/01/23 A	2d	0d	11/07/23 A		A2690	A2750	SPU 4x10 Schedule	Demo Existing Sidewalk, Curb, Asphalt in conflict with underground														
Telecommunication Demo inside Drywell	11/02/23 A	1d	0d	11/02/23 A		A2630, A	A2640	SPU 4x10 Schedule	Telecommunication Demo inside Drywell														
Lead Abatement of Existing Coatings	11/06/23 A	3d	0d	11/09/23 A		A2640	A2680, A	SPU 4x10 Schedule	Lead Abatement of Existing Coatings														
Excavate to top of PS for Ex FM Demo (Contaminated Soils)	11/08/23 A	1d	0d	11/09/23 A		A2690, A	A2800, A	SPU 4x10 Schedule	Excavate to top of PS for Ex FM Demo (Contaminated Soils)														
Demo Ex FM, including Plugs, and MH Rechannel (Protect Sleeve into PS)	11/13/23 A	1d	0d	12/12/23 A		A2750	A2760	SPU 4x10 Schedule	Demo Ex FM, including Plugs, and MH Rechannel (Protect S)														
Salvage Existing Pumps	11/20/23 A	1d	0d	11/21/23 A		A2650	A2700	SPU 4x10 Schedule	Salvage Existing Pumps														
Install 6" PS (FM) & Backfill Trench	11/22/23 A	5d	0d	12/11/23 A		A2750	A2870, A	SPU 4x10 Schedule	Install 6" PS (FM) & Backfill Trench														
Lead Abatement Dry Well Piping	12/11/23 A	3d	0d	12/14/23 A		A2650	A3750, A	SPU 4x10 Schedule	Lead Abatement Dry Well Piping														
Trench Compaction Test	12/12/23 A	1d	0d	12/12/23 A		A2770		SPU 4x10 Schedule	Trench Compaction Test														
Plan & Execute Support of Unknown Concrete Duct Bank to continue Excavation	12/14/23 A	8d	0d	12/26/23 A			A3760	SPU 4x10 Schedule	Plan & Execute Support of Unknown Concrete Duct Bank														
Demo Existing Mechanical	12/18/23 A	1d	0d	12/19/23 A		A3740	A2670, A	SPU 4x10 Schedule	Demo Existing Mechanical														
Lead Abatement Wet Well	12/18/23 A	1d	0d	12/19/23 A		A3740	A3850	SPU 4x10 Schedule	Lead Abatement Wet Well														
Expand PS Excavation for Pipe Penetration Slab	12/26/23 A	2d	0d	12/27/23 A		A3780	A2760, A	SPU 4x10 Schedule	Expand PS Excavation for Pipe Penetration Slab														
Core Drill PS Penetrations and Remove Existing Sleeves	01/02/24 A	2d	0d	01/03/24 A		A3760	A2700, A	SPU 4x10 Schedule	Core Drill PS Penetrations and Remove Existing Sleeves														
Remove Lead Abatement Blast Media	01/02/24 A	1d	0d	01/02/24 A		A3740, A	A2670	Standard w/ Basic Holidays	Remove Lead Abatement Blast Media														
Penetration Support Slabs	01/03/24 A	2d	0d	01/04/24 A		A3800	A2870, A	SPU 4x10 Schedule	Penetration Support Slabs														
Install FM, HVAC, and Conduits through PS Lid Penetrations	01/03/24 A	1d	0d	01/04/24 A		A3790	A2840, A	SPU 4x10 Schedule	Install FM, HVAC, and Conduits through PS Lid Penetrations														
Cure Pipe Penetration Slab	01/04/24 A	4d	0d	01/08/24 A		A2840	A2920	Standard 24/7 Workweek Schedule (see label)	Cure Pipe Penetration Slab														
Backfill Pipe Penetration Slab to Concrete Duct Bank	01/09/24 A	1d	0d	01/10/24 A		A3810	A2860, A	SPU 4x10 Schedule	Backfill Pipe Penetration Slab to Concrete Duct Bank														
Install 4" Prop Wet Well Supply and Exhaust Duct	01/10/24 A	3d	0d	01/17/24 A		A2840, A	A2910, A	SPU 4x10 Schedule	Install 4" Prop Wet Well Supply and Exhaust Duct														
Remove Concrete Duct Bank Support	01/10/24 A	1d	0d	01/10/24 A		A2920		SPU 4x10 Schedule	Remove Concrete Duct Bank Support														
Install Pump Intake Replacement	01/11/24 A	2d	0d	01/16/24 A		A2680, A	A2720, A	SPU 4x10 Schedule	Install Pump Intake Replacement														
Demo & Form Pump Concrete Pads (Includes Cure)	01/11/24 A	5d	0d	01/16/24 A		A2660	A2720, A	SPU 4x10 Schedule	Demo & Form Pump Concrete Pads (Includes Cure)														
Set Salvaged Pumps	01/16/24 A	1d	0d	01/16/24 A		A2700, A	A2850, A	SPU 4x10 Schedule	Set Salvaged Pumps														
Install Interior Forcemain to Roof Penetration	01/16/24 A	8d	0d	01/24/24 A		A3180, A	A2790, A	SPU 4x10 Schedule	Install Interior Forcemain to Roof Penetration														
Site Electrical Conduit/Handhole Install	01/23/24 A	4d	1d	01/29/24	11d	A2870, A	A2950, A	SPU 4x10 Schedule	Site Electrical Conduit/Handhole Install														
Demo Grating & Ladder	01/24/24 A	2d	2d	01/29/24	-2d	A2640, A	A2790	SPU 4x10 Schedule	Demo Grating & Ladder														
Pour Pumps Grout Pad	01/24/24 A	1d	0d	01/24/24 A		A3840, A		SPU 4x10 Schedule	Pour Pumps Grout Pad														
Install Drain from Odor Control Unit to PS	01/25/24	1d	1d	01/25/24	-1d	A2870	A2940, A	SPU 4x10 Schedule	Install Drain from Odor Control Unit to PS														
Install Water Service/RPBA/Hose Bib	01/25/24	2d	2d	01/29/24	11d	A2870, A	A3030, A	SPU 4x10 Schedule	Install Water Service/RPBA/Hose Bib														

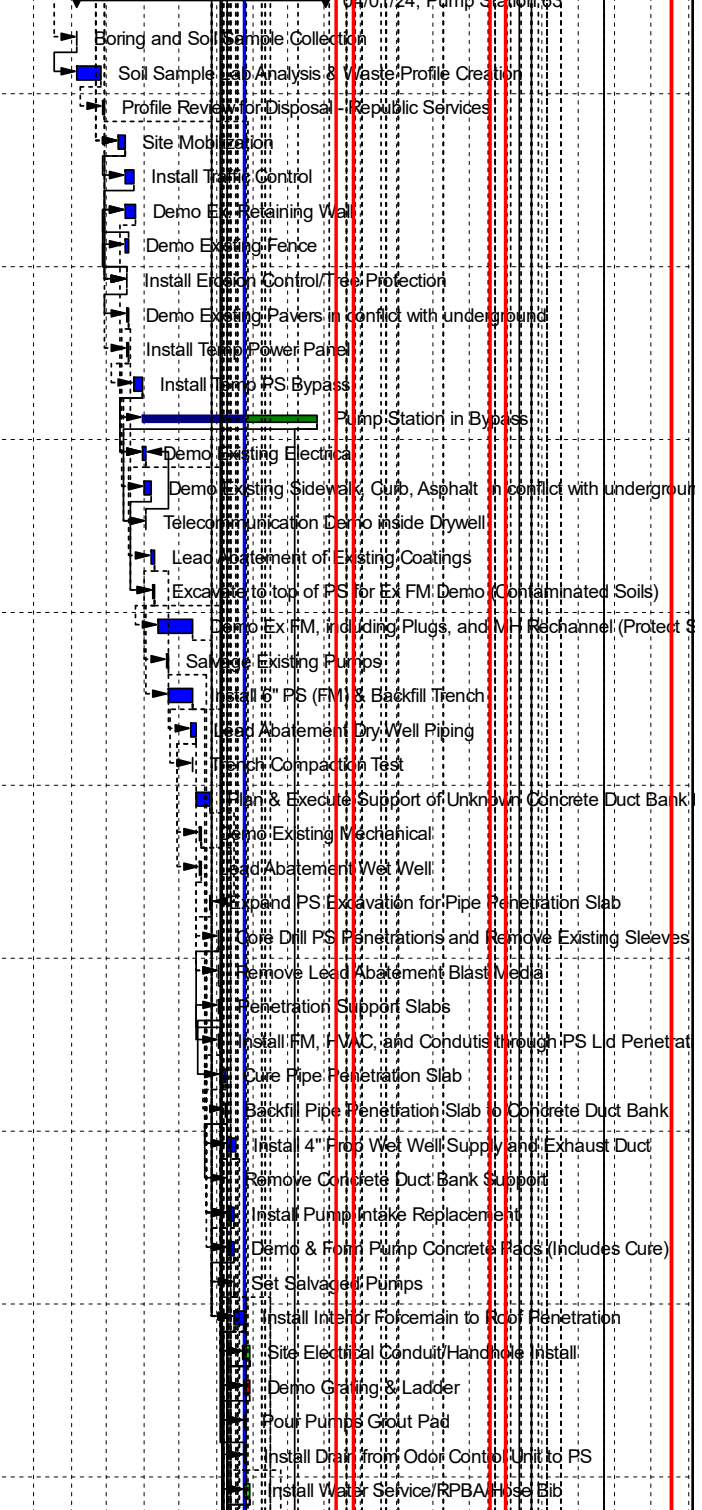


Remaining Level of Effort Actual Work Critical Remaining Work
 Actual Level of Effort Remaining Work Milestone Milestone

West Coast Waste - Rev3 (Including Zero Waste)				SPU					02/01/24 09:42																
Activity Name	Start	Original Duration	Remaining Duration	Finish	Total Float	Predecessors	Successors	Calendar	Tr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	2025								
									F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J
6" FM Hydrostatic & Leakage Test	01/25/24	1d	1d	01/25/24	20d	A2770, A:	A3070	SPU 4x10 Schedule																	
Install Interior Ventilation Ductwork to Roof Penetration	01/25/24	1d	1d	01/25/24	16d	A2760, A:	A2850	SPU 4x10 Schedule																	
Install Steel Framing/Grating/Ladders	01/25/24 A	3d	2d	01/31/24	12d	A2760, A:	A2820, A:	SPU 4x10 Schedule																	
Set Electrical Panels	01/29/24	2d	2d	01/30/24	1d	A3160, A:	A2890, A:	SPU 4x10 Schedule																	
CIP Odor Control Pad	01/29/24	2d	2d	01/31/24	12d	A2910, A:	A3830	SPU 4x10 Schedule																	
CIP Top Access Hatch Panel	01/29/24	3d	3d	02/01/24	11d	A2920, A:	A3830	SPU 4x10 Schedule																	
Prep Subgrade for Retaining Wall	01/29/24	1d	1d	01/29/24	11d	A2920, A:	A2960	SPU 4x10 Schedule																	
CIP EV Charging Station Base	01/29/24	2d	2d	01/31/24	12d	A2910	A3830	SPU 4x10 Schedule																	
Demo Ex Lumen Ped, and Install new Lumen HH	01/29/24	1d	1d	01/29/24	19d	A2910	A3040, A:	SPU 4x10 Schedule																	
CIP Wet Well Supply Fan Pad	01/29/24	2d	2d	01/31/24	11d	A2910, A:	A3830	SPU 4x10 Schedule																	
RPBA Inspection by SPU Cross Connections	01/29/24	1d	1d	01/30/24	30d	A2980	A3080	SPU 4x10 Schedule																	
CIP Retaining Wall	01/29/24	2d	2d	02/01/24	11d	A2860	A3030, A:	SPU 4x10 Schedule																	
Install Lighting	01/30/24	2d	2d	02/01/24	9d	A2810, A:	A2890	SPU 4x10 Schedule																	
Rough-In Electrical	01/30/24	8d	8d	02/13/24	1d	A2720, A:	A2850, A:	SPU 4x10 Schedule																	
Install Sump Pump & Discharge Line	02/01/24	1d	1d	02/01/24	12d	A2760, A:	A2850, A:	SPU 4x10 Schedule																	
Install Slide Gate in Wet Well	02/01/24	2d	2d	02/05/24	16d	A2660, A:	A3070, A:	SPU 4x10 Schedule																	
Cure CIP Pads & Retaining Wall	02/01/24	4d	4d	02/05/24	21d	A3010, A:	A2990, A:	Standard 24/7 Workweek Schedule (non-labor)																	
Install Interior Drain Line from Odor Control	02/01/24	1d	1d	02/05/24	12d	A2900, A:	A2850	SPU 4x10 Schedule																	
Install Odor Control Unit	02/05/24	1d	1d	02/06/24	11d	A3140, A:	A3070, A:	SPU 4x10 Schedule																	
Slide Gate Leakage Test	02/05/24	1d	1d	02/06/24	26d	A2830	A3080	SPU 4x10 Schedule																	
Install Wet Well Supply Fan & Enclosure	02/06/24	2d	2d	02/08/24	11d	A3120, A:	A3070, A:	SPU 4x10 Schedule																	
Install EV Charging Station	02/06/24	2d	2d	02/07/24	14d	A3510, A:	A3070	SPU 4x10 Schedule																	
Prep Concrete Pavement/Sidewalk/Parking Area/Roadway	02/08/24	4d	4d	02/15/24	11d	A2910, A:	A3040, A:	SPU 4x10 Schedule																	
Electrical Wire Pulling & Connections	02/13/24	10d	10d	03/04/24	1d	A2810, A:	A3070	SPU 4x10 Schedule																	
Painting in PS	02/13/24	4d	4d	02/21/24	7d	A2800, A:	A3070	SPU 4x10 Schedule																	
Concrete Sidewalk, Paver Base & Curb	02/15/24	2d	2d	02/21/24	11d	A3030, A:	A3050, A:	SPU 4x10 Schedule																	
Grind Existing Pavement/Pave Asphalt	02/21/24	1d	1d	02/22/24	16d	A3040	A3080	SPU 4x10 Schedule																	
Install Architectural Pavers	02/21/24	5d	5d	02/29/24	11d	A3040	A3050	SPU 4x10 Schedule																	
Install Fence & Arch Fence Panels	02/29/24	2d	2d	03/05/24	11d	A3040, A:	A3080	SPU 4x10 Schedule																	
Equipment Acceptance Testing	03/05/24	2d	2d	03/06/24	0d	A3000, A:	A3550	SPU Startup																	
Systems Acceptance Testing	03/06/24	2d	2d	03/12/24	0d	A3070	A3680	SPU Startup																	
Control Center Acceptance Testing	03/12/24	2d	2d	03/14/24	0d	A3550	A3610	SPU Startup																	
Operational Acceptance Testing	03/14/24	7d	7d	03/21/24	3d	A3680	A3080, A:	7-day workweek																	
Site Acceptance of PS 63	03/21/24	1d	1d	03/25/24	0d	A3050, A:	A3090, A:	SPU 4x10 Schedule																	
Demo Sewer Bypass	03/25/24	2d	2d	03/27/24	0d	A3080, A:	A2130	SPU 4x10 Schedule																	
Site Punchlist/Demob	03/25/24	4d	4d	04/01/24	168d	A3080	A3590	SPU 4x10 Schedule																	
Pump Station 62	02/15/24	170d	170d	10/15/24	79d																				
Site Mobilization	02/15/24	4d	4d	02/26/24	16d	A3460, A:	A2040, A:	SPU 4x10 Schedule																	
Schedule SCL Service Connection (3-12 Weeks)	02/26/24	0d	0d		189d	A2440		SPU 4x10 Schedule																	
Install Erosion Control	02/26/24	1d	1d	02/27/24	16d	A2030, A:	A2070, A:	SPU 4x10 Schedule																	
Install Traffic Control	02/26/24	1d	1d	02/27/24	189d	A2030		SPU 4x10 Schedule																	
Clear & Grub	02/27/24	1d	1d	02/28/24	27d	A2040	A2060, A:	SPU 4x10 Schedule																	
Partial Demo Ex. Site Materials (Bug Machine, Signage, RPBA, Fence, Valve Box, etc)	02/27/24	2d	2d	02/28/24	16d	A2040	A2090, A:	SPU 4x10 Schedule																	
Demo Pavement, Curb, & Gutter	02/28/24	2d	2d	03/04/24	185d	A2050		SPU 4x10 Schedule																	
Ex/In/BF 4" Vents & OCE Drain from Equipment Pads to FJs	02/28/24	6d	6d	03/12/24	181d	A2070		SPU 4x10 Schedule																	
Demo Ex Sidewalk	03/25/24	2d	2d	03/27/24	13d	A2050, A:	A2110, A:	SPU 4x10 Schedule																	
Install Temp Power Panel	03/25/24	1d	1d	03/26/24	2d	A2070, A:	A2130, A:	SPU 4x10 Schedule																	

█ Remaining Level of Effort █ Actual Work █ Critical Remaining Work
█ Actual Level of Effort █ Remaining Work ◆ Milestone

West Coast Waste - Rev3 (Including Zero Waste)			SPU							02/01/24 09:42																						
Activity Name	Start	Original Duration	Remaining Duration	Finish	Total Float	Predecessors	Successors	Calendar	Calendar																							
									Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	2025															
									F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	Apr	M	J	Jul	A	S	Oct	N	D	Jan
Adjust JB Rim & Replace Grate	10/10/24	1d	1d	10/14/24	12d	A1550, A	A1640	SPU 4x10 Schedule																								
Set Electrical Panels	10/10/24	2d	2d	10/16/24	3d	A1430, A:	A1690, A:	SPU 4x10 Schedule																								
Install Lighting	10/16/24	2d	2d	10/21/24	3d	A1470, A:	A1690	SPU 4x10 Schedule																								
CIP Electrical Cabinet Pad	10/21/24	2d	2d	10/22/24	0d	A1590	A1640, A	SPU 4x10 Schedule																								
CIP Odor Control Pad	10/21/24	2d	2d	10/22/24	0d	A1590, A	A1640, A	SPU 4x10 Schedule																								
CIP Wet Well Supply Fan Pad	10/21/24	2d	2d	10/22/24	0d	A1590, A	A1640, A	SPU 4x10 Schedule																								
Prep Concrete Pavement/Sidewalk/Parking Area	10/22/24	5d	5d	10/30/24	7d	A1630, A	A1680	SPU 4x10 Schedule																								
Cure Pads	10/22/24	1d	1d	10/23/24	0d	A1580, A	A1720, A	Standard w/ Basic Holidays																								
Install Electrical Service Cabinet	10/23/24	1d	1d	10/24/24	0d	A1580, A:	A1690, A:	SPU 4x10 Schedule																								
Install Exhaust Fan and Enclosure	10/23/24	2d	2d	10/28/24	12d	A1600, A:	A1700	SPU 4x10 Schedule																								
Install Wet Well Supply Fan & Enclosure	10/23/24	2d	2d	10/28/24	11d	A1610, A:	A1700	SPU 4x10 Schedule																								
Electrical Raceways & Wire Pulling	10/24/24	12d	12d	11/18/24	0d	A1470, A	A1700, A:	SPU 4x10 Schedule																								
Concrete Pavement, Sidewalk, Curb	10/30/24	2d	2d	11/04/24	7d	A1640	A1670, A	SPU 4x10 Schedule																								
Install Fence	11/04/24	2d	2d	11/06/24	18d	A1680, A	A1760	SPU 4x10 Schedule																								
Install Bench	11/04/24	1d	1d	11/05/24	19d	A1680	A1760	SPU 4x10 Schedule																								
Landscaping	11/04/24	12d	12d	11/26/24	7d	A1680, A	A1760	SPU Planting																								
Telecommunication Install	11/18/24	1d	1d	11/19/24	0d	A1690	A1700	SPU 4x10 Schedule																								
Equipment Acceptance Testing	11/19/24	2d	2d	11/21/24	0d	A1690, A	A3720	SPU Startup																								
Systems Acceptance Testing	11/21/24	2d	2d	12/03/24	0d	A1700	A3730	SPU Startup																								
Control Center Acceptance Testing	12/03/24	1d	1d	12/03/24	0d	A3720	A3630	SPU Startup																								
Operational Acceptance Testing	12/04/24	7d	7d	12/10/24	0d	A3730	A1750, A	7-day workweek																								
Site Acceptance of PS 71	12/11/24	1d	1d	12/11/24	0d	A1740, A	A1750, A:	SPU 4x10 Schedule																								
Demo Sewer Bypass	12/11/24	2d	2d	12/16/24	28d	A1760, A:	A3430	SPU 4x10 Schedule																								
Project Closeout	12/11/24	29d	29d	02/05/25	0d			SPU 4x10 Schedule																								
Punchlist/Demob	12/11/24	12d	12d	01/06/25	0d	A1760	A3600, A:	SPU 4x10 Schedule																								
Project Closeout Paperwork	01/06/25	17d	17d	02/05/25	0d	A3580	A3430	SPU 4x10 Schedule																								



█ Remaining Level of Effort
 █ Actual Work
 █ Critical Remaining Work
█ Actual Level of Effort
 █ Remaining Work
 ◆ Milestone
 ◆ Milestone
