West Point Treatment Plant Digester LSG Pipe Replacement - | WBS Layout w/ WBS Summary | Aug-06-24 21:29
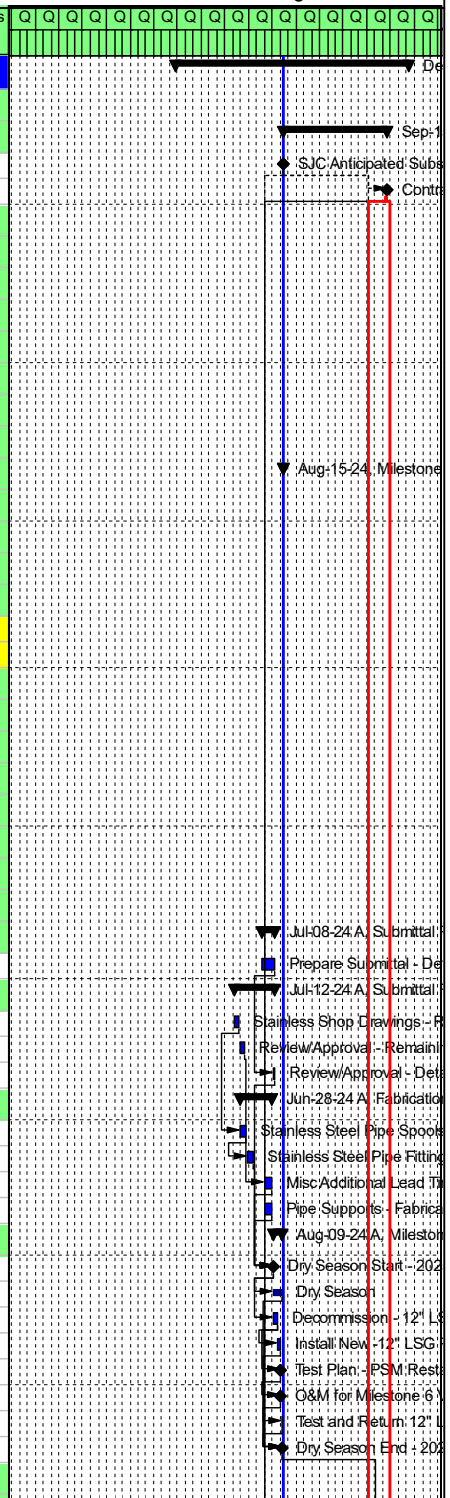
Activity ID	Activity Name	Original Duration	Remaining Duration	At Completion Duration	Start	Finish	Total Float	Predecessc	Successors
West Point Treatment Plant Digester LSG Pipe Replacemen		614.0	330.0	618.0	Jun-26-23 A	Dec-09-25	0.0		
Contract Items		0.0	0.0	0.0			0.0		
Milestones		270.0	270.0	270.0	Aug-15-24	Sep-15-25	0.0		
A2290	SJC Anticipated Substantial Completion (in work days)	0.0	0.0	0.0	Aug-15-24		270.0	A4340	A2280, A:
A2280	Contract Substantial Completion - September 15th, 2025	0.0	0.0	0.0		Sep-15-25*	0.0	A1010, A:	A2260, A:
Critical Milestone #1 Submittals Prepared by Contractor		0.0	0.0	0.0			0.0		
Critical Milestone #1 Submittal Reviews & Approval		0.0	0.0	0.0			0.0		
Milestone #1 Fabrication and Delivery Lead Time		0.0	0.0	0.0			0.0		
Mobilization		0.0	0.0	0.0			0.0		
Milestone 1 - All Digester 1 Dry Season Work 2021		0.0	0.0	0.0			0.0		
Submittal Prep by Contractor - Milestones 2		0.0	0.0	0.0			0.0		
Submittal Review / Approval Milestones 2		0.0	0.0	0.0			0.0		
Fabrication & Delivery Lead Time - Milestones 2		0.0	0.0	0.0			0.0		
Milestone 2 - All Digester 2 Dry Season Work 2022		0.0	0.0	0.0	Aug-15-24	Aug-15-24	-490.0		
Submittal Prep by Contractor - Milestones 3		0.0	0.0	0.0			0.0		
Submittal Review / Approval Milestones 3		0.0	0.0	0.0			0.0		
Fabrication & Delivery Lead Time - Milestones 3		0.0	0.0	0.0			0.0		
Milestone 3 - All Digester 3 & LSG Dry Season Work 2023		0.0	0.0	0.0			0.0		
Compressor Digester 3		0.0	0.0	0.0			0.0		
Auxiliary Compressor		0.0	0.0	0.0			0.0		
Submittal Prep by Contractor - Milestones 4		0.0	0.0	0.0			0.0		
Submittal Review / Approval Milestones 4		0.0	0.0	0.0			0.0		
Fabrication & Delivery Lead Time - Milestones 4		0.0	0.0	0.0			0.0		
Milestone 4 - 12" & 18" LSG Tunnel Piping - Wet Season 2(		0.0	0.0	0.0			0.0		
Submittal Prep by Contractor - Milestones 5		0.0	0.0	0.0			0.0		
Submittal Review / Approval Milestones 5		0.0	0.0	0.0			0.0		
Fabrication & Delivery Lead Time - Milestones 5		0.0	0.0	0.0			0.0		
Milestone 5 - All Digester 4 Dry Season Work 2024		0.0	0.0	0.0			0.0		
Submittal Prep by Contractor - Milestones 6		16.0	0.0	30.0	May-24-24 A	Jul-08-24 A			
A5250	Prepare Submittal - Detailed Safe Opening Plan - Submittal Prepar	16.0	0.0	30.0	May-24-24 A	Jul-08-24 A		A3720	A5230
Submittal Review / Approval Milestones 6		122.0	0.0	112.0	Feb-06-24 A	Jul-12-24 A			
A5220	Stainless Shop Drawings - Review/Approval/Fab - Milestones 6	20.0	0.0	14.0	Feb-06-24 A	Feb-23-24 A		A5260	A5280
A5240	Review/Approval - Remaining Sections - Milestones 6	15.0	0.0	15.0	Feb-26-24 A	Mar-15-24 A		A5270	A5320
A5230	Review/Approval - Detailed Safe Opening Plan - Milestones 6	15.0	0.0	5.0	Jul-08-24 A	Jul-12-24 A		A5250	A3730
Fabrication & Delivery Lead Time - Milestones 6		89.0	0.0	89.0	Feb-26-24 A	Jun-28-24 A			
A5280	Stainless Steel Pipe Spools - Fabrication Time	20.0	0.0	20.0	Feb-26-24 A	Mar-22-24 A		A5220	A5310
A5310	Stainless Steel Pipe Fittings / Fabrication to Spools	20.0	0.0	20.0	Mar-25-24 A	Apr-19-24 A		A5280	A3730
A5320	Misc Additional Lead Time Items	20.0	0.0	20.0	Jun-03-24 A	Jun-28-24 A		A5240	A3730
A5300	Pipe Supports - Fabrication Time	20.0	0.0	20.0	Jun-03-24 A	Jun-28-24 A		A5260	A3730
Milestone 6 - All Digester 5 Dry Season Work 2025		244.0	0.0	26.0	Jul-05-24 A	Aug-09-24 A			
A3730	Dry Season Start - 2025	0.0	0.0	0.0	Jul-05-24 A			A3720, A:	A3740, A:
A3740	Dry Season	73.0	0.0	25.0	Jul-05-24 A	Aug-09-24 A		A3730	A3750
A4290	Decommission - 12" LSG Pipe on Digester 5	4.0	0.0	10.0	Jul-08-24 A	Jul-19-24 A		A3730	A4300, A:
A4300	Install New -12" LSG Pipe on Digester 5 - inc. Supports and Bracir	15.0	0.0	10.0	Jul-22-24 A	Aug-02-24 A		A4290	A4310
A4740	Test Plan - PSM Restart	0.0	0.0	0.0	Aug-02-24 A			A4290	A4750
A4750	O&M for Milestone 6 Valves & If applicable a portion of 01 78 40A	0.0	0.0	0.0	Aug-02-24 A			A4740	A3750
A4310	Test and Return 12" LSG Pipe to Service inc. I&C	10.0	0.0	5.0	Aug-05-24 A	Aug-09-24 A		A4300	A3750
A3750	Dry Season End - 2025	0.0	0.0	0.0		Aug-09-24 A		A3740, A:	A5560
Submittal Prep by Contractor - Milestones 7 (Canceled Per		0.0	0.0	0.0			0.0
