Activity ID	Activity Name	Original Duration	naining Duration	Start	Finish	Total Float
SPU PS 62, 63, 71 Improvements - Update 2023-12		520	284	19-Jan-23 A	05-Feb-25	0
Milestones		342	47	19-Jan-23 A	05-Feb-25	0
A2020	Contract Execution	0	0	19-Jan-23 A		
A2780	Notice to Proceed	0	0	10-Oct-23 A		
A3590	SJC Anticipated Substantial Completion	1	1	27-Nov-24	27-Nov-24	46
A3430	Contract Physical Completion	0	0		05-Feb-25*	0
Procurement		400	183	19-Jan-23 A	11-Sep-24	47
Submittals		311	75	19-Jan-23 A	09-Apr-24	155
Submittal Prep		256	60	19-Jan-23 A	19-Mar-24	155
A1130	05 12 00 - Structural & Misc Steel - Prep & Submit	77	0	19-Jan-23 A	03-May-23	
A1140	05 50 00 - Metal Grating - Prep & Submit PS 63	122	0	19-Jan-23 A	08-May-23	
A1150	09 90 00 - Painting & Coatings - Prep & Submit	127	0	19-Jan-23 A	02-Jun-23	
A1160	23 00 00 - Ventilation Fans - Prep & Submit	96	0	19-Jan-23 A	14-Apr-23	
A1170	23 00 00 - Ventilation Enclosures - Prep & Submit PS	127	0	19-Jan-23 A	14-Jul-23 A	
A1180	23 80 00 - Odor Control Equipment	60	0	19-Jan-23 A	13-Apr-23	
A1200	26 24 19 - Motor Control Centers - Prep & Submit	108	0	19-Jan-23 A	20-Jun-23	
A1210	26 29 13 - Combination Motor Starter - Prep & Subn	75	0	19-Jan-23 A	04-May-23	
A1220	31 23 19 - Dewatering Plan - Prep & Submit	60	0	19-Jan-23 A	21-Nov-23	
A1230	Div 31 - Landscape Materials - Prep & Submit	60	60	19-Jan-23 A	19-Mar-24	155
A1260	40 05 08 - Stainless Steel Slide Gates Prep & Subm	60	0	19-Jan-23 A	13-Apr-23	
A1270	40 05 15 Pipe Supports- Prep & Submit PS63	50	0	19-Jan-23 A	30-Mar-23	
A1280	40 23 00 - Process Pipe, Fittings, & Accessories	45	0	19-Jan-23 A	23-Mar-23	
A1320	43 21 13 - Vert Centrifugal Non-Clog Sewage Pumps	52	0	19-Jan-23 A	03-Apr-23	
A1330	43 21 39 - Sump Pumps	67	0	19-Jan-23 A	24-Apr-23	
A1340	01 57 13 - Construction Stormwater & Erosion Contr	65	0	19-Jan-23 A	21-Apr-23	
A1350	00 31 00 - Site Security Plan	65	0	19-Jan-23 A	20-Apr-23	
A1360	01 57 13 - Tree, Vegetation, and Soil Protection Plan	55	0	19-Jan-23 A	06-Apr-23	
A1370	01 57 13 - Spill Plan	55	0	19-Jan-23 A	06-Apr-23	
A3110	26 24 00 - Panelboards - Prep & Submit	70	0	19-Jan-23 A	27-Apr-23	
A3280	26 50 00 Lighting - Prep & Submit	80	0	19-Jan-23 A	11-May-23	
A3340	05 50 00 - Metal Grating - Prep & Submit PS 62 & 7	80	0	19-Jan-23 A	22-Dec-23	48
A3480	26 05 00 EV Charging Station	59	0	19-Jan-23 A	13-Apr-23	
A3350	23 00 00 - Ventilation Enclosures - Prep & Submit P	80	30	30-Jan-23 A	06-Feb-24	114
A3360	40 05 15 Pipe Supports- Prep & Submit PS62 & PS	215	5	30-Jan-23 A	02-Jan-24	16
A1190	Div 26 - Electrical Materials - Prep & Submit	1	0	13-Mar-23 A	13-Mar-23	
A1290	40 23 01 - Pump Station Valves - Prep & Submit	1	0	21-Mar-23 A	21-Mar-23	
A1300	Div 40 - Instrumentation - Prep & Submit	1	0	13-Apr-23 A	13-Apr-23	
A1240	32 31 13/32 31 19 Fencing - Prep & Submit	6	0	19-Jun-23 A	10-Nov-23	
A1250	33 05 16 - Utility Structure - Prep & Submit	40	0	19-Jun-23 A	21-Nov-23	
A1310	41 22 13 - Cranes & Hoist - Prep & Submit	40	40	19-Jun-23 A	20-Feb-24	77
A3370	01 75 00 - Commishioning & Startup Plan - Prep & S	20	20	22-Dec-23	23-Jan-24	6
Submittal Review & Approval		275	75	13-Mar-23 A	09-Apr-24	155
A1830	Div 26 - Electrical Materials Review & Approved	132	0	13-Mar-23 A	14-Sep-23	
A1930	40 23 01 - Pump Station Valves - Review & Approve	15	0	21-Mar-23 A	01-May-23	
A1920	40 23 00 - Process Pipe, Fittings, & Accessories - Re	15	0	23-Mar-23 A	12-Apr-23	
A1910	40 05 15 Pipe Supports - Review & Approved PS 63	87	0	30-Mar-23 A	31-Jul-23 A	
A1960	43 21 13 - Vert Centrifugal Non-Clog Sewage Pumps	30	0	03-Apr-23 A	03-May-23	
A2000	01 57 13 - Tree, Vegetation, and Soil Protection Plan	8	0	06-Apr-23 A	14-Apr-23	
A2010	01 57 13 - Spill Plan - Review & Approved	24	0	06-Apr-23 A	08-May-23	
A3490	26 05 00 - EV Charing Station - Review & Approved	15	0	12-Apr-23 A	02-May-23	
A1820	23 80 00 - Odor Control Equipment - Review & Appr	18	0	13-Apr-23 A	08-May-23	
A1900	40 05 08 - Stainless Steel Slide Gates - Review & Ap	87	0	13-Apr-23 A	14-Aug-23	
A1940	Div 40 - Instrumentation - Review & Approved	97	0	13-Apr-23 A	28-Aug-23	
A1800	23 00 00 - Ventilation Fans - Review & Approved	36	0	14-Apr-23 A	02-Jun-23	
A1990	00 31 00 - Site Security Plan - Review & Approved	50	0	20-Apr-23 A	28-Jun-23	

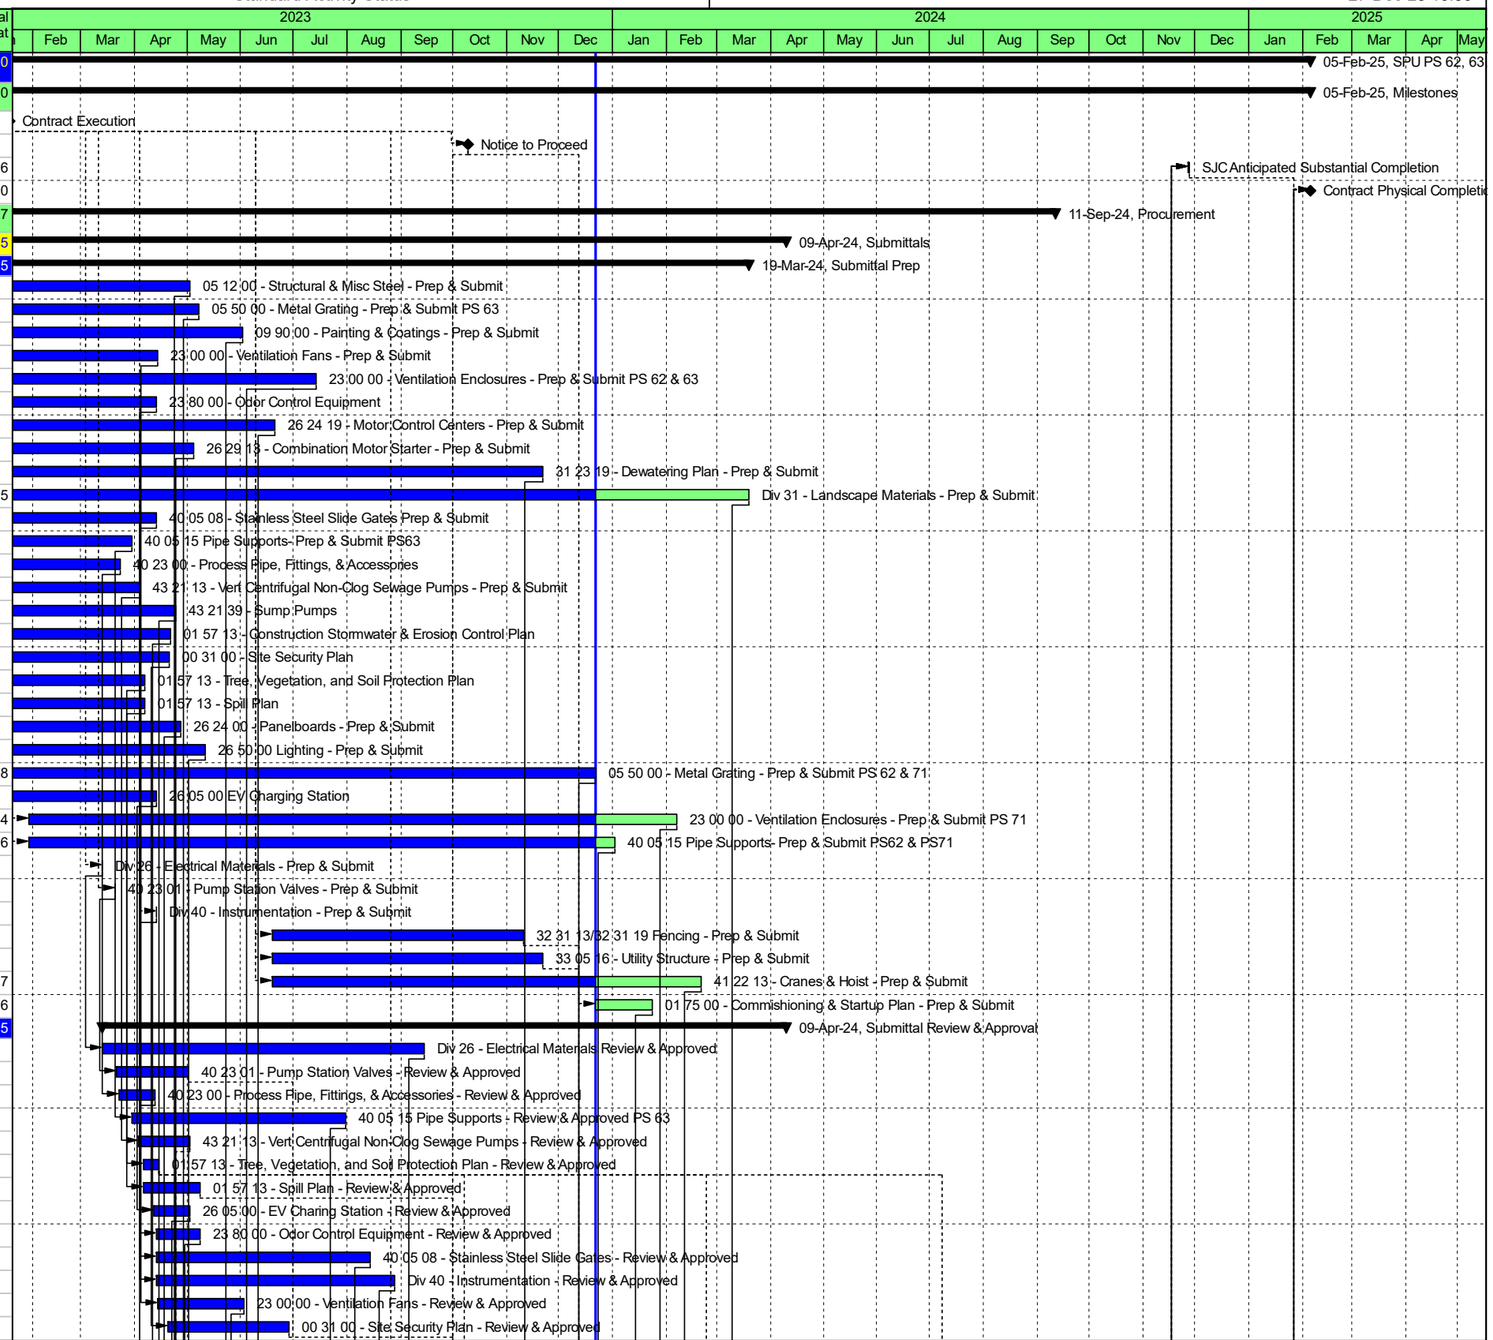

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	naining Duration	Start	Finish	Total Float
A1980	01 57 13 - Construction Stormwater & Erosion Contr	1	0	21-Apr-23 A	21-Apr-23	
A1970	43 21 39 - Sump Pumps - Review & Approved	7	0	24-Apr-23 A	02-May-23	
A3250	26 24 00 - Panelboards - Review & Approve	27	0	27-Apr-23 A	02-Jun-23	
A1770	05 12 00 - Structural & Misc Steel - Review & Approv	4	0	03-May-23 A	08-May-23	
A1850	26 29 13 - Combination Motor Starter - Review & Ap	64	0	04-May-23 A	02-Aug-23	
A1780	05 50 00 - Metal Grating - Review & Approved PS 63	46	0	08-May-23 A	11-Jul-23 A	
A3270	26 50 00 Lighting - Review & Approved	5	0	11-May-23 A	17-May-23	
A1790	09 90 00 - Painting & Coatings - Review & Approved	32	0	02-Jun-23 A	18-Jul-23 A	
A1810	23 00 00 - Ventilation Enclosures - Review & Approv	13	0	14-Jun-23 A	18-Jul-23 A	
A1840	26 24 19 - Motor Control Centers - Review & Approv	44	0	20-Jun-23 A	21-Aug-23	
A1860	31 23 19 - Dewatering Plan - Review & Approved	15	0	21-Nov-23 A	08-Dec-23	
A1880	32 31 13/32 31 19 Fencing - Review & Approved	15	15	22-Dec-23	16-Jan-24	40
A1890	33 05 16 - Utility Structure - Review & Approved	15	15	22-Dec-23	16-Jan-24	182
A3400	05 50 00 - Metal Grating - Review & Approved PS 62	15	15	22-Dec-23	16-Jan-24	48
A3390	40 05 15 Pipe Supports - Review & Approved PS 62	15	15	02-Jan-24	23-Jan-24	16
A3560	01 75 00 - Commishioning and Startup Plan - Revie	15	15	23-Jan-24	13-Feb-24	6
A3380	23 00 00 - Ventilation Enclosures - Review & Approv	15	15	06-Feb-24	27-Feb-24	114
A1950	41 22 13 - Cranes & Hoist - Review & Approved	15	15	20-Feb-24	12-Mar-24	77
A1870	Div 31 - Landscape Materials - Review & Approved	15	15	19-Mar-24	09-Apr-24	155
Delivery Lead		341	183	13-Apr-23 A	11-Sep-24	41
A3190	40 23 00 - Process Pipe, Fittings, & Accessories	50	0	13-Apr-23 A	29-Sep-23	
A3510	26 05 00 - EV Charing Station	60	2	02-May-23 A	27-Dec-23	38
A3210	43 21 13 - Vert Centrifugal Non-Clog Sewage Pumps	140	15	04-May-23 A	16-Jan-24	67
A3220	05 12 00 - Structural & Misc Steel	50	5	09-May-23 A	02-Jan-24	24
A3140	23 80 00 - Odor Control Equipment	85	0	09-May-23 A	30-Oct-23	
A3470	43 21 39 - Sump Pump Delivery	60	0	09-May-23 A	01-Aug-23	
A3290	26 50 00 - Lighting	45	0	18-May-23 A	22-Dec-23	25
A3120	23 00 00 - Ventilation Fans	65	0	05-Jun-23 A	22-Sep-23	
A3260	26 24 00 - Panelboards	110	2	05-Jun-23 A	27-Dec-23	22
A3200	40 23 01 - Pump Station Valves	50	0	10-Jul-23 A	19-Sep-23	
A3230	05 50 00 - Metal Grating	45	0	12-Jul-23 A	25-Oct-23	
A3130	23 00 00 - Ventilation Enclosures PS 62 & 63	65	0	19-Jul-23 A	20-Oct-23	
A3180	40 05 15 - Pipe Supports PS 63	50	0	01-Aug-23 A	13-Dec-23	
A3160	26 29 13 - Combination Motor Starter	50	10	03-Aug-23 A	09-Jan-24	14
A3170	40 05 08 - Stainless Steel Slide Gates	90	0	15-Aug-23 A	06-Dec-23	
A3150	26 24 19 - Motor Control Centers	250	183	22-Aug-23 A	11-Sep-24	23
A3300	Div 40 - Instrumentation	50	0	29-Aug-23 A	22-Dec-23	22
A3240	Div 26 - Electrical Materials	30	5	15-Sep-23 A	02-Jan-24	19
A3500	32 31 13/32 31 19 Fencing	1	1	16-Jan-24	17-Jan-24	40
A3570	05 50 00 - Metal Grating PS 62 & 71	30	30	16-Jan-24	27-Feb-24	48
A3420	40 05 15 - Pipe Supports PS 62 & 71	50	50	23-Jan-24	02-Apr-24	16
A3410	23 00 00 - Ventilation Enclosures PS 71	65	65	27-Feb-24	29-May-24	114
Pump Station 63		137	60	05-Sep-23 A	21-Mar-24	222
A3440	Boring and Soil Sample Collection	1	0	05-Sep-23 A	06-Sep-23	
A3450	Soil Sample Lab Analysis & Waste Profile Creation	1	0	05-Sep-23 A	26-Sep-23	
A3460	Profile Review for Disposal - Republic Services	2	0	27-Sep-23 A	29-Sep-23	
A2570	Site Mobilization	3	0	10-Oct-23 A	16-Oct-23	
A3100	Install Traffic Control	1	0	16-Oct-23 A	24-Oct-23	
A2590	Demo Ex. Retaining Wall	2	0	17-Oct-23 A	24-Oct-23	
A2620	Demo Existing Fence	1	0	17-Oct-23 A	18-Oct-23	
A2580	Install Erosion Control/Tree Protection	1	0	17-Oct-23 A	17-Oct-23	
A2690	Demo Existing Pavers in conflict with underground	2	0	17-Oct-23 A	19-Oct-23	
A2600	Install Temp Power Panel	2	0	18-Oct-23 A	19-Oct-23	
A2610	Install Temp PS Bypass	4	0	24-Oct-23 A	30-Oct-23	
A2630	Pump Station in Bypass	58	43	30-Oct-23 A	14-Mar-24	2

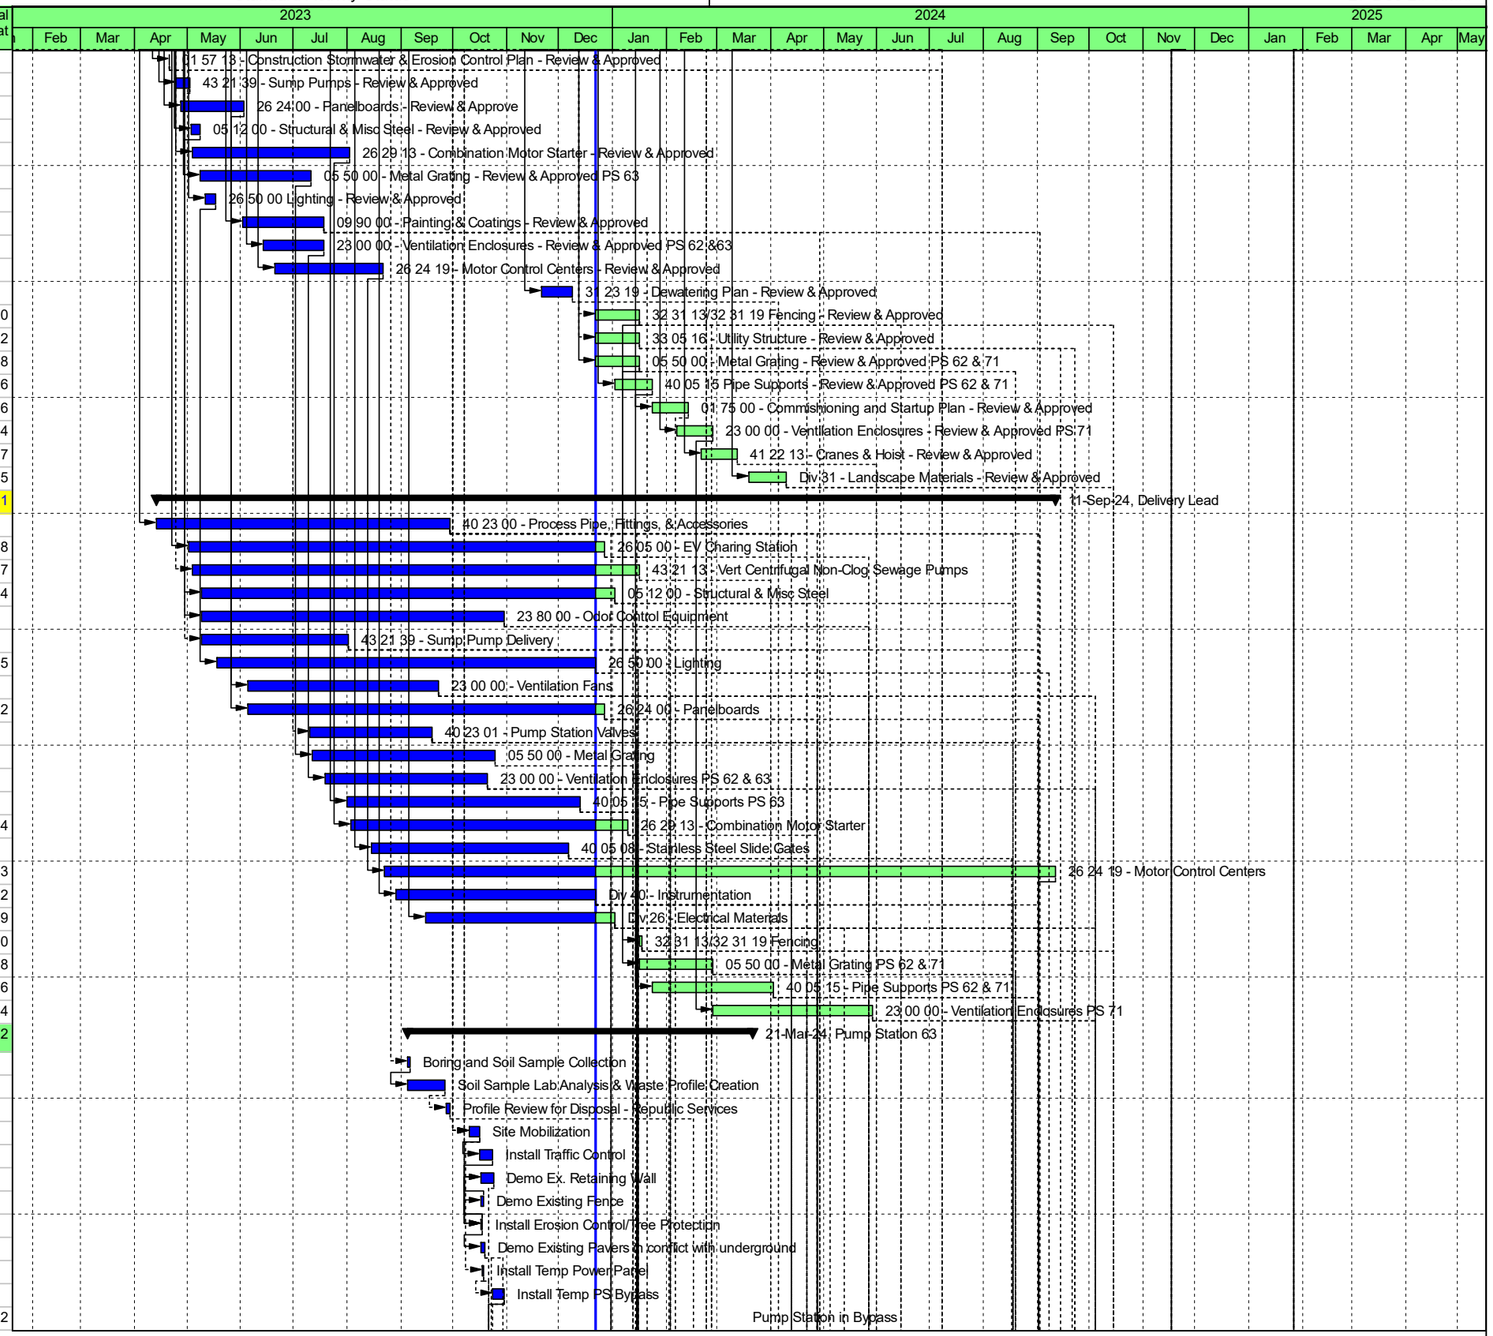

© Oracle Corporation

Activity ID	Activity Name	Original Duration	naining Duration	Start	Finish	Total Float
A2640	Demo Existing Electrical	2	0	31-Oct-23 A	02-Nov-23	
A2710	Demo Existing Sidewalk, Curb, Asphalt in conflict wi	2	0	01-Nov-23 A	07-Nov-23	
A3520	Telecommunication Demo inside Drywell	1	0	02-Nov-23 A	02-Nov-23	
A2650	Lead Abatement of Existing Coatings	3	0	06-Nov-23 A	09-Nov-23	
A2750	Excavate to top of PS for Ex FM Demo (Contaminat	1	0	08-Nov-23 A	09-Nov-23	
A2730	Demo Ex FM, including Plugs, and MH Rechannel (I	1	0	13-Nov-23 A	12-Dec-23	
A2680	Salvage Existing Pumps	1	0	20-Nov-23 A	21-Nov-23	
A2770	Install 6" PS (FM) & Backfill Trench	5	0	22-Nov-23 A	11-Dec-23	
A3740	Lead Abatement Dry Well Piping	3	0	11-Dec-23 A	14-Dec-23	
A3770	Trench Compaction Test	1	0	12-Dec-23 A	12-Dec-23	
A3780	Plan & Execute Support of Unknown Concrete Duct	8	3	14-Dec-23 A	28-Dec-23	2
A2660	Demo Existing Mechanical	1	0	18-Dec-23 A	19-Dec-23	
A3750	Lead Abatement Wet Well	1	0	18-Dec-23 A	19-Dec-23	
A2670	Demo Grating & Ladder	2	2	26-Dec-23	27-Dec-23	21
A3840	Demo & Form Pump Pads (Includes Cure)	5	5	26-Dec-23	03-Jan-24	5
A3760	Expand PS Excavation for Pipe Penetration Slab	2	2	27-Dec-23	28-Dec-23	2
A3790	Core Drill PS Penetrations and Remove Existing Sle	2	2	02-Jan-24	03-Jan-24	2
A3800	Install FM, HVAC, and Condutis through PS Lid Pen	2	2	03-Jan-24	08-Jan-24	2
A2700	Install Pump Intake Replacement	2	2	08-Jan-24	09-Jan-24	2
A2840	Penetration Support Slabs	2	2	08-Jan-24	09-Jan-24	4
A2720	Set Salvaged Pumps	1	1	09-Jan-24	10-Jan-24	2
A2760	Install Interior Forcemain to Roof Penetration	8	8	09-Jan-24	24-Jan-24	9
A3810	Cure Pipe Penetration Slab	4	4	09-Jan-24	13-Jan-24	9
A3310	Rough-In Electrical	8	8	10-Jan-24	25-Jan-24	2
A2920	Backfill Pipe Penetration Slab	1	1	16-Jan-24	16-Jan-24	3
A2870	Install 4" Prop Wet Well Supply and Exhaust Duct	3	3	16-Jan-24	22-Jan-24	3
A2860	Prep Subgrade for Retaining Wall	1	1	16-Jan-24	17-Jan-24	18
A2960	CIP Retaining Wall	2	2	17-Jan-24	22-Jan-24	18
A2790	Install Steel Framing/Grating/Ladders	3	3	22-Jan-24	25-Jan-24	9
A2900	Install Drain from Odor Control Unit to PS	1	1	23-Jan-24	23-Jan-24	3
A2980	Install Water Service/RPBA/Hose Bib	2	2	23-Jan-24	24-Jan-24	7
A2910	Site Electrical Conduit/Handhole Install	4	4	23-Jan-24	30-Jan-24	3
A2810	Set Electrical Panels	2	2	24-Jan-24	25-Jan-24	2
A3820	RPBA Inspection by SPU Cross Connections	1	1	24-Jan-24	25-Jan-24	28
A2800	Install Interior Ventilation Ductwork to Roof Penetrati	1	1	24-Jan-24	25-Jan-24	11
A3690	6" FM Hydrostatic & Leakage Test	1	1	24-Jan-24	25-Jan-24	15
A2820	Install Sump Pump & Discharge Line	1	1	25-Jan-24	29-Jan-24	9
A2830	Install Slide Gate in Wet Well	2	2	25-Jan-24	30-Jan-24	13
A2890	Electrical Wire Pulling & Connections	12	12	25-Jan-24	15-Feb-24	2
A2880	Install Lighting	2	2	25-Jan-24	31-Jan-24	2
A2930	Install Interior Drain Line from Odor Control	1	1	29-Jan-24	30-Jan-24	9
A2850	Painting in PS	4	4	30-Jan-24	06-Feb-24	9
A2940	CIP Odor Control Pad	2	2	30-Jan-24	05-Feb-24	4
A2950	CIP Wet Well Supply Fan Pad	2	2	30-Jan-24	05-Feb-24	4
A2970	CIP Top Access Hatch Panel	3	3	30-Jan-24	05-Feb-24	3
A3010	CIP EV Charging Station Base	2	2	30-Jan-24	05-Feb-24	4
A3530	Demo Ex Lumen Ped, and Install new Lumen HH	1	1	30-Jan-24	31-Jan-24	12
A3830	Cure CIP Pads	4	4	05-Feb-24	09-Feb-24	6
A2990	Install Odor Control Unit	1	1	12-Feb-24	12-Feb-24	3
A3000	Install Wet Well Supply Fan & Enclosure	2	2	12-Feb-24	15-Feb-24	3
A3020	Install EV Charging Station	2	2	12-Feb-24	14-Feb-24	4
A3030	Prep Concrete Pavement/Sidewalk/Parking Area/Ro	4	4	15-Feb-24	26-Feb-24	3
A3070	Equipment Acceptance Testing	2	2	15-Feb-24	22-Feb-24	1
A3550	Systems Acceptance Testing	2	2	22-Feb-24	29-Feb-24	1
A3040	Concrete Sidewalk, Paver Base & Curb	2	2	26-Feb-24	28-Feb-24	3
A3320	Grind Existing Pavement/Pave Asphalt	1	1	28-Feb-24	29-Feb-24	9

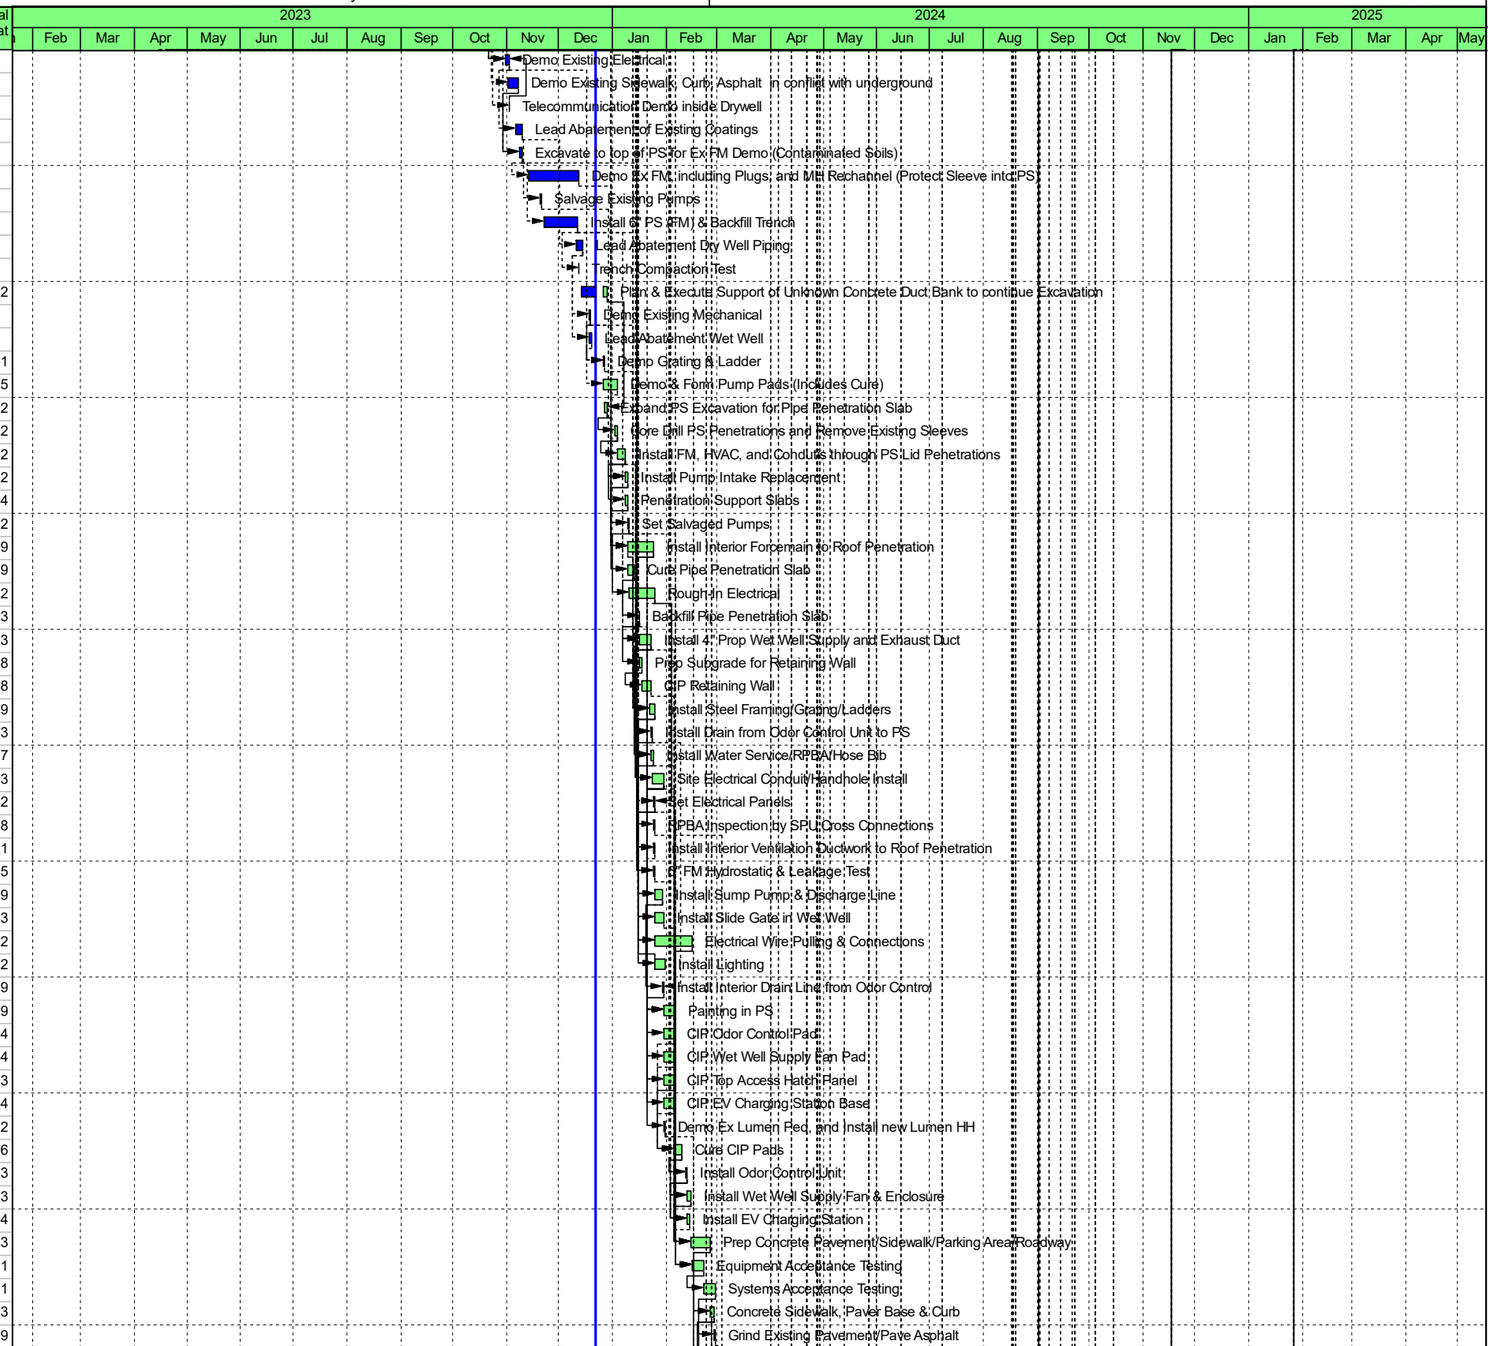

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	naining Duration	Start	Finish	Total Float
A3060	Install Architectual Pavers	5	5	28-Feb-24	07-Mar-24	3
A3680	Control Center Acceptance Testing	2	2	29-Feb-24	06-Mar-24	1
A3610	Operational Acceptance Testing	7	7	06-Mar-24	13-Mar-24	5
A3050	Install Fence & Arch Fence Panels	2	2	07-Mar-24	11-Mar-24	3
A3080	Site Acceptance of PS 63	1	1	13-Mar-24	14-Mar-24	2
A3090	Demo Sewer Bypass	2	2	14-Mar-24	19-Mar-24	2
A3330	Site Punchlist/Demob	4	4	14-Mar-24	21-Mar-24	173
Pump Station 62		166	166	21-Feb-24	15-Oct-24	78
A3650	Schedule SCL Service Connection (3-12 Weeks)	0	0	21-Feb-24		190
A2030	Site Mobilization	4	4	26-Feb-24	04-Mar-24	8
A2040	Install Erosion Control	1	1	04-Mar-24	04-Mar-24	8
A2070	Demo Ex. Site Materials (Bug Machine, Signage, RF	2	2	05-Mar-24	06-Mar-24	8
A2090	Install Temp Power Panel	1	1	06-Mar-24	07-Mar-24	8
A2130	Install Temp PS Bypass	2	2	19-Mar-24	25-Mar-24	2
A2150	Pump Station in Bypass	59	59	25-Mar-24	09-Jul-24	5
A2170	Lead Abatement of Existing Coatings	2	2	25-Mar-24	27-Mar-24	2
A2080	Demo Ex Hatch and Top Slap	2	2	27-Mar-24	01-Apr-24	2
A2180	Demo Existing Mechanical	2	2	01-Apr-24	03-Apr-24	2
A2160	Demo Existing Electrical	2	2	01-Apr-24	02-Apr-24	3
A2190	Demo Grating & Ladder	2	2	03-Apr-24	08-Apr-24	2
A2200	Demo Existing Pumps	1	1	08-Apr-24	08-Apr-24	2
A2050	Clear & Grub	1	1	08-Apr-24	09-Apr-24	2
A2210	Install Pump Intake Replacement	2	2	08-Apr-24	10-Apr-24	5
A2060	Demo Ex Sidewalk	2	2	09-Apr-24	11-Apr-24	2
A2220	Set New Pumps	3	3	10-Apr-24	16-Apr-24	5
A2110	Cut/Cap Existing Service	1	1	11-Apr-24	15-Apr-24	2
A2100	Install Dewatering Well & System	4	4	15-Apr-24	22-Apr-24	2
A2140	Excavate to top of PS	1	1	22-Apr-24	22-Apr-24	2
A2240	Install Interior Forcemain through Roof Penetration	8	8	22-Apr-24	06-May-24	2
A2320	Excavate/Install/Backfill 8 PS Line from MH to PS	2	2	22-Apr-24	25-Apr-24	8
A2330	Reconnect Ex 6" FM	1	1	25-Apr-24	29-Apr-24	8
A2250	Install Steel Framing/Grating/Ladders	3	3	01-May-24	07-May-24	2
A2270	Install Interior Ventilation Ductwork Through Roof Pe	1	1	07-May-24	08-May-24	2
A2260	Set Electrical Panels	4	4	07-May-24	14-May-24	2
A2280	Install Sump Pump & Discharge Line	1	1	07-May-24	08-May-24	15
A2230	Install Slide Gate in Wet Well	2	2	08-May-24	13-May-24	12
A2290	Penetration Support Slabs	2	2	08-May-24	13-May-24	2
A2300	Painting in PS	4	4	08-May-24	15-May-24	15
A2350	Complete FM & Drain to bypass Vault	1	1	13-May-24	13-May-24	12
A2360	Install 4" Prop Wet Well Supply and Exhaust Duct	5	5	13-May-24	20-May-24	2
A2340	Install Lighting	2	2	14-May-24	20-May-24	2
A2310	Electrical Raceways & Wire Pulling	12	12	20-May-24	11-Jun-24	2
A2550	Install Drain from Odor Control Unit to PS	2	2	20-May-24	22-May-24	2
A2370	Site Electrical Conduit Install	4	4	22-May-24	30-May-24	2
A2520	Backfill Top of PS to top hatches	2	2	30-May-24	04-Jun-24	2
A2380	CIP Electrical Cabinet Pad	2	2	04-Jun-24	05-Jun-24	3
A2390	CIP Odor Control Pad	2	2	04-Jun-24	05-Jun-24	3
A2400	CIP Wet Well Supply Fan Pad	2	2	04-Jun-24	05-Jun-24	2
A2530	Set Bypass Vault	1	1	04-Jun-24	04-Jun-24	13
A2540	CIP Top Access Hatch Panel	3	3	04-Jun-24	10-Jun-24	11
A2560	Install Water Service to reset Meter	1	1	04-Jun-24	04-Jun-24	13
A2410	Install Odor Control Unit	2	2	05-Jun-24	10-Jun-24	3
A2420	Install Wet Well Supply Fan & Enclosure	2	2	05-Jun-24	11-Jun-24	2
A2440	Install Electrical Service Cabinet	1	1	05-Jun-24	06-Jun-24	3
A2510	Install EV Charging Station	2	2	05-Jun-24	10-Jun-24	3

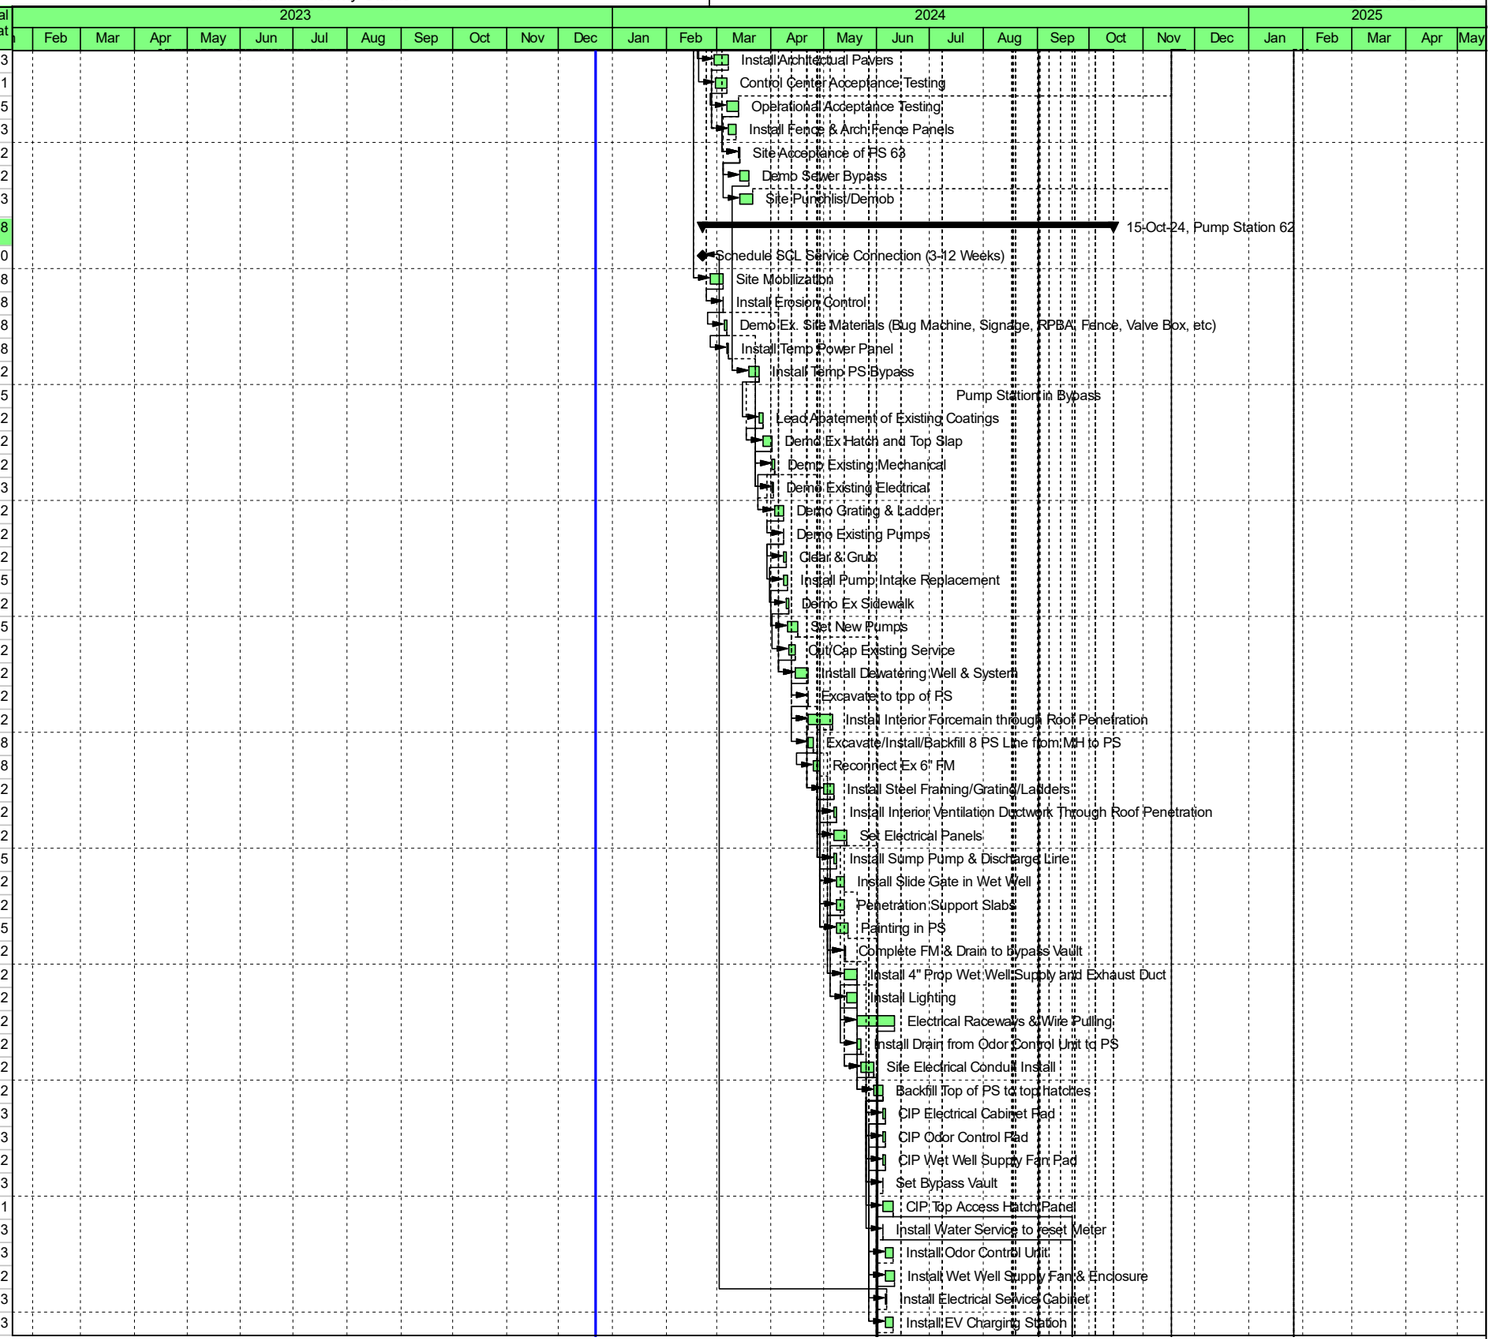

© Oracle Corporation

Activity ID	Activity Name	Original Duration	naining Duration	Start	Finish	Total Float
A2430	Prep Concrete Pavement/Sidewalk/Parking Area	5	5	10-Jun-24	18-Jun-24	11
A2480	Equipment Acceptance Testing	2	2	11-Jun-24	13-Jun-24	2
A3710	Systems Acceptance Testing	2	2	13-Jun-24	26-Jun-24	2
A2450	Concrete Pavement, Sidewalk, Curb	2	2	18-Jun-24	24-Jun-24	11
A2460	Install Fence	2	2	24-Jun-24	26-Jun-24	11
A3700	Control Center Acceptance Testing	2	2	26-Jun-24	02-Jul-24	2
A3620	Operational Acceptance Testing	7	7	02-Jul-24	08-Jul-24	8
A2490	Site Acceptance of PS 62	1	1	09-Jul-24	09-Jul-24	5
A2500	Demo Sewer Bypass	2	2	09-Jul-24	11-Jul-24	5
A2740	Punchlist/Demob	4	4	09-Jul-24	16-Jul-24	110
A2470	Landscaping	8	8	01-Oct-24	15-Oct-24	60
Pump Station 71		110	110	26-Jun-24	02-Dec-24	44
A3640	Schedule SCL Service Connection (3-12 Weeks)	0	0	26-Jun-24		121
A1000	Site Mobilization	4	4	11-Jul-24	18-Jul-24	5
A1010	Install Erosion Control	1	1	18-Jul-24	22-Jul-24	5
A1450	Civil Demo (Bench, Guardrail, Etc)	1	1	22-Jul-24	22-Jul-24	5
A1020	Clear & Grub	2	2	23-Jul-24	24-Jul-24	5
A1030	Demo Asphalt Pavement/Concrete	2	2	24-Jul-24	29-Jul-24	5
A1060	Install Temp Power Panel	1	1	24-Jul-24	25-Jul-24	8
A1120	Salvage Existing Dry Well Hatch	1	1	29-Jul-24	29-Jul-24	5
A1460	Cut/Cap Existing Service	1	1	29-Jul-24	29-Jul-24	5
A1530	Install 1" Water Service	2	2	30-Jul-24	31-Jul-24	5
A1070	Install Temp PS Bypass	2	2	31-Jul-24	05-Aug-24	5
A1040	Excavate to top of PS	1	1	06-Aug-24	06-Aug-24	11
A1080	Pump Station in Bypass	59	59	06-Aug-24	20-Nov-24	5
A1100	Demo Existing Electrical	2	2	06-Aug-24	07-Aug-24	5
A3660	Excavation Dewatering	25	25	06-Aug-24	18-Sep-24	5
A3540	Telecommunication Demo	1	1	06-Aug-24	06-Aug-24	6
A1050	Demo Concrete Riser of PS	1	1	06-Aug-24	07-Aug-24	11
A1380	Lead Abatement of Existing Coatings	2	2	07-Aug-24	12-Aug-24	5
A1090	Demo Existing Mechanical	2	2	13-Aug-24	15-Aug-24	5
A1390	Demo Grating & Ladder	1	1	15-Aug-24	19-Aug-24	5
A1110	Salvage Existing Pumps	1	1	19-Aug-24	19-Aug-24	5
A1440	Install Pump Intake Replacement	2	2	20-Aug-24	21-Aug-24	7
A1510	Cast-In-Place Hatch Curb	4	4	20-Aug-24	26-Aug-24	5
A1400	Set Salvaged Pumps	1	1	27-Aug-24	27-Aug-24	5
A1490	Install Slide Gate in Wet Well	2	2	27-Aug-24	28-Aug-24	43
A1410	Install Interior Forcemain through Roof Penetration	8	8	27-Aug-24	11-Sep-24	5
A1430	Install Grating/Ladders/MCC Support	2	2	29-Aug-24	04-Sep-24	9
A1420	Install Interior Ventilation Ductwork Through Roof Pe	1	1	11-Sep-24	12-Sep-24	5
A1480	Install Sump Pump & Discharge Line	1	1	11-Sep-24	12-Sep-24	35
A1470	Set Electrical Panels	2	2	11-Sep-24	17-Sep-24	18
A1500	Penetration Support Slabs	2	2	12-Sep-24	17-Sep-24	5
A1740	Painting in PS	4	4	12-Sep-24	19-Sep-24	43
A1520	Backfill Excavation at PS	2	2	17-Sep-24	18-Sep-24	5
A2120	Install Lighting	2	2	17-Sep-24	19-Sep-24	18
A1570	Re-Install Salvaged Hatch	1	1	18-Sep-24	18-Sep-24	5
A1540	Install 4" FM from PS to MH 300-010	2	2	18-Sep-24	24-Sep-24	5
A1620	Install CB & 8" Drain Line	2	2	24-Sep-24	26-Sep-24	5
A1550	Install 4" Wet Well Supply Duct	2	2	26-Sep-24	01-Oct-24	5
A1560	Install 4" Wet Well Exhaust Duct	2	2	01-Oct-24	02-Oct-24	5
A1590	Site Electrical Conduit Install	4	4	02-Oct-24	09-Oct-24	5
A1630	Adjust JB Rim & Replace Grate	1	1	02-Oct-24	03-Oct-24	16
A1580	CIP Electrical Cabinet Pad	2	2	09-Oct-24	14-Oct-24	5
A1600	CIP Odor Control Pad	2	2	09-Oct-24	14-Oct-24	11

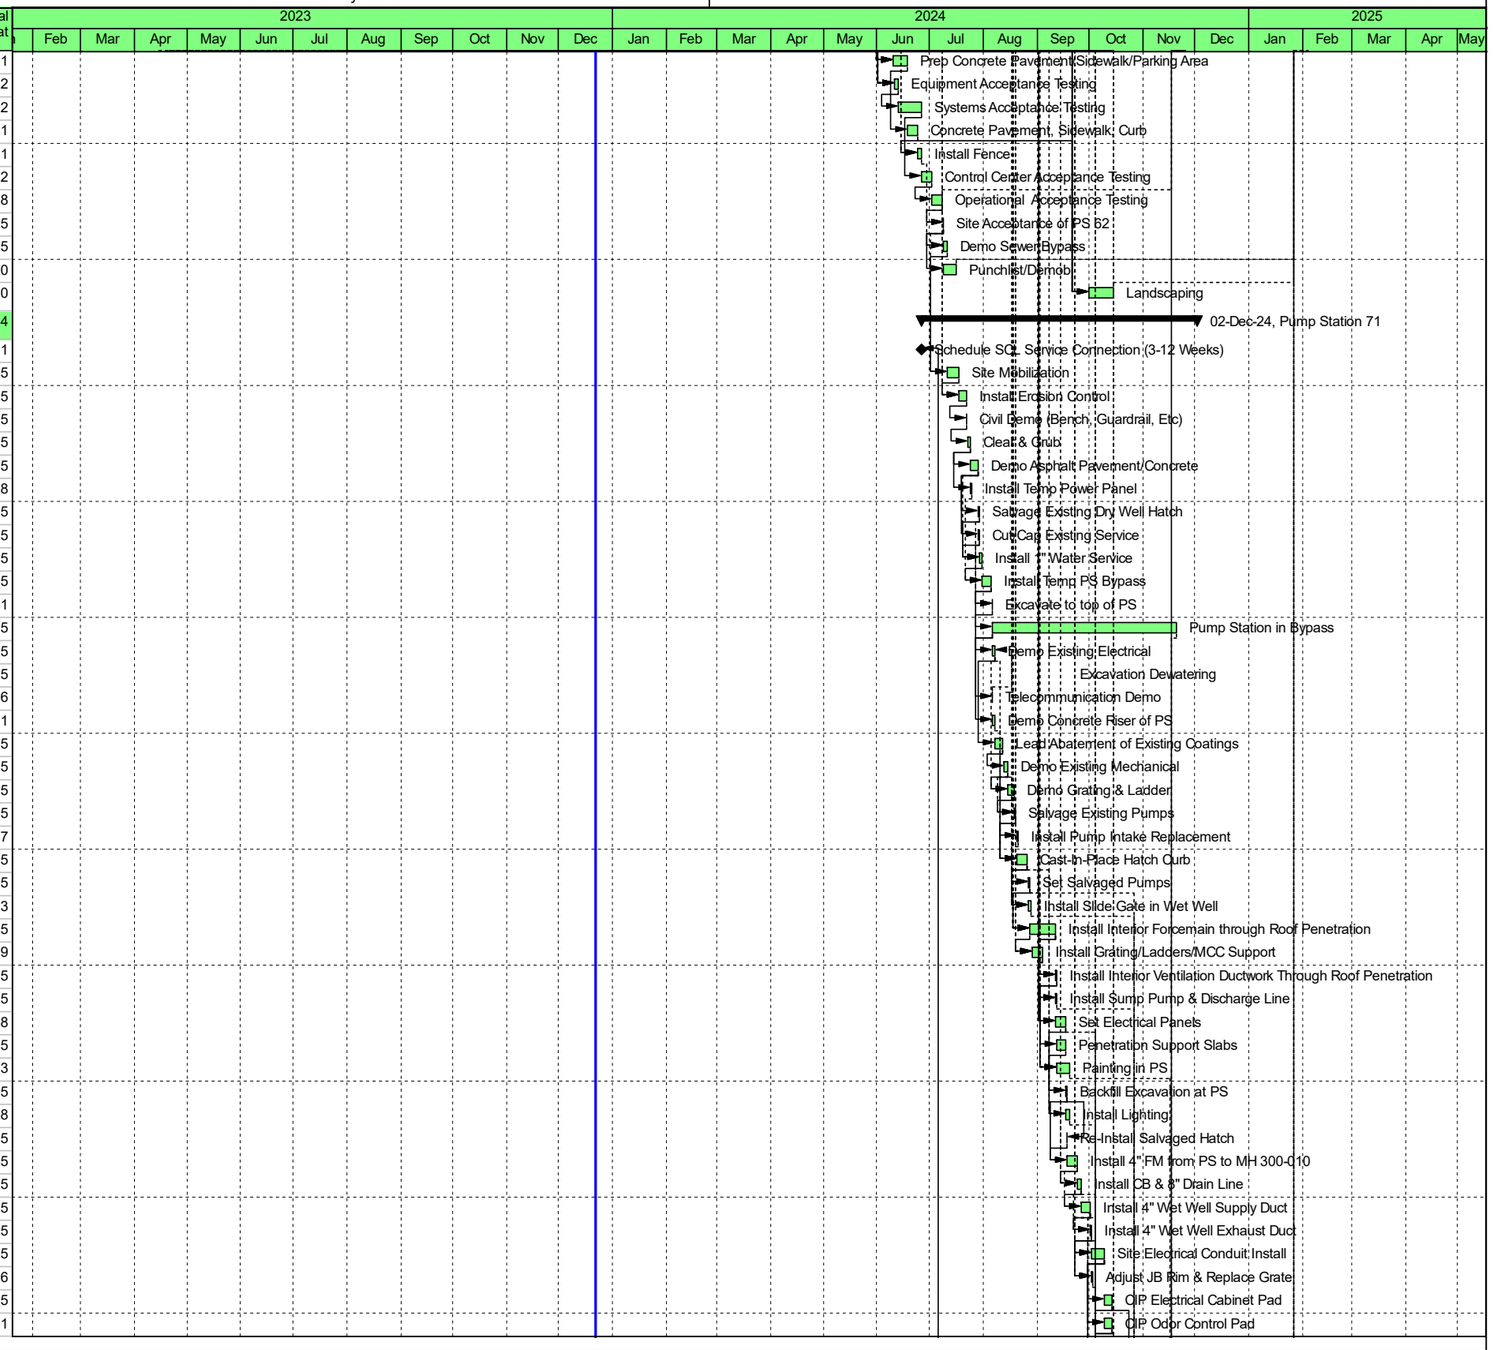

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	naining Duration	Start	Finish	Total Float
A1610	CIP Wet Well Supply Fan Pad	2	2	09-Oct-24	14-Oct-24	11
A1710	Install Electrical Service Cabinet	1	1	10-Oct-24	14-Oct-24	5
A1640	Prep Concrete Pavement/Sidewalk/Parking Area	5	5	14-Oct-24	22-Oct-24	11
A1690	Electrical Raceways & Wire Pulling	12	12	14-Oct-24	04-Nov-24	5
A1720	Install Exhaust Fan and Enclosure	2	2	14-Oct-24	16-Oct-24	16
A1730	Install Wet Well Supply Fan & Enclosure	2	2	14-Oct-24	16-Oct-24	15
A1680	Concrete Pavement, Sidewalk, Curb	2	2	22-Oct-24	24-Oct-24	11
A1650	Install Fence	2	2	24-Oct-24	29-Oct-24	22
A1660	Install Bench	1	1	24-Oct-24	28-Oct-24	23
A1670	Landscaping	12	12	24-Oct-24	18-Nov-24	11
A3670	Telecommunication Install	1	1	04-Nov-24	05-Nov-24	5
A1700	Equipment Acceptance Testing	2	2	05-Nov-24	07-Nov-24	4
A3720	Systems Acceptance Testing	2	2	07-Nov-24	14-Nov-24	4
A3730	Control Center Acceptance Testing	1	1	14-Nov-24	19-Nov-24	4
A3630	Operational Acceptance Testing	7	7	19-Nov-24	26-Nov-24	14
A1760	Site Acceptance of PS 71	1	1	26-Nov-24	26-Nov-24	7
A1750	Demo Sewer Bypass	2	2	27-Nov-24	02-Dec-24	34
Project Closeout		29	29	27-Nov-24	22-Jan-25	7
A3580	Punchlist/Demob	12	12	27-Nov-24	18-Dec-24	7
A3600	Project Closeout Paperwork	17	17	19-Dec-24	22-Jan-25	7

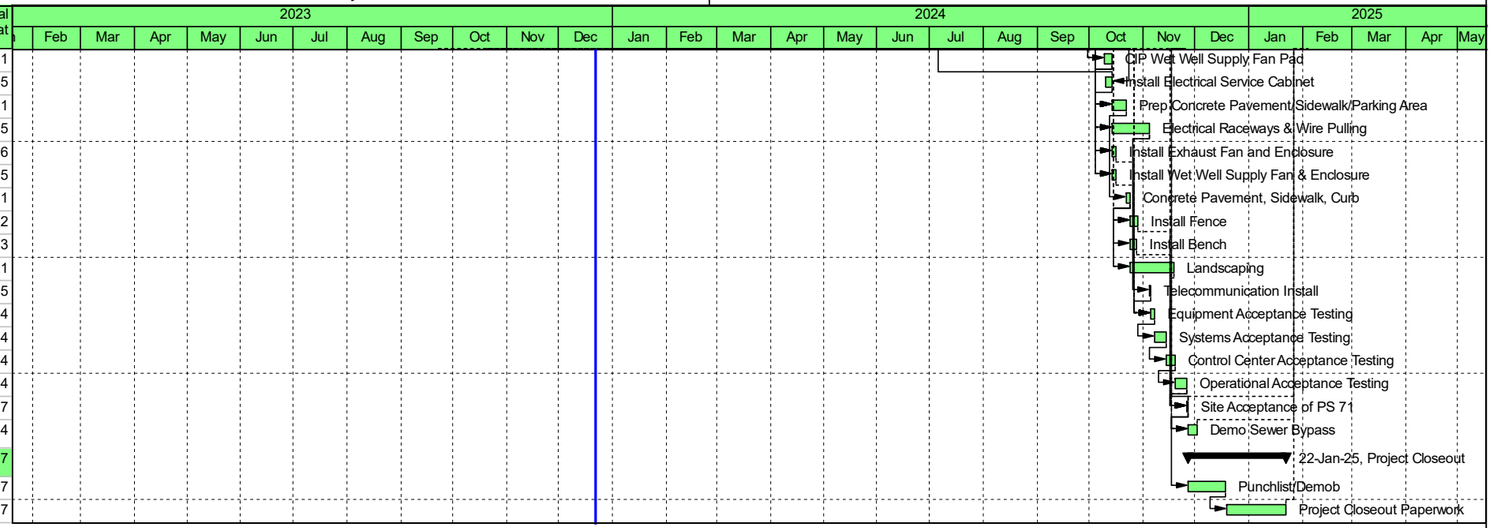

© Oracle Corporation
