Data Date: 31-December-23

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float
23009 Port Orchard Marina Pump Station_Update 2_December 2023		483	422	18-Sep-23 A	25-Aug-25	0
Project Milestones		422	21	02-Oct-23 A	25-Aug-25	0
A1000	Notice to Proceed	0	0	02-Oct-23 A		
A1010	SJC Substantial Completion	0	0		25-Jul-25	0
A1240	Contract Substantial Completion	0	0		25-Jul-25*	0
A1020	Punchlist	20	20	28-Jul-25	22-Aug-25	0
A1030	Project Closeout	20	20	28-Jul-25	22-Aug-25	0
A1040	SJC Physical Completion	0	0		22-Aug-25	0
A1400	Contract Physical Completion	1	1	25-Aug-25	25-Aug-25*	0
Major Submittals and Procurement		311	250	18-Sep-23 A	20-Dec-24	172
Submittal Prep		191	130	18-Sep-23 A	02-Jul-24	262
A1180	Submittal Prep- Division 15 Ductile Iron Pipe/Fittings	10	0	18-Sep-23 A	25-Sep-23 A	
A1190	Submittap Prep-Division 15 Gate Valves	10	0	18-Sep-23 A	25-Sep-23 A	
A1260	Submittal Prep-2.20 Earthwork Materials	10	0	20-Sep-23 A	26-Sep-23 A	
A1470	Submittal Prep-Division 15 PVC Pipe/Fittings	10	0	20-Sep-23 A	25-Sep-23 A	
A1110	Submittal Prep-11.12.20 Emergency Diesel-Driven Sewage Pump	10	0	29-Sep-23 A	29-Sep-23 A	
A1050	Submittal Prep- Temporary Sewer Bypass	20	20	02-Oct-23 A	29-Jan-24	74
A1060	Submittal Prep-Concrete Ready Mix	10	0	02-Oct-23 A	23-Oct-23 A	
A1070	Submittal Prep-Concrete Reinforcement	15	0	02-Oct-23 A	26-Oct-23 A	
A1080	Submittal Prep-Precast Structures	30	0	02-Oct-23 A	23-Oct-23 A	
A1090	Submittal Prep-11.12.10 Sump Pump	20	10	02-Oct-23 A	15-Jan-24	275
A1100	Submittal Prep-11.12.20 Dry Pit Sewage Pump	20	0	02-Oct-23 A	20-Oct-23 A	
A1120	Submittal Prep-11.12.23 Emergency Storage Sewage Sump Pump and Motor	10	0	02-Oct-23 A	10-Oct-23 A	
A1130	Submittal Prep-11.96 Odor Control System	15	0	02-Oct-23 A	16-Nov-23 A	
A1140	Submittal Prep-11.95 HVAC	40	0	02-Oct-23 A	04-Dec-23 A	
A1150	Submittal Prep-Divison 15 Knife Gate Valves	10	0	02-Oct-23 A	24-Oct-23 A	
A1160	Submittal Prep-13.63 Rehabilitation of Wetwell	20	10	02-Oct-23 A	15-Jan-24	382
A1170	Submittal Prep-14.41.13 Bridge Crane	10	0	02-Oct-23 A	17-Oct-23 A	
A1200	Submittal Prep-Division 15 Check Valves	10	0	02-Oct-23 A	03-Nov-23 A	
A1210	Submittal Prep-Division 15 Plug Valves	10	0	02-Oct-23 A	04-Dec-23 A	
A1220	Submittal Prep-15.50 Flow Meters	10	0	02-Oct-23 A	30-Oct-23 A	
A1230	Submittal Prep-15.70 Plumbing	20	20	02-Oct-23 A	29-Jan-24	66
A1250	Submittal Prep-2.10 Dewatering	10	0	02-Oct-23 A	20-Oct-23 A	
A1270	Submittal Prep-2.30 Asphalt Paving	10	10	02-Oct-23 A	15-Jan-24	371
A1280	Submittal Prep-2.50 Excavation Support and Calculations	15	0	02-Oct-23 A	20-Nov-23 A	
A1290	Submittal Prep-4.22 CMU	10	10	02-Oct-23 A	15-Jan-24	156
A1300	Submittal Prep-4.22 CMU Rebar	10	10	02-Oct-23 A	15-Jan-24	156
A1310	Submittal Prep-5.00 Structural Steel and Fabricated Metals	40	20	02-Oct-23 A	29-Jan-24	127
A1320	Submittal Prep-5.30 Metal Decking	20	0	02-Oct-23 A	04-Dec-23 A	
A1330	Submittal Prep-6.70 FRP Package Supply	20	10	02-Oct-23 A	15-Jan-24	116
A1340	Submittal Prep-7.60 Flashing and Sheet Metal	20	10	02-Oct-23 A	15-Jan-24	273
A1350	Submittal Prep-7.40 Roofing and Siding Panels	30	10	02-Oct-23 A	15-Jan-24	156
A1360	Submittal Prep-8.10 HM Doors and Frames	30	10	02-Oct-23 A	15-Jan-24	312
A1370	Submittal Prep-8.90 Louvers and Vents	40	0	02-Oct-23 A	04-Dec-23 A	
A1380	Submittal Prep-9.90 Painting and Coatings	20	0	02-Oct-23 A	02-Nov-23 A	
A1390	Submittal Prep-Division 15 Stainless Steel Pipe/Fittings	10	10	02-Oct-23 A	15-Jan-24	312
A1410	Submittal Prep-16.40 Low Voltage Motor Control Equipment/Electrical Gear	30	0	02-Oct-23 A	13-Dec-23 A	
A1420	Submittal Prep-16.50 Panelboards/VFD'S	60	0	02-Oct-23 A	20-Nov-23 A	
A1430	Submittal Prep-16.60 Conductors	30	0	02-Oct-23 A	09-Oct-23 A	
A1440	Submittal Prep-16.70 Raceways, Boxes, and Fittings	30	0	02-Oct-23 A	31-Oct-23 A	
A1450	Submittal Prep-16.85 Lighting	20	0	02-Oct-23 A	16-Oct-23 A	
A1460	Submittal Prep-16.90 Power Generation	30	0	02-Oct-23 A	09-Oct-23 A	
A1480	Submittal Prep-Controls/Instrumentation	60	0	02-Oct-23 A	30-Oct-23 A	
A1490	Submittal Prep-Fire Alarm	30	0	02-Oct-23 A	06-Nov-23 A	
A1500	Submittal Prep-Arc/Flash Study	130	130	02-Oct-23 A	02-Jul-24	252
Submittal Review and Approval		180	140	25-Sep-23 A	17-Jul-24	262
A1640	Submittal Review/Approval- Division 15 Ductile Iron Pipe/Fittings	10	0	25-Sep-23 A	04-Oct-23 A	
A1650	Submittal Review/Approval-Division 15 Gate Valves	10	0	25-Sep-23 A	27-Oct-23 A	
A3430	Submittal Review/Approval-Division 15 PVC Pipe/Fittings	10	0	25-Sep-23 A	27-Oct-23 A	
A1720	Submittal Review/Approval-2.20 Earthwork Materials	10	0	26-Sep-23 A	11-Oct-23 A	
A1570	Submittal Review/Approval-11.12.20 Emergency Diesel-Driven Sewage Pump	10	10	29-Sep-23 A	15-Jan-24	106
A1880	Submittal Review/Approval-16.60 Conductors	10	0	09-Oct-23 A	15-Dec-23 A	
A1910	Submittal Review/Approval-16.90 Power Generation	10	10	09-Oct-23 A	15-Jan-24	181
A1580	Submittal Review/Approval-11.12.23 Emergency Storage Sewage Sump Pump and Motor	10	0	10-Oct-23 A	07-Nov-23 A	
A1900	Submittal Review/Approval-16.85 Lighting	10	0	16-Oct-23 A	12-Dec-23 A	
A1630	Submittal Review/Approval-14.41.13 Bridge Crane	10	10	17-Oct-23 A	15-Jan-24	62
A1560	Submittal Review/Approval-11.12.20 Dry Pit Sewage Pump	10	0	20-Oct-23 A	05-Dec-23 A	
A1710	Submittal Review/Approval-2.10 Dewatering	10	0	20-Oct-23 A	27-Dec-23 A	
A1520	Submittal Review/Approval-Concrete Ready Mix	10	0	23-Oct-23 A	07-Nov-23 A	
A1540	Submittal Review/Approval-Precast Structures	10	0	23-Oct-23 A	06-Dec-23 A	
A1610	Submittal Review/Approval-Divison 15 Knife Gate Valves	10	0	24-Oct-23 A	03-Nov-23 A	
A1530	Submittal Review/Approval-Concrete Reinforcement	10	10	26-Oct-23 A	15-Jan-24	9
A1680	Submittal Review/Approval-15.50 Flow Meters	10	10	30-Oct-23 A	15-Jan-24	271
A2380	Submittal Review/Approval-Controls/Instrumentation	10	10	30-Oct-23 A	15-Jan-24	90
A1890	Submittal Review/Approval-16.70 Raceways, Boxes, and Fittings	10	10	31-Oct-23 A	15-Jan-24	200
A1840	Submittal Review/Approval-9.90 Painting and Coatings	10	10	03-Nov-23 A	15-Jan-24	152

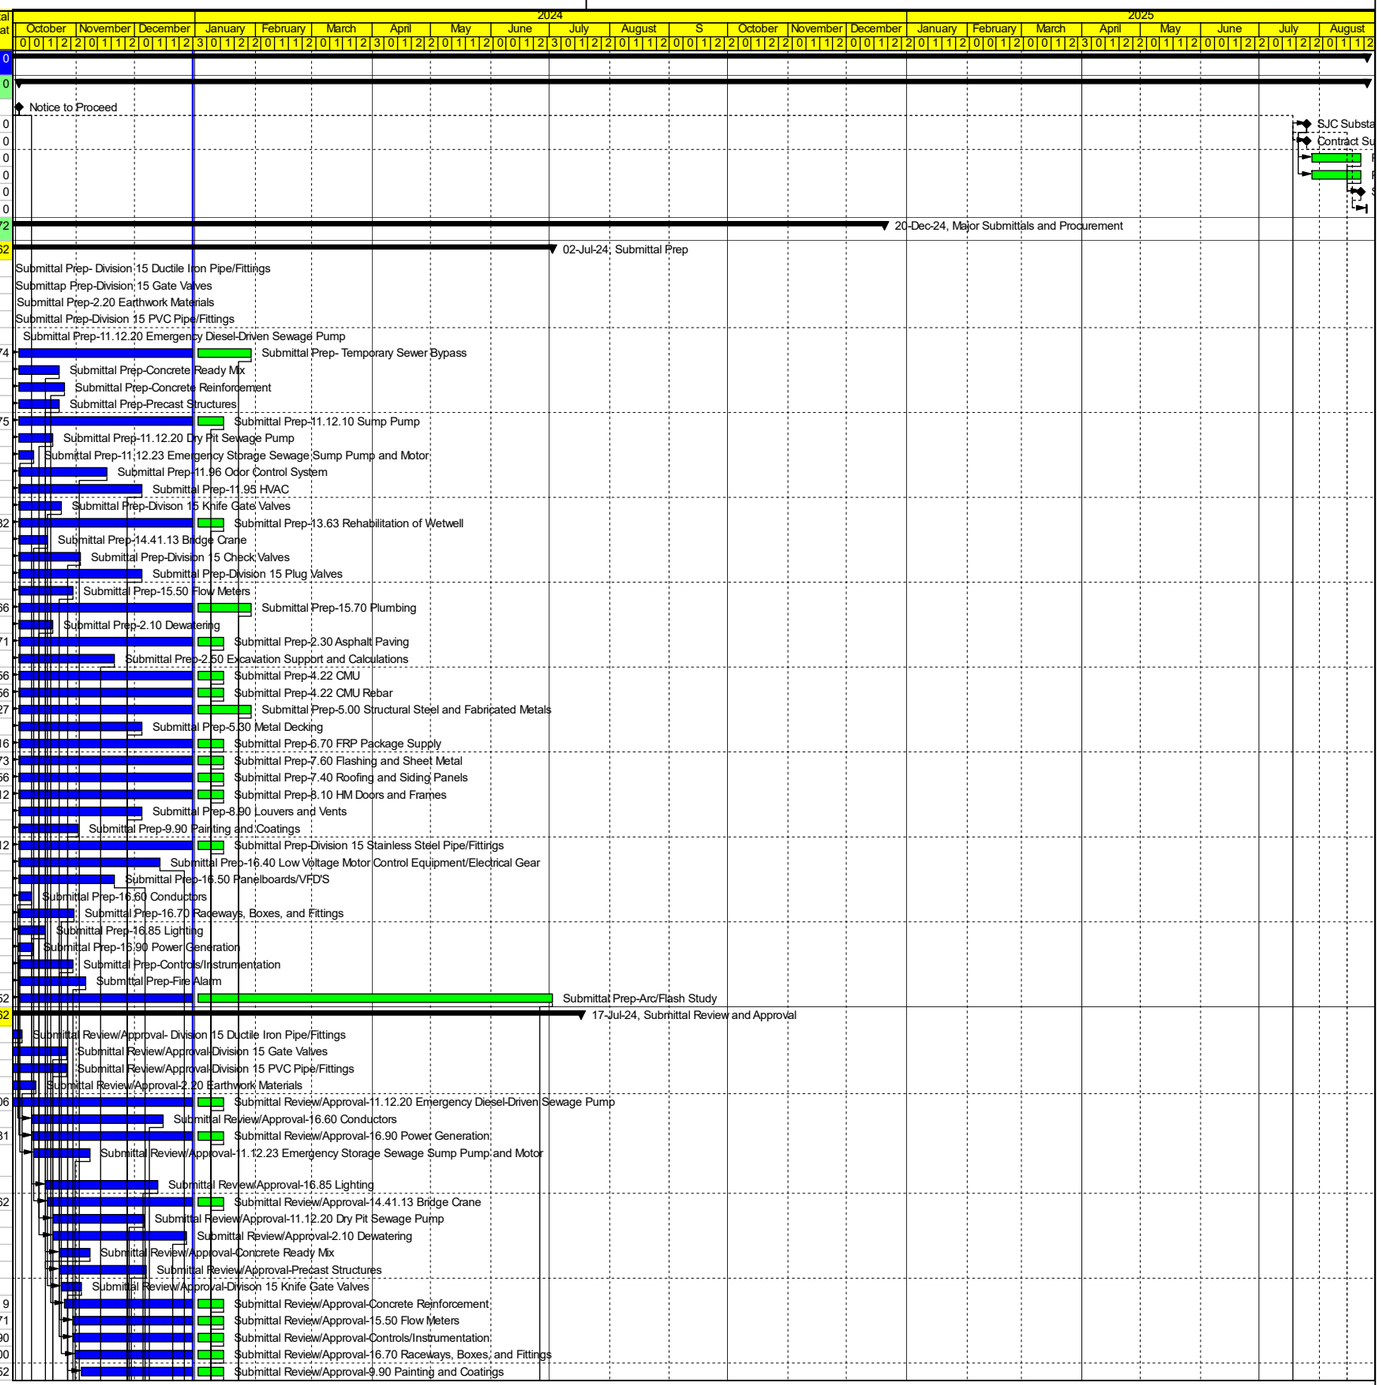

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Stellar J Corporation
23009 Port Orchard Marina Pump Station_Update 2 _December 2023

Data Date: 31-December-23

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float
A1660	Submittal Review/Approval-Division 15 Check Valves	10	0	03-Nov-23 A	13-Nov-23 A	
A2400	Submittal Review/Approval-Fire Alarm	10	10	06-Nov-23 A	15-Jan-24	200
A1590	Submittal Review/Approval-11.96 Odor Control System	10	10	09-Nov-23 A	15-Jan-24	126
A1740	Submittal Review/Approval-2.50 Excavation Support and Calculations	10	5	20-Nov-23 A	08-Jan-24	2
A1600	Submittal Review/Approval-11.95 HVAC	10	10	04-Dec-23 A	15-Jan-24	136
A1670	Submittal Review/Approval-Division 15 Plug Valves	10	0	04-Dec-23 A	15-Dec-23 A	
A1780	Submittal Review/Approval-5.30 Metal Decking	10	0	04-Dec-23 A	27-Dec-23 A	
A1830	Submittal Review/Approval-8.90 Louvers and Vents	10	10	04-Dec-23 A	15-Jan-24	123
A1870	Submittal Review/Approval-16.50 Panelboards/VFD	10	10	13-Dec-23 A	15-Jan-24	60
A1860	Submittal Review/Approval-16.40 Low Voltage Motor Control Equipment	10	10	02-Jan-24	15-Jan-24	50
A1550	Submittal Review/Approval-11.12.10 Sump Pump	10	10	16-Jan-24	29-Jan-24	275
A1620	Submittal Review/Approval-13.63 Rehabilitation of Wetwell	10	10	16-Jan-24	29-Jan-24	382
A1730	Submittal Review/Approval-2.30 Asphalt Paving	10	10	16-Jan-24	29-Jan-24	371
A1750	Submittal Review/Approval-4.22 CMU	10	10	16-Jan-24	29-Jan-24	156
A1760	Submittal Review/Approval-4.22 CMU Rebar	10	10	16-Jan-24	29-Jan-24	156
A1790	Submittal Review/Approval-6.70 FRP Package Supply	10	10	16-Jan-24	29-Jan-24	116
A1800	Submittal Review/Approval-7.60 Flashing and Sheet Metal	10	10	16-Jan-24	29-Jan-24	273
A1810	Submittal Review/Approval-7.40 Roofing and Siding Panels	10	10	16-Jan-24	29-Jan-24	156
A1820	Submittal Review/Approval-8.10 HM Doors and Frames	10	10	16-Jan-24	29-Jan-24	312
A1850	Submittal Review/Approval-Division 15 Stainless Steel Pipe/Fittings	10	10	16-Jan-24	29-Jan-24	312
A1510	Submittal Review/Approval-Temporary Sewer Bypass	10	10	30-Jan-24	12-Feb-24	74
A1690	Submittal Review/Approval-15.70 Plumbing	10	10	30-Jan-24	12-Feb-24	66
A1770	Submittal Review/Approval-5.00 Structural Steel and Fabricated Metals	10	10	30-Jan-24	12-Feb-24	127
A2420	Submittal Review/Approval-Arc/Flash Study	10	10	03-Jul-24	17-Jul-24	252
Manufacturing and Delivery		290	250	04-Oct-23 A	20-Dec-24	172
A2050	Delivery Lead- Division 15 Ductile Iron Pipe/Fittings	30	0	04-Oct-23 A	31-Oct-23 A	
A2130	Delivery Lead-2.20 Earthwork Materials	5	0	11-Oct-23 A	18-Oct-23 A	
A1930	Delivery Lead-Concrete Ready Mix	5	0	23-Oct-23 A	30-Oct-23 A	
A2060	Delivery Lead-Division 15 Gate Valves	10	0	27-Oct-23 A	09-Nov-23 A	
A3440	Delivery Lead-Division 15 PVC Pipe/Fittings	30	10	27-Oct-23 A	15-Jan-24	352
A2020	Delivery Lead-Divison 15 Knife Gate Valves	60	20	03-Nov-23 A	29-Jan-24	341
A1990	Delivery Lead-11.12.23 Emergency Storage Sewage Sump Pump and Motor	100	65	07-Nov-23 A	01-Apr-24	300
A2070	Delivery Lead-Division 15 Check Valves	110	80	13-Nov-23 A	22-Apr-24	281
A1970	Delivery Lead-11.12.20 Dry Pit Sewage Pump	160	145	05-Dec-23 A	24-Jul-24	71
A1950	Delivery Lead-Precast Structures	50	35	06-Dec-23 A	19-Feb-24	364
A2310	Delivery Lead-16.85 Lighting	60	50	12-Dec-23 A	11-Mar-24	280
A2080	Delivery Lead-Division 15 Plug Valves	110	100	15-Dec-23 A	20-May-24	261
A2290	Delivery Lead-16.60 Conductors	10	10	15-Dec-23 A	15-Jan-24	203
A2120	Delivery Lead-2.10 Dewatering	10	10	27-Dec-23 A	15-Jan-24	17
A2190	Delivery Lead-5.30 Metal Decking	40	40	27-Dec-23 A	26-Feb-24	160
A1940	Delivery Lead-Concrete Reinforcement	30	30	16-Jan-24	26-Feb-24	9
A1980	Delivery Lead-11.12.20 Emergency Diesel-Driven Sewage Pump	100	100	16-Jan-24	04-Jun-24	106
A2000	Delivery Lead-11.96 Odor Control System	80	80	16-Jan-24	06-May-24	126
A2010	Delivery Lead-11.95 HVAC	70	70	16-Jan-24	22-Apr-24	136
A2040	Delivery Lead-14.41.13 Bridge Crane	100	100	16-Jan-24	04-Jun-24	62
A2090	Delivery Lead-15.50 Flow Meters	80	80	16-Jan-24	06-May-24	271
A2240	Delivery Lead-8.90 Louvers and Vents	70	70	16-Jan-24	22-Apr-24	123
A2250	Delivery Lead-9.90 Painting and Coatings	20	20	16-Jan-24	12-Feb-24	152
A2270	Delivery Lead-16.40 Low Voltage Motor Control Equipment/Electrical Gear	240	240	16-Jan-24	20-Dec-24	50
A2280	Delivery Lead-16.50 Panelboards/VFD'S	240	240	16-Jan-24	20-Dec-24	60
A2300	Delivery Lead-16.70 Raceways, Boxes, and Fittings	10	10	16-Jan-24	29-Jan-24	200
A2320	Delivery Lead-16.90 Power Generation	140	140	16-Jan-24	31-Jul-24	181
A2390	Delivery Lead-Controls/Instrumentation	210	210	16-Jan-24	07-Nov-24	90
A2410	Delivery Lead-Fire Alarm	100	100	16-Jan-24	04-Jun-24	200
A1960	Delivery Lead-11.12.10 Sump Pump	70	70	30-Jan-24	06-May-24	275
A2030	Delivery Lead-13.63 Rehabilitation of Wetwell	20	20	30-Jan-24	26-Feb-24	382
A2140	Delivery Lead-2.30 Asphalt Paving	10	10	30-Jan-24	12-Feb-24	371
A2160	Delivery Lead-4.22 CMU	20	20	30-Jan-24	26-Feb-24	156
A2170	Delivery Lead-4.22 CMU Rebar	20	20	30-Jan-24	26-Feb-24	156
A2210	Delivery Lead-7.60 Flashing and Sheet Metal	80	80	30-Jan-24	20-May-24	273
A2220	Delivery Lead-7.40 Roofing and Siding Panels	30	30	30-Jan-24	11-Mar-24	156
A2230	Delivery Lead-8.10 HM Doors and Frames	30	30	30-Jan-24	11-Mar-24	312
A2260	Delivery Lead-Division 15 Stainless Steel Pipe/Fittings	30	30	30-Jan-24	11-Mar-24	312
A1920	Delivery Lead-Temporary Sewer Bypass	10	10	13-Feb-24	26-Feb-24	74
A2100	Delivery Lead-15.70 Plumbing	40	40	13-Feb-24	08-Apr-24	66
A2180	Delivery Lead-5.00 Structural Steel and Fabricated Metals	40	40	13-Feb-24	08-Apr-24	127
A2200	Delivery Lead-6.70 FRP Package Supply	50	50	09-Apr-24	18-Jun-24	66
A2430	Delivery Lead-Arc/Flash Study	30	30	18-Jul-24	28-Aug-24	252
Construction		426	401	16-Oct-23 A	25-Jul-25	21
Sitework		425	400	16-Oct-23 A	24-Jul-25	21
A2330	Mobilization and Site Setup	10	0	16-Oct-23 A	18-Dec-23 A	
A2350	Temporary Erosion and Sediment Control	3	0	16-Oct-23 A	19-Oct-23 A	
A2360	Temporary Fencing	2	0	18-Oct-23 A	19-Oct-23 A	
A2340	Survey	3	0	23-Oct-23 A	25-Oct-23 A	
A2950	Demo Concrete, Curb, Landscaping, Existing Structures	4	0	25-Oct-23 A	27-Oct-23 A	
A2940	Demo Asphalt	4	0	26-Oct-23 A	31-Oct-23 A	
A3170	Pothole for Manhole #6 and Existing FM	2	0	22-Dec-23 A	22-Dec-23 A	
A2370	Temporary Relocate Communication Conduits	2	2	02-Jan-24	03-Jan-24	5

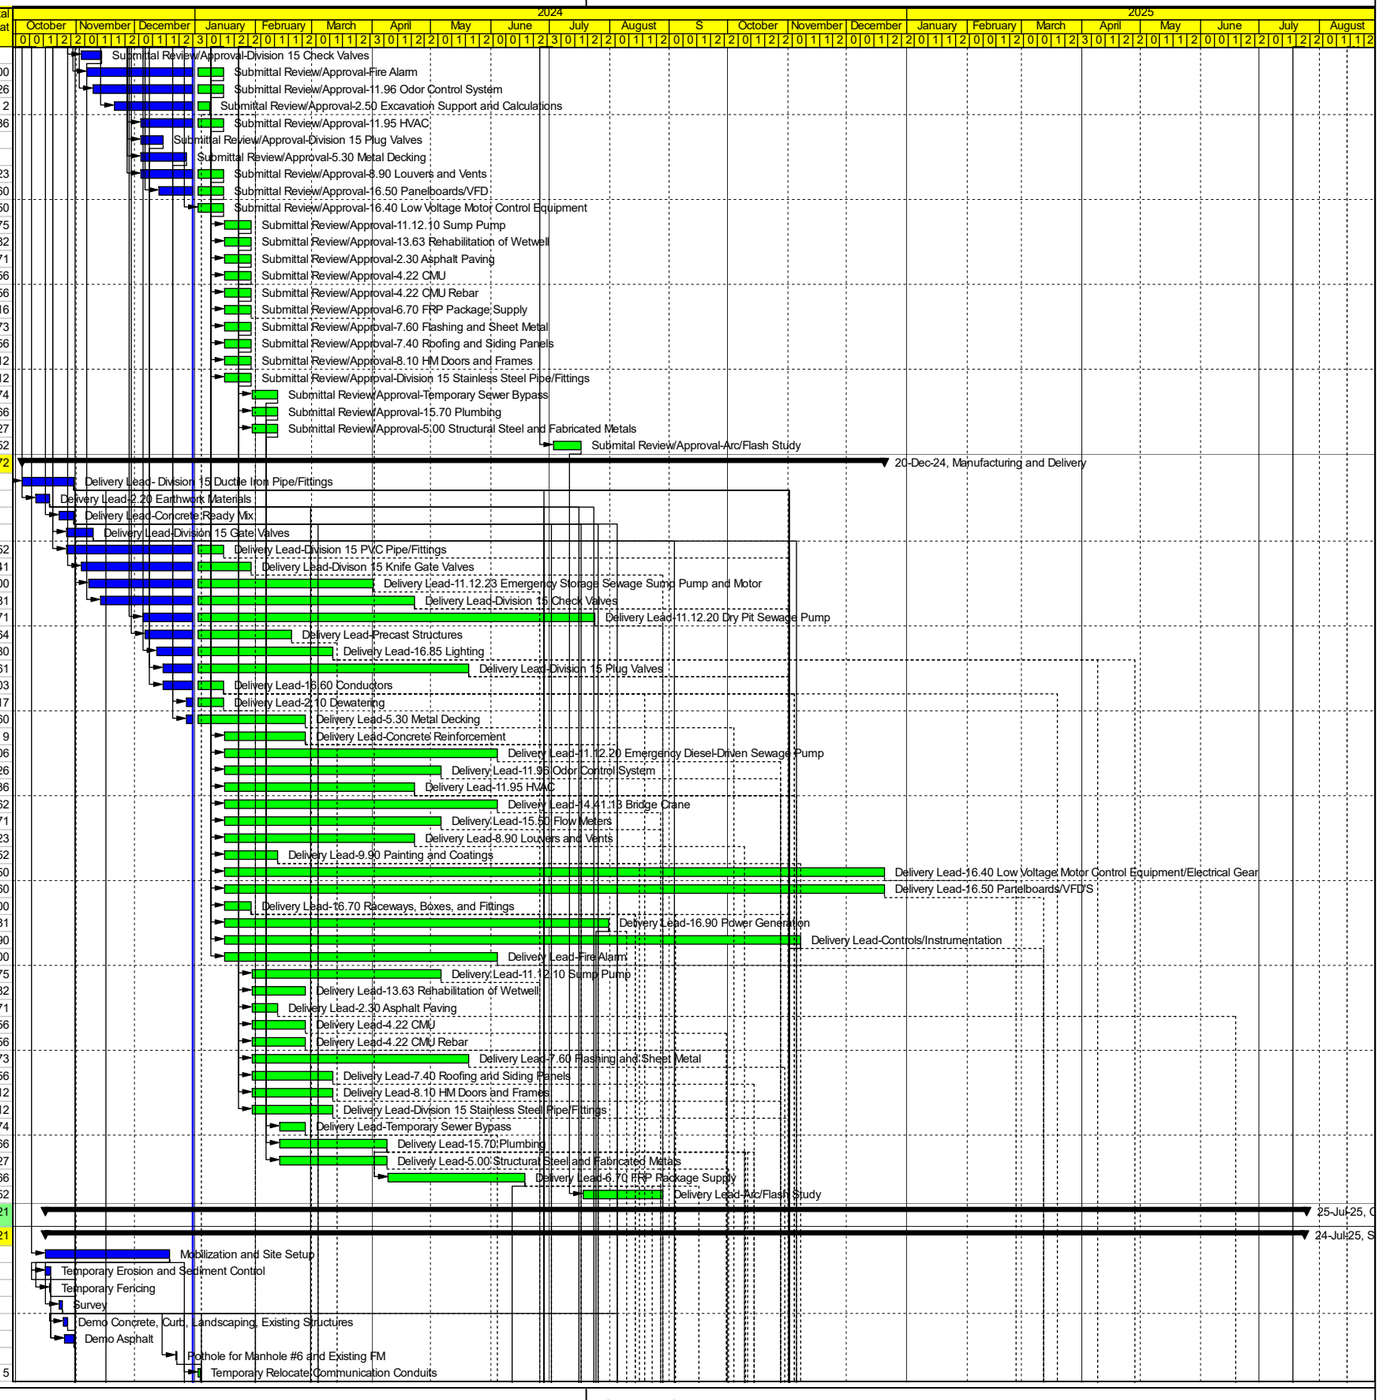

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

Stellar J Corporation
23009 Port Orchard Marina Pump Station_Update 2 _December 2023

Data Date: 31-December-23

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float
A2900	Underground Conduits/Pull Wire	7	7	12-Aug-24	20-Aug-24	56
A2880	Remove Emergency Bypass Pumping System	4	4	20-Jun-25	25-Jun-25	21
A2890	Complete Site Restoration and Parking Improvements	20	20	26-Jun-25	24-Jul-25	21
Yard Piping		113	2	07-Nov-23 A	27-Jun-24	16
A2560	Phase 1 and 2 New Water Main Construction 8", 12" DI and Valves	10	0	07-Nov-23 A	22-Nov-23 A	
A2730	Phase 3 Wate Main Construction 12" DI	5	0	23-Nov-23 A	12-Dec-23 A	
A2710	Demo Existing Force Main	2	2	26-Jun-24	27-Jun-24	16
Emergency Storage Structure		223	223	02-Jan-24	12-Nov-24	199
Civil		114	114	02-Jan-24	10-Jun-24	308
A2960	Relocate Telephone Line	2	2	02-Jan-24	03-Jan-24	0
A2970	Relocate Power Manhole	5	5	04-Jan-24	10-Jan-24	0
A2980	Shoring at Emergency Storage Structure	20	20	11-Jan-24	07-Feb-24	0
A2990	Install Dewatering Wells for Manholes, ESS, VV	10	10	08-Feb-24	21-Feb-24	0
A3560	Mass Excavation for Emergency Storage Structure	10	10	22-Feb-24	06-Mar-24	0
A3000	Foundation Prep at Emergency Storage Structure	2	2	07-Mar-24	08-Mar-24	0
A3910	Mass Excavation for Manholes	10	10	07-Mar-24	20-Mar-24	342
A3120	Install Manholes	20	20	21-Mar-24	17-Apr-24	342
A3100	Bacfill for Manholes	3	3	18-Apr-24	22-Apr-24	342
A3010	Backfill at Emergency Storage Structure	8	8	30-May-24	10-Jun-24	0
Structural and Architectural		81	81	11-Mar-24	02-Jul-24	235
A2910	F/R/P/S-Foundation Slab and Sump	10	10	11-Mar-24	22-Mar-24	0
A3020	F/R//P/S-Walls	30	30	25-Mar-24	03-May-24	0
A3030	F/R/P/S-Top Slab	15	15	06-May-24	24-May-24	0
A3050	Clean and Leak Test	2	2	28-May-24	29-May-24	0
A3370	FRP Ladders, Walkways, and Stairs for Emergency Storage	10	10	19-Jun-24	02-Jul-24	235
Process and Mechanical		3	3	03-Jul-24	08-Jul-24	240
A2920	Install 11.12.23 Emergency Storage Sewage Pump	1	1	03-Jul-24	03-Jul-24	235
A3410	Install 11.12.10 Sump Pump for ESS	1	1	03-Jul-24	03-Jul-24	235
A3400	3" DI for ESS, DW, WW	2	2	05-Jul-24	08-Jul-24	239
A3420	1 1/2" PVC Pipe, Check Valve, Gate Valve for ESS	2	2	05-Jul-24	08-Jul-24	240
Electrical and Controls		59	59	21-Aug-24	12-Nov-24	149
A2930	Raceways and Rough In	3	3	21-Aug-24	23-Aug-24	202
A3330	Install Instrumentation	1	1	08-Nov-24	08-Nov-24	149
A3340	Pull Wire	1	1	11-Nov-24	11-Nov-24	149
A3570	Terminations	1	1	12-Nov-24	12-Nov-24	149
Temporary Bypass		11	11	11-Jun-24	25-Jun-24	0
A2480	Install Temporary Bypass Pumping System	8	8	11-Jun-24	20-Jun-24	0
A2490	Test Temporary Bypass Pumping System	2	2	21-Jun-24	24-Jun-24	0
A2500	Close/Plug lines to use Temp Bypass Pumping System	1	1	25-Jun-24	25-Jun-24	0
Valve Vault		196	196	08-Feb-24	12-Nov-24	151
Civil		144	144	08-Feb-24	29-Aug-24	16
A3140	Shoring for Valve Vault	10	10	08-Feb-24	21-Feb-24	106
A3070	Demo Existing FM	2	2	26-Jun-24	27-Jun-24	16
A3090	Excavation for Valve Vault	4	4	28-Jun-24	03-Jul-24	16
A3150	Foundation Prep for Valve Vault	2	2	05-Jul-24	08-Jul-24	16
A3970	Backfill for Valve Vault	2	2	28-Aug-24	29-Aug-24	16
Structural and Architectural		40	40	09-Jul-24	03-Sep-24	188
A3240	F/R/P/S-Foundation Slab Valve Vault	8	8	09-Jul-24	18-Jul-24	16
A3250	F/R/P/S-Walls Valve Vault	15	15	19-Jul-24	08-Aug-24	16
A3270	F/R/P/S-Top Slab and Thrust Blocks	10	10	09-Aug-24	22-Aug-24	16
A3990	Coatings for Valve Vault	3	3	23-Aug-24	27-Aug-24	16
A3280	Install Access Hatches	1	1	30-Aug-24	30-Aug-24	188
A3290	Install Ladders	1	1	03-Sep-24	03-Sep-24	188
Process and Mechanical		7	7	04-Sep-24	12-Sep-24	194
A3300	Install 18" and 24" DI Interior/Exterior Piping and Valves in Valve Vault	4	4	04-Sep-24	09-Sep-24	188
A3350	Install 4" DI Gate Valve with 4" Air Release Valve	1	1	10-Sep-24	10-Sep-24	188
A3360	Install Pipe Supports	3	3	10-Sep-24	12-Sep-24	194
Electrical		45	45	11-Sep-24	12-Nov-24	151
A4170	Raceways and Rough In	5	5	11-Sep-24	17-Sep-24	188
A4180	Instrumentation	1	1	08-Nov-24	08-Nov-24	151
A4190	Pull Wire	1	1	11-Nov-24	11-Nov-24	151
A4200	Terminations	1	1	12-Nov-24	12-Nov-24	151
Multi Use Facility		244	244	26-Jun-24	10-Jun-25	5
Civil		32	32	26-Jun-24	09-Aug-24	0
A3450	Demolish Existing Restroom and Access to Drywell	2	2	26-Jun-24	27-Jun-24	0
A3460	Demo Lid to Drywell and Wetwell	14	14	23-Jul-24	09-Aug-24	0
Structural and Architectural		95	95	17-Jul-24	27-Nov-24	140
A3490	Install Bracing in Drywell and Wetwell	4	4	17-Jul-24	22-Jul-24	0
A3500	F/R/P/S Walls in DW and WW	15	15	12-Aug-24	30-Aug-24	0
A4300	CMU Exterior Building Layout	1	1	30-Aug-24	30-Aug-24	16
A3610	F/R/P/S Pump Pads in DW	1	1	03-Sep-24	03-Sep-24	43
A3510	F/R/P/S Base Slab for Multi Use Facility	10	10	09-Sep-24	20-Sep-24	0
A3520	Remove Bracing in Drywell and Wetwell	2	2	23-Sep-24	24-Sep-24	0
A3720	Install Hatches at Multi Use Facility	2	2	23-Sep-24	24-Sep-24	0
A3670	F/R/P/S Walls Multi Use Facility	8	8	25-Sep-24	04-Oct-24	0
A3710	Masonry Block at Multi Use Facility	1	1	07-Oct-24	07-Oct-24	0
A3730	F/R/P/S Equipment Pads at Multi Use Facility	2	2	07-Oct-24	08-Oct-24	18
A3840	Install Roof Structural Steel	3	3	08-Oct-24	10-Oct-24	0

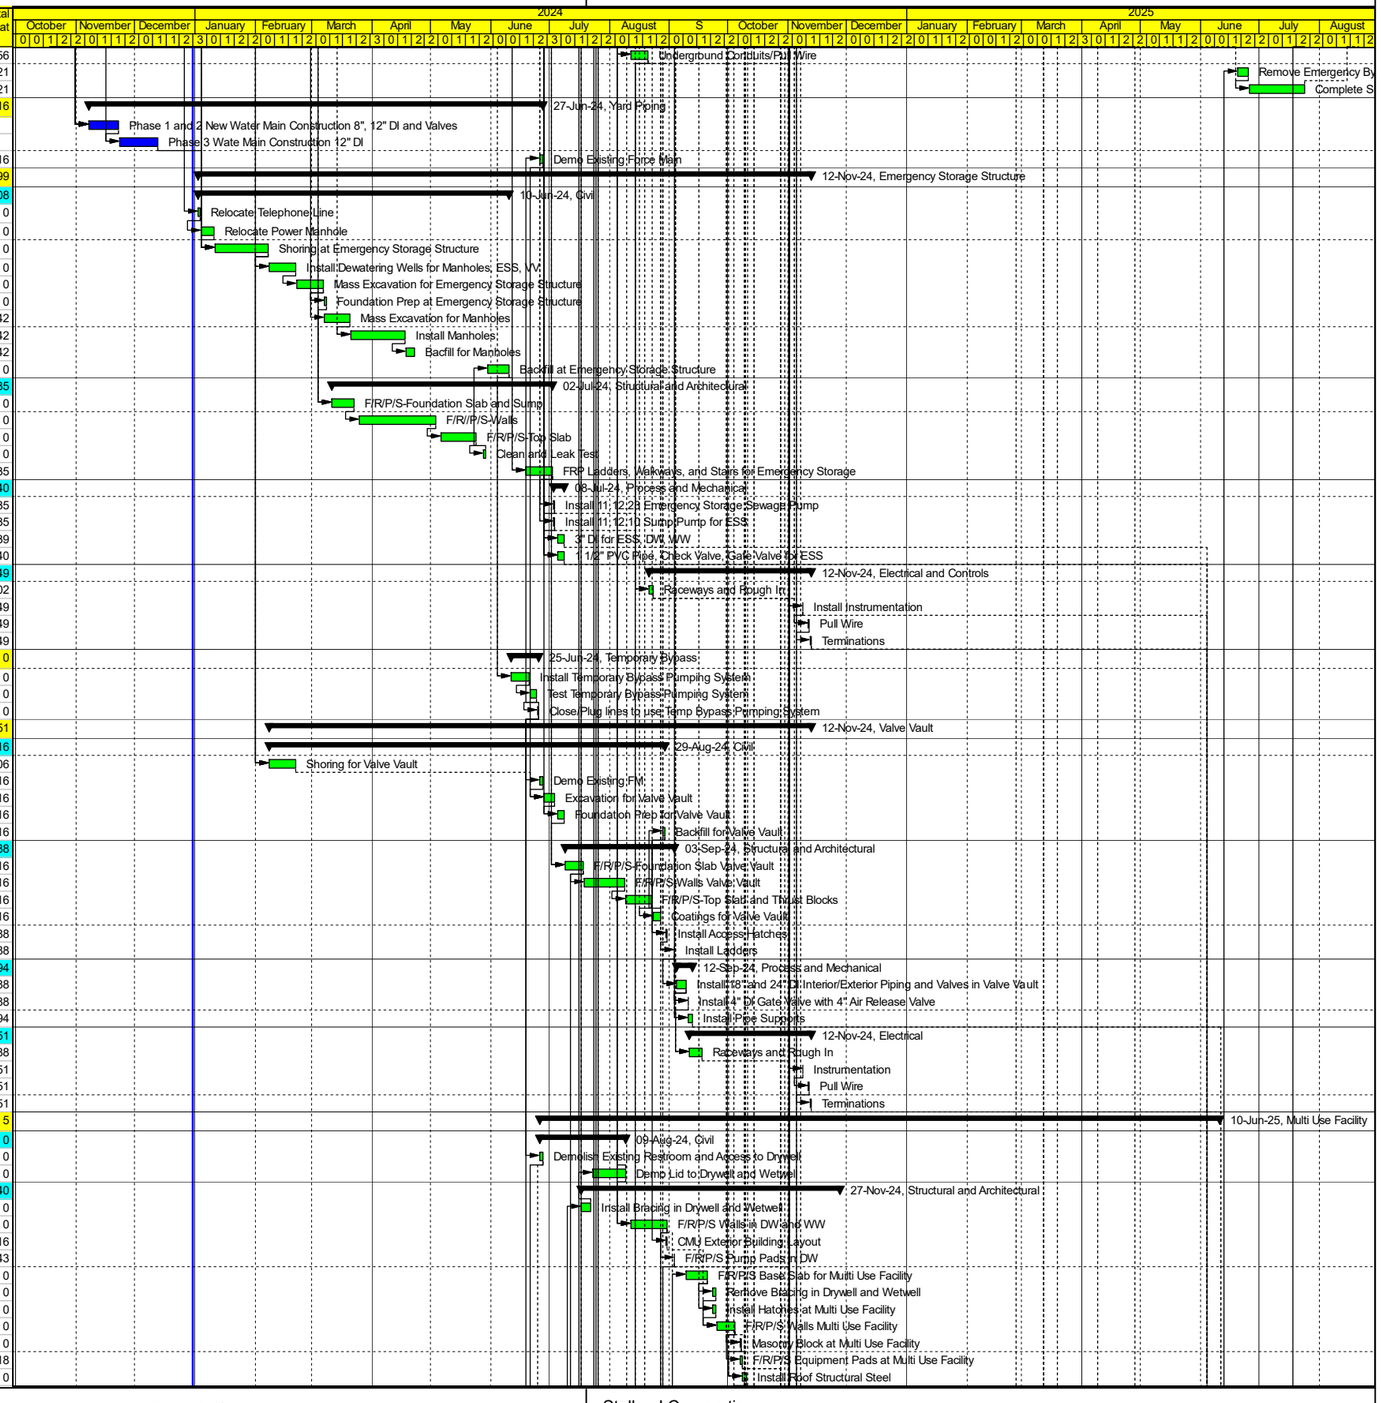

Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Milestone

Stellar J Corporation

23009 Port Orchard Marina Pump Station_Update 2 _December 2023

Data Date: 31-December-23

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float
A4230	Install Metal Decking	3	3	11-Oct-24	15-Oct-24	0
A3690	Louvers at Mullti Use Facility	3	3	16-Oct-24	18-Oct-24	0
A3680	Install Roofing and Siding Panels at the Mulit Use Facility	10	10	21-Oct-24	01-Nov-24	0
A3700	Install Doors at Multi Use Facility	2	2	04-Nov-24	05-Nov-24	146
A4240	Flashing and Sheet Metal at the Multi Use Facility	1	1	06-Nov-24	06-Nov-24	155
A4250	Interior Coatings at the Multi Use Facility	10	10	14-Nov-24	27-Nov-24	140
Process and Mechanical		95	95	02-Jul-24	13-Nov-24	140
A3480	Demo Piping and Mechanical in DW and WW	10	10	02-Jul-24	16-Jul-24	0
A3660	Install Bridge Crane	4	4	03-Sep-24	06-Sep-24	0
A3640	Install Pumps at DW	4	4	04-Sep-24	09-Sep-24	43
A4020	Plumbing-Rough In	1	1	16-Oct-24	16-Oct-24	157
A4010	Plumbing-Floor Drain Piping and Floor Drains	1	1	17-Oct-24	17-Oct-24	157
A4030	Plumbing-Fixtures and Equipment	1	1	18-Oct-24	18-Oct-24	157
A4040	Plumbing-Finish	1	1	21-Oct-24	21-Oct-24	157
A3650	Install HVAC-Heaters, Fans, Heat Pump	4	4	04-Nov-24	07-Nov-24	0
A3740	Install Odor Control Unit at Multi Use Facility	4	4	04-Nov-24	07-Nov-24	0
A3750	Install Emergency Diesel Driven Pump at Multi Use Facility	4	4	04-Nov-24	07-Nov-24	0
A3530	Install 8" DI and Valves at DW and WW	2	2	08-Nov-24	11-Nov-24	142
A3540	Install 16" DI at DW and WW	2	2	08-Nov-24	11-Nov-24	142
A3550	Install 24" DI at DW and WW	2	2	08-Nov-24	11-Nov-24	142
A3760	Install 18" DI and Valves at Multi Use Facility	2	2	08-Nov-24	11-Nov-24	142
A3780	Install 12" DI at Multi Use Facility	2	2	08-Nov-24	11-Nov-24	141
A3790	Install 16" DI and Valves at Multi Use Facility	2	2	08-Nov-24	11-Nov-24	141
A3770	Install HVAC-Ductwork and Piping	2	2	08-Nov-24	11-Nov-24	140
A4260	Stainless Steel Piping	2	2	08-Nov-24	11-Nov-24	142
A4270	PVC Piping	2	2	08-Nov-24	11-Nov-24	142
A3800	Install 4" Gate Valve at Multi Use Facility	1	1	12-Nov-24	12-Nov-24	141
A4000	Install HVAC-Piping for Odor Control	2	2	12-Nov-24	13-Nov-24	140
Electrical and Controls		242	242	28-Jun-24	10-Jun-25	0
A3810	Demo (Make Safe)	2	2	28-Jun-24	01-Jul-24	0
A4090	Raceways and Rough In	80	80	08-Nov-24	04-Mar-25	0
A4100	Electrical Gear	10	10	05-Mar-25	18-Mar-25	0
A4110	Panels	5	5	19-Mar-25	25-Mar-25	0
A4130	Pull Wire	15	15	26-Mar-25	15-Apr-25	0
A4120	Lighting	10	10	16-Apr-25	29-Apr-25	0
A4150	Terminations	15	15	06-May-25	27-May-25	0
A4140	Permanent Service	10	10	28-May-25	10-Jun-25	0
Generator		203	203	19-Jul-24	05-May-25	30
Civil		3	3	19-Jul-24	23-Jul-24	181
A3890	Excavation for Generator	2	2	19-Jul-24	22-Jul-24	181
A3900	Foundation Prep for Generator	1	1	23-Jul-24	23-Jul-24	181
Structural and Architectual		12	12	24-Jul-24	08-Aug-24	218
A3920	F/R/P/S Stem Walls Generator	3	3	24-Jul-24	26-Jul-24	181
A3930	F/R/P/S Generator Pad	2	2	29-Jul-24	30-Jul-24	181
A3940	F/R/P/S Stairs at Generator	1	1	31-Jul-24	31-Jul-24	181
A3950	Install Green Wall and Gates at Generator	4	4	05-Aug-24	08-Aug-24	218
Process and Mechanical		2	2	01-Aug-24	02-Aug-24	181
A3960	Install Generator	2	2	01-Aug-24	02-Aug-24	181
Electrical and Controls		180	180	21-Aug-24	05-May-25	0
A4050	Raceways and Rough In	3	3	21-Aug-24	23-Aug-24	169
A4080	Pull Wire	2	2	26-Aug-24	27-Aug-24	169
A4060	Grounding	2	2	28-Aug-24	29-Aug-24	169
A4280	Terminations	3	3	30-Apr-25	02-May-25	0
A4070	Lighting	1	1	05-May-25	05-May-25	0
Existing Pump Control Structure		30	30	26-Jun-24	07-Aug-24	267
A4210	Electrical-Demo (Make Safe)	10	10	26-Jun-24	10-Jul-24	267
A3820	Demo Mechanical Existing Pump Control Structure	5	5	11-Jul-24	17-Jul-24	267
A3830	Demo Structure Existing Pump Control Structure	5	5	18-Jul-24	24-Jul-24	267
A3850	Excavation at Existing Pump Control Sutructure	4	4	25-Jul-24	30-Jul-24	267
A3860	Foundation Prep at Existing Pump Control Structure	2	2	31-Jul-24	01-Aug-24	267
A3880	F/R/P/S Topping Slab at Existing Pump Control Structure	2	2	02-Aug-24	05-Aug-24	267
A3870	Install Guardail at Existing Pump Control Structure	2	2	06-Aug-24	07-Aug-24	267
Startup Testing and Training		57	57	06-May-25	25-Jul-25	0
A2640	Startup and Testing Generator	3	3	06-May-25	08-May-25	27
A2590	Manufacturer Startup and Testing Sump Pump	1	1	11-Jun-25	11-Jun-25	4
A2600	Manufacturer Startup and Testing Dry Pit Sewage Pumps	2	2	11-Jun-25	12-Jun-25	0
A2620	Manufacturer Startup and Testing Emergency Storage Sewage Sump Pump and Motor	2	2	11-Jun-25	12-Jun-25	3
A2650	Startup and Testing Electrical, Instrumentation, and Control	6	6	11-Jun-25	18-Jun-25	4
A2660	Startup and Testing Odor Control Systems	2	2	11-Jun-25	12-Jun-25	8
A2610	Manufacturer Startup and Testing Emergency Diesel-Driven Sewage Pump	3	3	13-Jun-25	17-Jun-25	0
A2690	Facility Inital Startup and Testing	5	5	18-Jun-25	24-Jun-25	0
A2720	Remove Plugs in MH 2 and MH E and direct flow to Wet Well	1	1	18-Jun-25	18-Jun-25	21
A2740	Plug and abandon pipe from MH 2 to MH 7 and MH7 to Em Storage Structure	1	1	19-Jun-25	19-Jun-25	21
A2670	Owner Training	5	5	25-Jun-25	01-Jul-25	0
A2700	Facility Operational Testing	17	17	02-Jul-25	25-Jul-25	0

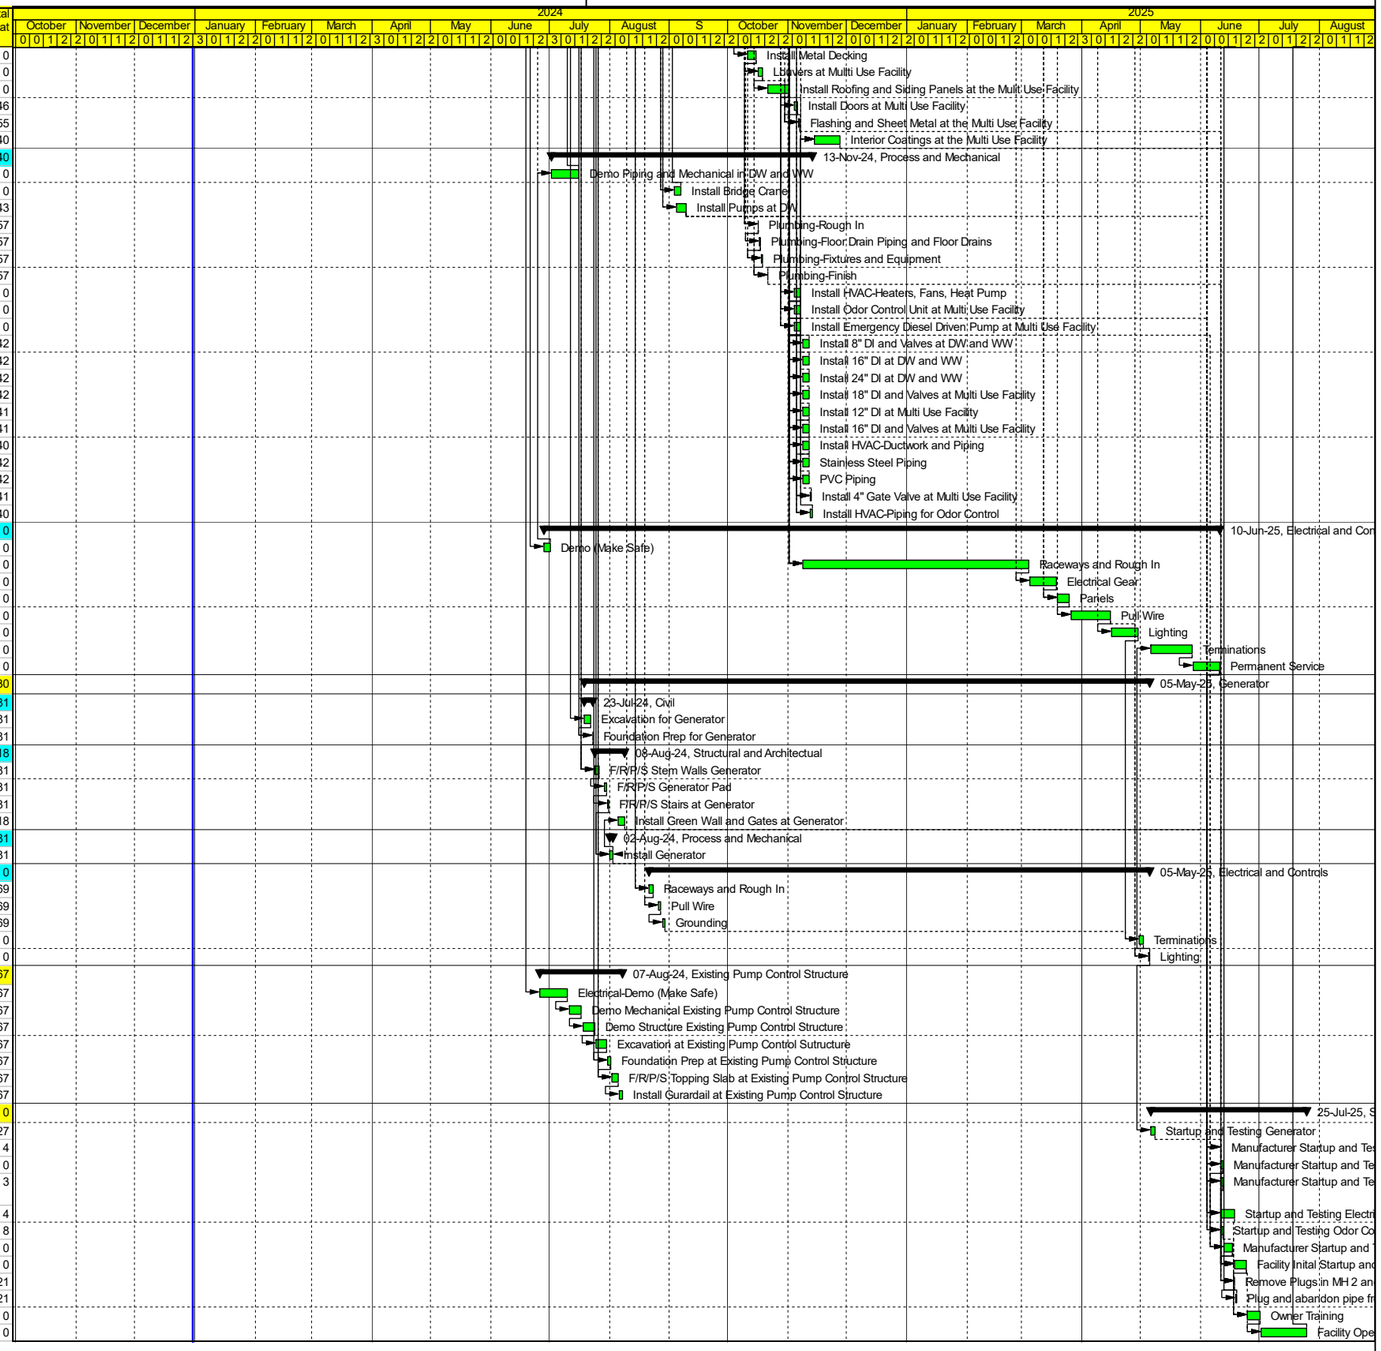

Remaining Level of Effort | Actual Work | Critical Remaining Work

Actual Level of Effort | Remaining Work | Milestone

Stellar J Corporation

23009 Port Orchard Marina Pump Station_Update 2 _December 2023
